

***Finals Paper Output for
CitiSense: A Smart Web App for Automated Multilingual Feedback
Processing and Data Visualization***

Project Documentation Submitted to the Faculty of the
School of Computing and Information Technologies
Asia Pacific College

In Partial Fulfillment of the Requirements for
Systems Analysis and Detailed Design MSYADD1

Submitted by:

Mark Lyster Marabi (Team Leader)

Lorenzo Emil Bernal (Member)

Gabrielle Cabangcala (Member)

Luis Lorenzo Lazaro (Member)

G07 QuadThink – SF 231

Submitted to:

Mr. Jose Euginio L. Quesada

Course Instructor

October 2025

1st Term

A.Y. 2025 – 2026

Comments Matrix

OpenProject Unit and Labor Costs:

Panelist Comment

A contingency budget must be included in the OpenProject budget. Update the labor costs to suit the market standards today.

Action

Add a contingency reserve budget for the phases in the OpenProject and update the budget breakdown to reflect hourly computations for accuracy and transparency.

Updated OpenProject Unit and Labor Costs:

Planned unit costs			
UNITS	COST TYPE	COMMENT	BUDGET
0.10	Contingency Reserve		PHP 1,000.00
20.00	Transportation expenses Php 100	For gas and commute money	PHP 2,000.00
5.00	Office Supplies Php100	For printing documents, whiteboards, and writin...	PHP 500.00
1.00	Cloud Services Monthly Subscription	Cloud storage subscription	PHP 283.00
			PHP 3,783.00

LABOR			
Planned labor costs			
HOURS	USER	COMMENT	BUDGET
100.00 hours	 Gabrielle Cabangcala		PHP 30,000.00
100.00 hours	 Lorenzo Bernal		PHP 35,000.00
100.00 hours	 Luis Lazaro		PHP 30,000.00
100.00 hours	 Mark Marabi		PHP 40,000.00
			PHP 135,000.00

DFD Level 2 – 1.0 Manage Account


Panelist Comment

There should be a way for the system admin to edit their profile within the system

Action

We connected the system admin to the 1.2 - Manage Profile process.

Updated DFD Level 2 – 1.0 Manage Account:

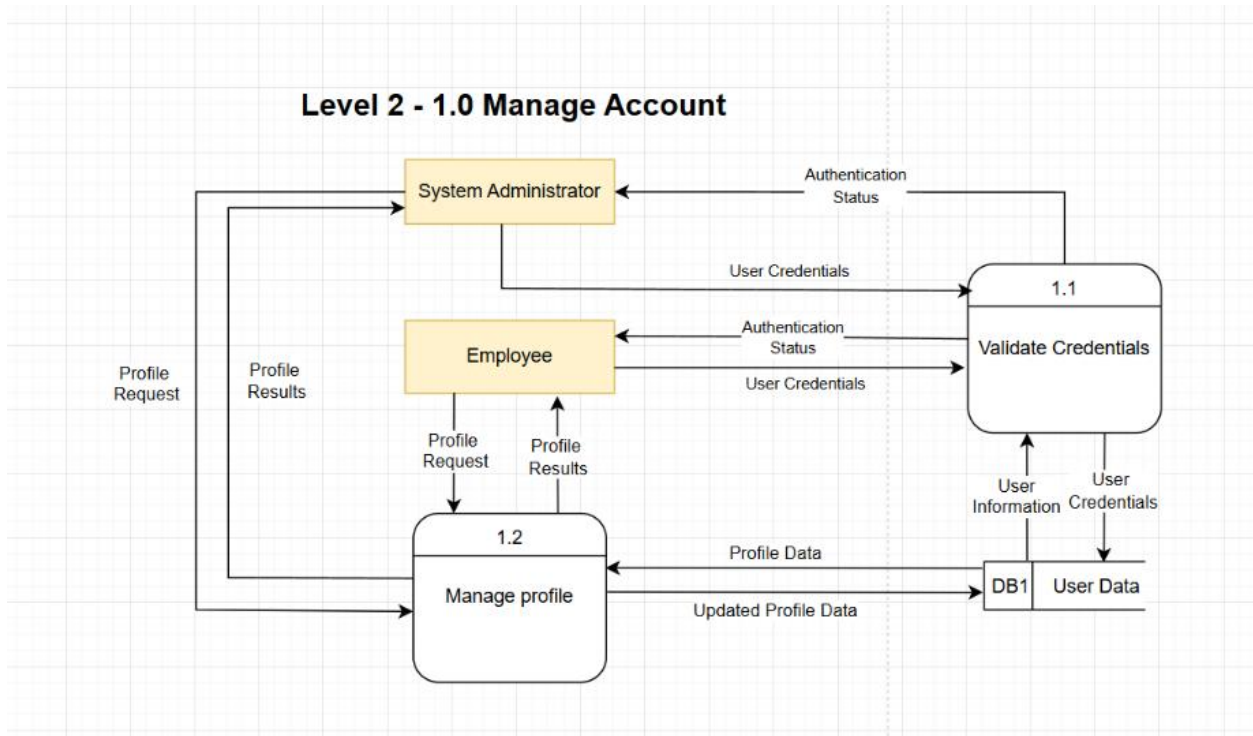

DFD Level 2 – 4.0 Manage Reports


Panelist Comment

Reports should be saved locally by the actor and not to a database.

Action

The generated reports are now given to the user and employee.

Updated DFD Level 2 – 4.0 Manage Reports:

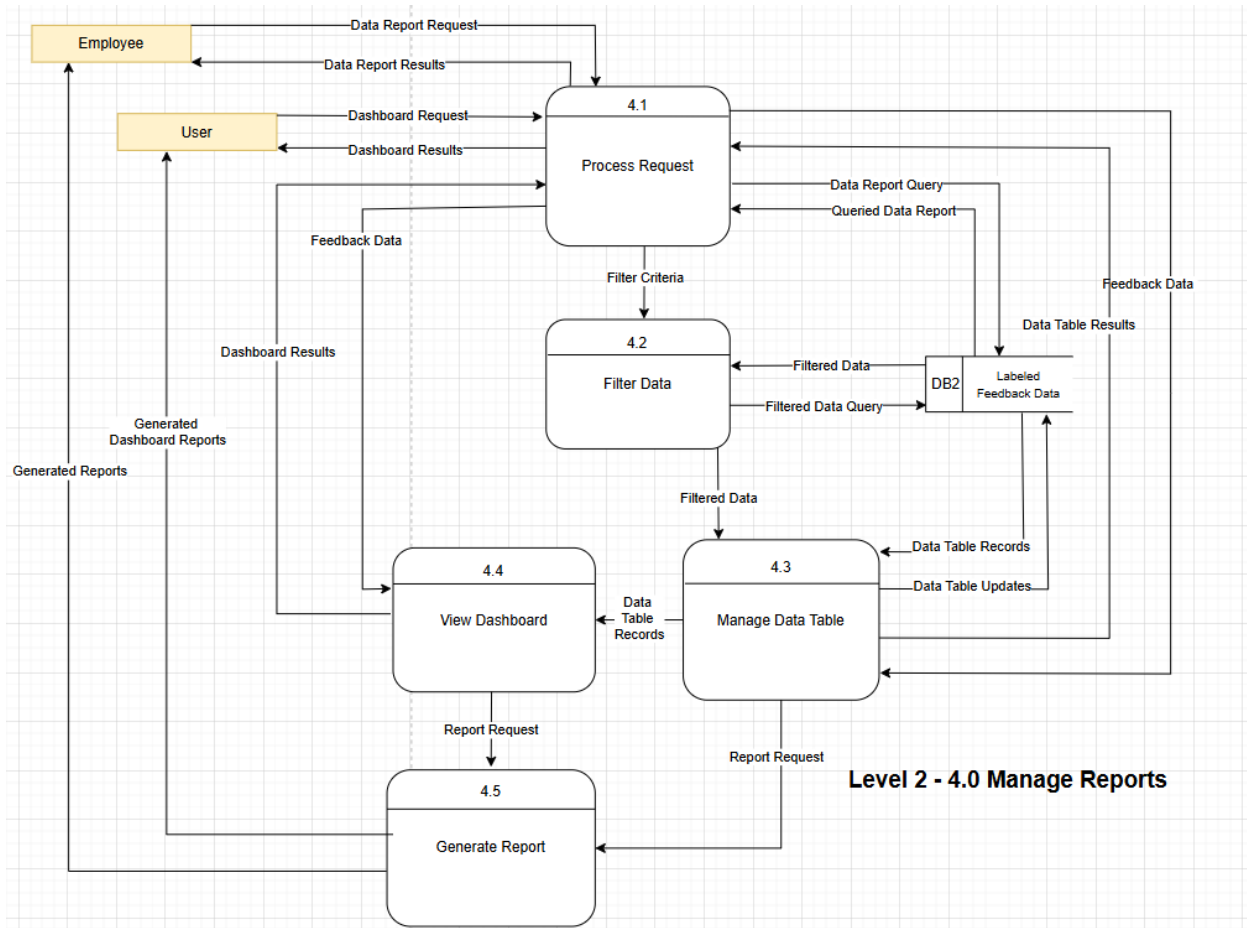

Product Roadmap

Panelist Comment

There should be no gaps in the product roadmap, specifically the 3rd and 4th phase.

Action

Revise the roadmap to ensure that there is no gap between the 3rd and 4th phase.

Updated Product Roadmap:



Use Case Diagram


Panelist Comment

Replace “Data Analyst” with “Employee” in the Use Case Diagram.

Action

Update the diagram to use the appropriate term.

Updated Use Case Diagram:

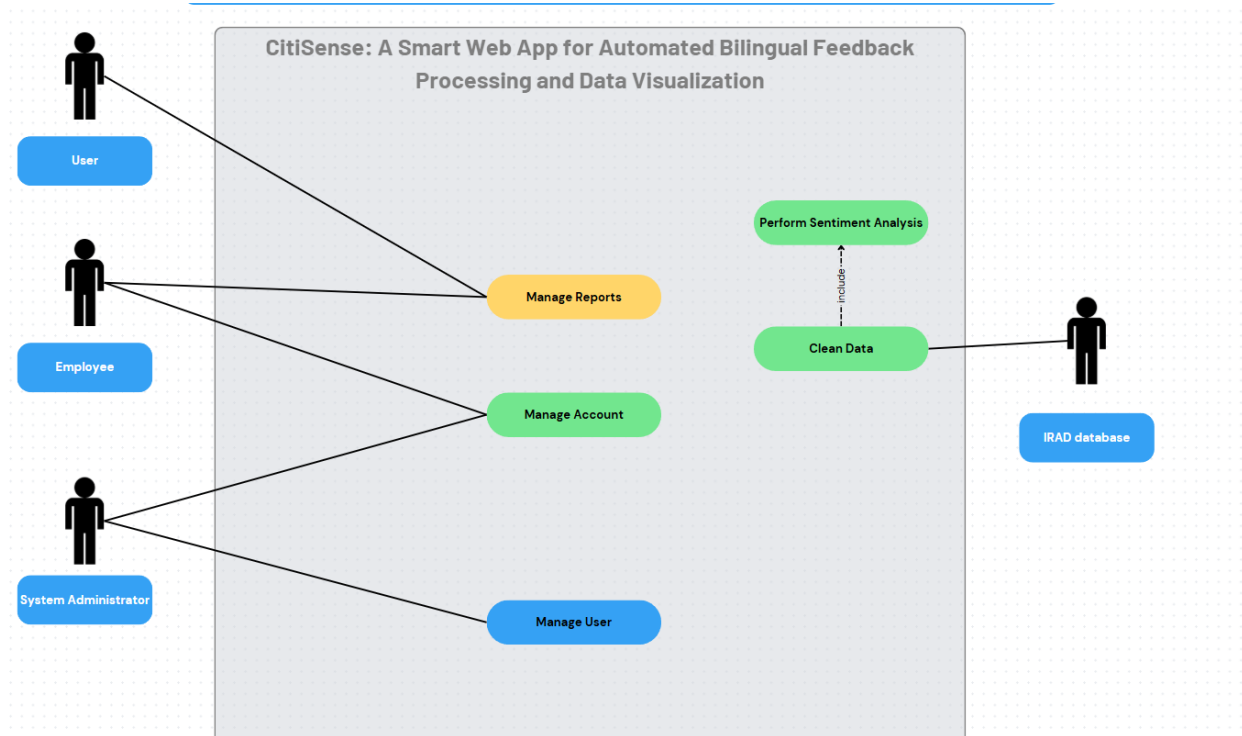

PM Docs Chapter 2

Project Charter

Project Name: *CitiSense: A SMART Web Application for Automated Bilingual Feedback Processing and Data Visualization*

Purpose

The purpose of the CitiSense project is to address the time-consuming, manual processing of feedback data currently handled by the IRAD department of the Department of Science and Technology – Science and Technology Information Institute (DOST–STII). The project responds to the growing need for automated sentiment analysis tools that support both English and Tagalog inputs, enabling faster, data-driven decisions. This initiative aligns with DOST-STII's strategic goal to enhance public science communication and increase responsiveness to stakeholder feedback.

High-level project description

CitiSense is a web-based system that leverages Natural Language Processing (NLP) to automatically analyze and classify textual feedback in English, Tagalog, or a mix of both. The system processes sentiment as positive, neutral, or negative and presents the results in a real-time interactive dashboard. Key features include:

- NLP model for bilingual sentiment analysis (minimum 85% accuracy).
- Real-time data visualization through charts and keyword trends.
- Seamless integration with DOST–STII's existing feedback collection systems.

High-level milestone schedule

The project has begun officially in **July 2025**, starting with the selection and initial fine-tuning of the Natural Language Processing (NLP) model tailored for bilingual sentiment analysis. In **August**, the development of the backend using Django will commence alongside the initial implementation of the frontend using React. By **September**, the team aims to complete a working prototype of the sentiment analysis system capable of processing and classifying feedback.

In **October**, efforts will shift toward integrating a data visualization dashboard that will display sentiment trends and keyword insights in real time. **November** will be dedicated to system testing using actual feedback data from the IRAD department, ensuring that the application meets performance and usability expectations. During **December**, final enhancements, usability improvements, and interface refinements will be applied based on testing feedback.

The project will conclude in **January of 2026**, with the full deployment of the CitiSense system and formal turnover to the IRAD department of DOST–STII for integration into their operations.

Rough cost estimate and budget

Estimated Budget: PHP 0 (Open-source development)

Cost Breakdown:

- NLP Model: Free (HuggingFace open-source models)
- Backend: Django (open-source)
- Frontend: React (open-source)

- Database: MySQL (open-source)
- Hosting: Free tier services (Vercel for frontend, Render/AWS for backend)

Funding Sources:

- DOST-STII support (non-monetary, testing data and validation)
- Team resources (QuadThink student-led development)

Stakeholders

Primary Stakeholder:

- IRAD Department, DOST-STII – End users and beneficiaries

Other Stakeholders:

- Researchers and Data Analysts at DOST
- Other Government Agencies with similar feedback systems
- Future Project Developers
- Educational Institutions (for research and learning applications)

Project manager

Name: Mark Marabi

Position: Project Lead, QuadThink Team

Project manager's responsibilities

- Oversee the full development lifecycle
- Ensure adherence to the timeline and deliverables
- Manage collaboration with IRAD stakeholders
- Facilitate testing, documentation, and deployment
- Report regularly on progress and challenges

Project manager's authority

- Coordinate team assignments and workload
- Make technical decisions regarding design and implementation
- Resolve conflicts within the development team
- Communicate directly with stakeholders for feedback and validation
- Approve sprint outputs and initiate changes as needed

Formal declaration of sponsor's support

Name: Arjay Escondo

Position: Division Head, IRAD – DOST-STII

Authority: Project sponsor and approving authority on behalf of DOST-STII

Sponsor Statement of Support:

“As the sponsor of the CitiSense project, I fully endorse its development and implementation to enhance the feedback analysis capabilities of the IRAD department. I recognize the value of automating sentiment classification and visualization for better decision-making and institutional responsiveness. I am committed to supporting the QuadThink team in developing a solution aligned with DOST-STII’s mission.”

Project Objectives

Objective	Category	Measure
Develop a web application that uses Natural Language Processing (NLP)	System Development	CitiSense web application deployed with NLP sentiment analysis with visualization features
Accurately classify survey responses (positive, neutral, negative) in English and Tagalog	Quality	Achieve $\geq 85\%$ accuracy within a 6-month development timeline
Automate feedback processing to reduce manual workload	Efficiency	Reduce workload by $\geq 80\%$ and accelerate report turnaround time
Ensure timely, data-driven decision-making within DOST-STII’s IRAD department	Information Responsiveness	Feedback reports generated in real-time
Support English, Tagalog, and code-switched input in sentiment classification	Technical	Bilingual model with $\geq 85\%$ classification accuracy

Project Scope

Project goal and objectives

CitiSense is a web-based application that will supplement the current system of CitiSense with a means to automatically analyse and display sentiments in English, Tagalog, or multilingual survey answers using Natural Language Processing (NLP). Its key objective is to categorize the feedback as positive, neutral, and negative as accurately as possible, with an accuracy not lower than 85 percent per six months. The automated process shall save 80 percent of the manual workload, which will improve the turnaround time for feedback reports in order to make quick, responsive decisions. CitiSense is also designed to integrate easily with current workflows and future scalability (e.g., the addition of new languages and new data sources).

Project Boundaries

Within scope: In this project, the objective is the development of CitiSense, a web application that will make an automatic analysis of feelings and see figures presented in questionnaire answers in English or Tagalog, or a combination of both languages. A properly tuned Natural Language Processing (NLP) model will be used in the system. Subjecting feedback to three categories: that is, positive, neutral, and negative. Also, it will include a dynamically updated dashboard complete with sentiment trends and keywords, aiding the IRAD division of DOST to be more enlightened about what people feel. It will be an app. To be integrated with the already existing feedback collection form used by DOST-STII, and will be able to receive text-based feedback. The main audiences of this system are data analysts, data researchers, and government officials following up on the reactions of the people.

Out of scope: Audio and visual responses will not be supported, and the system will only support text responses. Although the model of NLP is made to deal with both Tagalog and English inputs, when dealing with regional languages, it is better to use regional languages. Very informal language or dialects may affect the precision of sentiment classification. The performance of this model is influenced by the training data used, as it has to depend on its quality and diversity. Furthermore, the visualization segment will be reduced only to the sentiment patterns and keywords; more sophisticated Predictive analytics or topic modeling will also not be added in this first release. Moreover, they will not incorporate real-time data from any external sources into the current feedback system. form

Project Deliverables

- Text Only NLP Feedback System: A Web application that feeds back and parses feedback containing either English or Tagalog input or both in any permutation with the 3 possible sentiment conditions (Positive, Negative, or Neutral).
- Sentiment Visualization Dashboard: A simplified dashboard of:
 - Trends in sentiment or by category
 - There were highlighted keywords indicating themes of feedback
- Language Model (NLP engine) The Language Model is an NLP model trained to work with English and Tagalog input (to some extent, the input of informal or dialectal words).
- Feedback Processing Pipeline - Backend infrastructure that ingests the feedback data and generates structured sentiment classes.
- Static Dataset Integration - A system that uses preloaded/static feedback data (not live online or other live

systems).

- Documentation-User Guides, model restrictions, and documentation of use and feedback management in the system.

Success Criteria

The project and its deliverables will be deemed completed when the NLP model categorizes the feedback on English and Tagalog correctly, and the sentiment visualization dashboard will show noticeable trends and meaningful terms. It should not be underdeveloped in functionality, free of bugs, and be able to process static feedback information and meet the desired level of performance without depending on external sources in real-time.

Passing through User Acceptance Testing (UAT), stakeholder approval, and provision of complete documentation are also determinants of success. After the system is deployed, tested, and officially delivered to IRAD with relevant training and sign-off, the project may be considered complete

Project Assumptions

- The security and privacy are already operational in the DOSTSTII to manage user information.
- DOSTSTII already has security and privacy policies in place so that it can deal with the data of the users.
- The training data on which the NLP model is trained has the quality and quantity needed to give decent accuracy on the sentiment classification.

Project Constraints

Time Constriction has to be done within a strict timeframe, including development, testing, and releasing, which reduces the number of features and possible fixes that can be incorporated into it.

Data Constraint – The effectiveness of the model is bound to available training data, whose quality and variety can impact the overall system accuracy.

Technical Limitations- There will be no connection to live external sources or APIs, and the system will handle only static (uploaded) data.

Stakeholder Analysis

Stakeholder Analysis							
Name	Department / Company	Position	Advisers	Objectives, Requirements, Interests	Influence	Project Contribution	Resistance
Arjay Escondo	DOST-STII IRAD	Head of Data Analytics and Evaluation in IRAD	Head of IRAD	Increase productivity and efficiency of current workflow (manual sentiment analysis), improve decision-making	High	Provides information, supports work, and approves deliverables.	N/A
Chester Francisco	DOST-STII IRAD	Senior Science Research Specialist under MIS and planning section	Head of IRAD	Efficient development of the web application. Ensure system is accurate, maintainable and scalable	High	Provides information about technology/frameworks to be used, and supports work.	N/A
IRAD Department	DOST-STII IRAD		Head of IRAD	Faster decision making	Low	Provides information and delegates to the Department Head to relay to the development team (if there ever is any), supports work	N/A

OpenProject Activities

INITIAL BUDGETS

1 – Initiation Phase

1. Initiation Phase Budget

Added by Mark Marabi 30 days ago. Updated 17 days ago.

Cost type

Budget

Fixed date

08/11/2025

Spent (ratio)

2% Total progress

Description

This task involves preparing an initial financial outline for the project during the initiation phase. The goal is to estimate and allocate resources required to successfully launch the project, including costs for research, tools, documentation, and client engagement activities.

UNITS

Planned unit costs

UNITS	COST TYPE	COMMENT	BUDGET
20.00	Transportation expenses Php 100	For gas and commute money	PHP 2,000.00
0.10	Contingency Reserve		PHP 1,000.00
1.00	Office Supplies Php100	Document printing, and writing materials	PHP 100.00
			PHP 3,100.00

Actual unit costs

WORK PACKAGE	UNITS	COST TYPE	COSTS
Task-#1617: 1.0.1 Prospective Client Discovery	5.00	Transportation expenses Php 100	PHP 500.00
Task-#1627: 1.0.2 Finalize choice of IP/PEL Client	5.00	Transportation expenses Php 100	PHP 500.00
Summary-Task-#1629: 1.2 PM Foundations Ch 2 Initiate a p...	4.00	Food Allowance	PHP 400.00
			PHP 1,400.00

LABOR

Planned labor costs

HOURS	USER	COMMENT	BUDGET
100.00 hours	 Gabielle Cabangala		PHP 30,000.00
100.00 hours	 Lorenzo Bernal		PHP 35,000.00
100.00 hours	 Luis Lazaro		PHP 30,000.00
100.00 hours	 Mark Marabi		PHP 40,000.00
			PHP 135,000.00

Actual labor costs

WORK PACKAGE	HOURS	USER	COSTS
Task-#1626: 1.1 Design Thinking Stage 1: Empathize	6.00 hours	 Mark Marabi	PHP 600.00
Task-#1632: 1.2.3 Create Scope	2.00 hours	 Mark Marabi	PHP 200.00
Task-#1631: 1.2.2 Create Objectives	3.00 hours	 Mark Marabi	PHP 300.00
Task-#1633: 1.2.4 Create Stakeholder Analysis	5.00 hours	 Mark Marabi	PHP 500.00
Task-#1630: 1.2.1 Create Charter	2.00 hours	 Mark Marabi	PHP 200.00
			PHP 1,800.00

2 – Planning Phase

2. Planning Phase Budget

Added by Mark Marabi 30 days ago. Updated 8 days ago.

Cost type	Budget
Fixed date	08/11/2025
Spent (ratio)	4% Total progress
Description	Defining financial needs for the planning phase of the creation C6Sense automated sentiment analysis system.

UNITS

Planned unit costs				Actual unit costs			
UNITS	COST TYPE	COMMENT	BUDGET	WORK PACKAGE	UNITS	COST TYPE	COSTS
0.10	Contingency Reserve		PHP 1,000.00	Summary-Task-#449: 2.3.1 Dataflow Diagrams	3.00	Miscellaneous Php100	PHP 300.00
20.00	Transportation expenses Php 100	For gas and commute money	PHP 2,000.00	Summary-Task-#447: 2.2 Design Thinking Stage 3: Ideate	2.00	Office Supplies Php100	PHP 200.00
5.00	Office Supplies Php100	For printing documents, whiteboards, and writing materi...	PHP 500.00				PHP 500.00
1.00	Cloud Services Monthly Subscription	Cloud storage subscription	PHP 283.00				
			PHP 3,783.00				

LABOR

Planned labor costs				Actual labor costs			
HOURS	USER	COMMENT	BUDGET	WORK PACKAGE	HOURS	USER	COSTS
100.00 hours	 Gabrielle Cabangcala		PHP 30,000.00	Summary-Task-#447: 2.2 Design Thinking Stage 3: Ideate	24.00 hours	 Lorenzo Bernal	PHP 2,400.00
100.00 hours	 Lorenzo Bernal		PHP 35,000.00	Summary-Task-#441: 2.4 Allocate Resources	8.00 hours	 Lorenzo Bernal	PHP 800.00
100.00 hours	 Luis Lazaro		PHP 30,000.00	Summary-Task-#400: 2.6 Set deadlines	3.00 hours	 Lorenzo Bernal	PHP 300.00
100.00 hours	 Mark Marabi		PHP 40,000.00	Summary-Task-#442: 2.5 Develop strategies for managing risks	2.00 hours	 Lorenzo Bernal	PHP 200.00
			PHP 135,000.00	Summary-Task-#399: 2.1 Design Thinking Stage 2: Define	3.00 hours	 Lorenzo Bernal	PHP 300.00
							PHP 4,900.00

ROADMAP

1 – Project Setup and Direction



Project Setup and Direction

Identifying stakeholders and their needs, defining project goals, and planning tasks and timelines.

97% Total progress

32 closed (97%) 1 open (3%)

RELATED WORK PACKAGES

- Phase-#394: 1.0 Initiation Phase
- Phase-#395: 2.0 Planning Phase
- Task-#431: 2.3.3 Entity Relationship Diagrams
- Task-#434: 2.3.1.1 Context Diagram
- Task-#435: 2.3.1.2 Dataflow Diagram Level 1
- Task-#436: 2.3.2.1 Use Case Diagram
- Task-#438: 2.3.1.2.1 Dataflow Diagram Level 2.1
- Task-#439: 2.3.1.2.2 Dataflow Diagram Level 2.2
- Task-#441: 2.3.2.1.2 Use Case Fully Dressed 2.3.2.1.2
- Task-#442: 2.3.2.1.1.1 Test Case for UCD 2.3.2.1.1
- Task-#1617: 1.0.1 Prospective Client Discovery
- Task-#1627: 1.0.2 Finalize choice of IIP/PBL Client
- Task-#1628: 1.1 Design Thinking Stage 1: Empathize
- Task-#1630: 1.2.1 Create Charter
- Task-#1631: 1.2.2 Create Objectives
- Task-#1632: 1.2.3 Create Scope
- Task-#1633: 1.2.4 Create Stakeholder Analysis
- Task-#1637: 1.0.3 Initial Client Interview
- Task-#2005: 2.3.1.2.3 Dataflow Diagram Level 2.3
- Task-#2006: 2.3.1.2.4 Dataflow Diagram Level 2.4

2 – Development and Delivery Phase

Development and Delivery Phase

Doing planned tasks, and delivering project outputs

 50% Total progress
2 closed (20%) 8 open (80%)

^ RELATED WORK PACKAGES

- Phase #396: 3.0 Executing Phase
- Phase #2214: 3.1.2 User Story 02
- Phase #2216: 3.1.2.1 Feature 01
- Phase #2217: 3.1.2.1 Task 01
- Task #418: 3.1 Design Thinking Stage 4: Prototype
- Task #419: 3.2 Design Thinking Stage 5: Test
- Task #437: 3.1.1.1 Task 01
- Epic #401: 3.3 Epic 01
- Feature #433: 3.1.1.1 Feature 01
- User story #423: 3.1.1 User Story 01

3 – Managing Progress

Managing Progress

Tracking progress, comparing it to the plan, and identifying any deviations or issues.

 0% Total progress
0 closed (0%) 5 open (100%)

^ RELATED WORK PACKAGES

- Phase #397: 4.0 Monitoring and Controlling
- Task #402: 4.1 Tracking progress
- Task #407: 4.2 Comparing it to the plan
- Task #408: 4.3 Identifying any deviations or issues
- Task #409: 4.4 Measuring performance

4 – Finalization Phase

Finalization Phase

External testing phase, involving a wider audience to gather feedback on usability and performance.

 0% Total progress
0 closed (0%) 7 open (100%)

^ RELATED WORK PACKAGES

- Phase #398: 5.0 Closing Phase
- Task #403: 5.1 Completing all tasks
- Task #404: 5.2 Obtaining final approvals
- Task #405: 5.3 Archiving project documentation
- Task #406: 5.4 Conducting a final review
- Task #410: 5.5 Project Turnover
- Sub Task #432: 5.1.1 User Acceptance Test Completions

WORK PACKAGE

WBS:	2.1
Work Package:	2.1 Design Thinking Stage 2: Define
Package Owner:	QuadThink
Owner Organization:	DOST-STII IRAD
Participants:	• Mark Lyster Marabi • Lorenzo Emil Bernal • Gab Cabangcaia • Luis Lorenzo Lazaro
Description:	Identify the problems and pain points of the client to better see the bigger picture of the overall problem.
Completion State:	Completed main problem statements and "How Might We" statements. This will guide us for the ideation process in Design Thinking Stage 3.
Assumptions:	• Stakeholders (IRAD – DOST-STII) can adopt a full working automated system in their current workflow. • We believe the current manual sentiment analysis workflow of IRAD is very tedious and repetitive.
Risks:	• The AI model behind the automated sentiment analysis system might yield inaccurate results, as human language, primarily English and Tagalog, has semantic meaning and sarcasm that the model might not identify or generalize well to. • There might be an issue regarding the integration of the system in the current sentiment analysis workflow.
Risk Mitigation:	• The AI model must be picked carefully and fine-tuned to handle both English and Tagalog. In the case of unavoidable circumstances, such as the model not generalizing well to Taglish, there might be a need for transparency, which might lead to inaccurate results • The system must be simple enough for IRAD employees to adopt it seamlessly in their workflow.
Budget:	
Reference Docs:	QuadThink_Design Thinking Stages Final Documentation.pdf

PEOPLE

Assignee	 Lorenzo Bernal	Responsible*	 Lorenzo Bernal
Accountable	 Mark Marabi		

ESTIMATES AND PROGRESS

Work	1h	Remaining work	0h
% Complete	100%	Spent time	1h 

DETAILS

Priority *	 Normal	Date	no start date - no finish date
Project phase	 Planning	Category	-
Version	Initiation and planning		

COSTS

Spent units	-	Labor costs	PHP 100.00
Unit costs	-	Overall costs	PHP 100.00
Budget	2. Planning Phase Budget		

BOARDS

1 – Initiation Phase

OpenProject / APC_2025_2026_T1_Mi232_G07 QuadThink CitiSense DOST: Sentiment Analysis System / Boards / Public: 01 Initiation Phase

01 Initiation Phase



To Do	Doing	For Review	Done
+	+	+	+ Closed #1836 - APC_2025_2026_T1... 1.4 Define Timelines Aug 06, 2025 - Aug 14, 2025 LL Closed #1834 - APC_2025_2026_T1... 1.2.5 PM Foundations Ch 2 Initiate a project Completed VM Closed #1837 - APC_2025_2026_T1... 1.0.3 Initial Client Interview Aug 06, 2025 - Aug 14, 2025 VM Closed #1827 - APC_2025_2026_T1... 1.0.2 Finalize choice of IIP/PBL Client Aug 06, 2025 - Aug 14, 2025 VM Closed #1817 - APC_2025_2026_T1... 1.0.1 Prospective Client Discovery Aug 06, 2025 - Aug 14, 2025 VM

2 – Planning Phase

02 Planning Phase

To Do	Doing	For Review	Done
+	+	+ Closed #430 - APC_2025_2026_T1... SUMMARY TASK 2.3.2 Use Cases Jun 06, 2025 - Jun 09, 2025 LL Closed #429 - APC_2025_2026_T1... SUMMARY TASK 2.3.1 Dataflow Diagrams GC	+ Closed #417 - APC_2025_2026_T1... SUMMARY TASK 2.2 Design Thinking Stage 3: Ideate Aug 30, 2025 - Sep 02, 2025 LL Closed #399 - APC_2025_2026_T1... SUMMARY TASK 2.1 Design Thinking Stage 2: Define LL Closed #435 - APC_2025_2026_T1... TASK 2.3.1.2 Dataflow Diagram Level 1 GC Closed #419 - APC_2025_2026_T1... TASK 3.2 Design Thinking Stage 5: Test GC Closed #438 - APC_2025_2026_T1... TASK 2.3.1.2.1 Dataflow Diagram Level 2.1 GC Closed #439 - APC_2025_2026_T1... TASK 2.3.1.2.2 Dataflow Diagram Level 2.2 GC Closed #440 - APC_2025_2026_T1... SUMMARY TASK 2.3.2.1.1 Documents for Test Cases 2.3.2.1.1 Jun 06, 2025 - Jun 09, 2025 LL

OpenProject Updates

Initiation Phase Budget

1. Initiation Phase Budget

Added by Mark Marabi 3 months ago. Updated 2 months ago.

Cost type	Budget
Fixed date	08/11/2025
Spent (ratio)	8% Total progress
Description	This task involves preparing an initial financial outline for the project during the initiation phase. The goal is to estimate and allocate resources required to successfully launch the project, including costs for research, tools, documentation, and client engagement activities.

Planned unit costs				Actual unit costs			
UNITS	COST TYPE	COMMENT	BUDGET	WORK PACKAGE	UNITS	COST TYPE	COSTS
20.00	Transportation expenses Php 100	For gas and commute money	PHP 2,000.00	Summary-Task-#1029: 1.2 PM Foundations Ch 2 Initiate a ...	4.00	Food Allowance	PHP 400.00
0.10	Contingency Reserve		PHP 1,000.00	Task-#1017: 1.0.1 Prospective Client Discovery	5.00	Transportation expenses Php 100	PHP 500.00
1.00	Office Supplies Php100	Document printing, and writing materials	PHP 100.00	Task-#1027: 1.0.2 Finalize choice of IIP/PBL Client	5.00	Transportation expenses Php 100	PHP 500.00
			PHP 3,100.00				PHP 1,400.00

Planned labor costs				Actual labor costs			
HOURS	USER	COMMENT	BUDGET	WORK PACKAGE	HOURS	USER	COSTS
100.00 hours	 Gabrielle Cabangcala		PHP 30,000.00	Task-#1037: 1.0.3 Initial Client Interview	1.00 hours	 Lorenzo Bernal	PHP 100.00
100.00 hours	 Lorenzo Bernal		PHP 35,000.00	Task-#1020: 1.1 Design Thinking Stage 1: Empathize	48.00 hours	 Lorenzo Bernal	PHP 4,800.00
100.00 hours	 Luis Lazaro		PHP 30,000.00	Task-#1020: 1.1 Design Thinking Stage 1: Empathize	6.00 hours	 Mark Marabi	PHP 600.00
100.00 hours	 Mark Marabi		PHP 40,000.00	Summary-Task-#1036: 1.4 Define Timelines	4.00 hours	 Lorenzo Bernal	PHP 400.00
			PHP 135,000.00	Task-#1017: 1.0.1 Prospective Client Discovery	2.00 hours	 Lorenzo Bernal	PHP 200.00
				Task-#1027: 1.0.2 Finalize choice of IIP/PBL Client	2.00 hours	 Lorenzo Bernal	PHP 200.00

Planning Phase Budget

2. Planning Phase Budget

Added by Mark Marabi 3 months ago. Updated about 2 months ago.

Cost type	Budget
Fixed date	08/11/2025
Spent (ratio)	8% Total progress
Description	Defining financial needs for the planning phase of the creation CitiSense automated sentiment analysis system.

Planned unit costs				Actual unit costs			
UNITS	COST TYPE	COMMENT	BUDGET	WORK PACKAGE	UNITS	COST TYPE	COSTS
0.10	Contingency Reserve		PHP 1,000.00	Summary-Task-#429: 2.3.1 Dataflow Diagrams	3.00	Miscellaneous Php100	PHP 300.00
20.00	Transportation expenses Php 100	For gas and commute money	PHP 2,000.00	Summary-Task-#417: 2.2 Design Thinking Stage 3: Ideate	2.00	Office Supplies Php100	PHP 200.00
5.00	Office Supplies Php100	For printing documents, whiteboards, and writin...	PHP 500.00				PHP 500.00
1.00	Cloud Services Monthly Subscription	Cloud storage subscription	PHP 283.00				
			PHP 3,783.00				

Planned labor costs				Actual labor costs			
HOURS	USER	COMMENT	BUDGET	WORK PACKAGE	HOURS	USER	COSTS
100.00 hours	 Gabrielle Cabangcala		PHP 30,000.00	Task-#442: 2.3.2.1.1.1 Test Case for UCD 2.3.2.1	3.00 hours	 Lorenzo Bernal	PHP 300.00
100.00 hours	 Lorenzo Bernal		PHP 35,000.00	Summary-Task-#417: 2.2 Design Thinking Stage 3: Id...	24.00 hours	 Lorenzo Bernal	PHP 2,400.00
100.00 hours	 Luis Lazaro		PHP 30,000.00	Summary-Task-#411: 2.4 Allocate Resources	8.00 hours	 Lorenzo Bernal	PHP 800.00

Roadmap



Project Setup and Direction

Identifying stakeholders and their needs, defining project goals, and planning tasks and timelines.

100% Total progress

33 closed (100%) 0 open (0%)

RELATED WORK PACKAGES

- [Phase #394](#): 1.0 Initiation Phase
- [Phase #395](#): 2.0 Planning Phase
- [Task #431](#): 2.3.3 Entity Relationship Diagrams
- [Task #434](#): 2.3.1.1 Context Diagram
- [Task #435](#): 2.3.1.2 Dataflow Diagram Level 1
- [Task #436](#): 2.3.2.1 Use Case Diagram
- [Task #438](#): 2.3.1.3.1 Dataflow Diagram Level 2: 1.0 - Manage Account
- [Task #439](#): 2.3.1.3.2 Dataflow Diagram Level 2: 2.0 - Perform Sentiment Analysis
- [Task #441](#): 2.3.2.1.2 Use Case Fully Dressed for UCD 2.3.2.1
- [Task #442](#): 2.3.2.1.1.1 Test Case for UCD 2.3.2.1
- [Task #1017](#): 1.0.1 Prospective Client Discovery
- [Task #1027](#): 1.0.2 Finalize choice of IIP/PBL Client
- [Task #1028](#): 1.1 Design Thinking Stage 1: Empathize
- [Task #1030](#): 1.2.1 Create Charter
- [Task #1031](#): 1.2.2 Create Objectives
- [Task #1032](#): 1.2.3 Create Scope
- [Task #1033](#): 1.2.4 Create Stakeholder Analysis
- [Task #1037](#): 1.0.3 Initial Client Interview
- [Task #2005](#): 2.3.1.3.3 Dataflow Diagram Level 2: 4.0 - Manage Reports
- [Task #3014](#): 2.3.4 Activity Diagram with Swimlanes

New and Unassigned Work Packages

APC_2025_2026_T1_M123...	OpenProject / APC_2025_2026_T1_M1232_G07 QuadThink CtiSense DOST: Sentiment Analysis System / Work packages / Default: All open							
← Work packages	+ Create Include projects Baseline Filter							
Q Search by name	All open							
FAVORITE	ID	SUBJECT	TYPE	STATUS	ASSIGNEE	PRIORITY	PROJECT PHASE	VERSION
All Budgets and Costs	396	3.0 Executing Phase	PHASE	To be scheduled	-	Normal	Executing	Development and Delivery Phase
All Work Packages	401	3.3 Epic 01	EPIC	In progress	-	Normal	Executing	-
DEFAULT	423	3.1.1 User Story 1: User Account Management	USER STORY	New	18 Lorenzo Bernal	Normal	Executing	-
All open	433	3.1.1.1 Feature: Credentials Login	FEATURE	New	-	Normal	Executing	Development and Delivery Phase
Latest activity	2598	3.1.1.1.1 Task: Develop a Login Form	TASK	New	-	Normal	Executing	Development and Delivery Phase
Recently created	2652	3.1.1.1.2 Task: Validate User Inputs for Login	TASK	New	-	Normal	Executing	Development and Delivery Phase
Overdue	2654	3.1.1.1.3 Task: Handling Errors for Login	TASK	New	-	Normal	Executing	Development and Delivery Phase
Summary	2585	3.1.1.2 Feature: Google OAuth	FEATURE	New	-	Normal	Executing	Development and Delivery Phase
Created by me	2606	3.1.1.2.1 Task: Implement Google OAuth Login	TASK	New	-	Normal	Executing	Development and Delivery Phase
Assigned to me	2587	3.1.1.3 Feature: Edit Profile	FEATURE	New	-	Normal	Executing	Development and Delivery Phase
Shared with users	2614	3.1.1.3.1 Task: Setup Edit Profile Functionality	TASK	New	-	Normal	Executing	Development and Delivery Phase
Shared with me	2600	3.1.1.4 Feature: Register Account	FEATURE	New	-	Normal	Executing	Development and Delivery Phase
PRIVATE	2622	3.1.1.4.1 Task: Create Register Form	TASK	New	-	Normal	Executing	Development and Delivery Phase
New manually sorted query	2650	3.1.1.4.2 Task: Validate User Inputs for Registration	TASK	New	-	Normal	Executing	Development and Delivery Phase
New manually sorted query	2651	3.1.1.4.3 Task: Handling Errors for Registration	TASK	New	-	Normal	Executing	Development and Delivery Phase
	2214	3.1.2 User Story 2: Automated Sentiment Analysis and Reporting	USER STORY	New	-	Normal	Executing	-
	2216	3.1.2.1 Feature: Dashboard	FEATURE	In progress	-	Normal	Executing	Development and Delivery Phase
	(1 - 47/47)							
	Per page: 20 100							

Backlogs

- These are the prioritized features that need to be completed.

Development and Delivery Phase 0 ▾		
2216	Feature: 3.1.2.1 Feature: Dashboard	In progr...
2590	Feature: 3.1.2.3 Feature: AI Model	In progr...
2585	Feature: 3.1.1.2 Feature: Google OAuth	New
2600	Feature: 3.1.1.4 Feature: Register Account	New
433	Feature: 3.1.1.1 Feature: Credentials Login	New
2640	Feature: 3.1.4.1 Feature: User Roles	New
2587	Feature: 3.1.1.3 Feature: Edit Profile	New
2561	Feature: 3.1.3.1 Feature: Data Table	New

AY 2025-2026 T1 Sprint 01 Board

AY 2025-2026 Sprint 01 - QuadThink

Committed Backlog Items

+

In progress ▾ #2604 - APC_2025_202...

TASK 3.1.2.1.1 Task: Generate Charts from Labeled Data

GC Sep 18, 2025 - Oct 06, 2025

New ▾ #2601 - APC_2025_2026_T1_M...

TASK 3.1.2.3.1 Task: Fine-tune chosen AI Model

MM Sep 18, 2025 - Oct 06, 2025

Tasks Assigned (Not Started)

+

In Progress

+

Closed ▾ #3014 - APC_2025_2026_T1...

TASK 2.3.4 Activity Diagram with Swimlanes

LB Sep 18, 2025 - Oct 06, 2025

Closed ▾ #2085 - APC_2025_2026_T1...

TASK 2.3.1.3.3 Dataflow Diagram Level 2: 4.0 - Manage Reports

LB

Closed ▾ #442 - APC_2025_2026_T1_...

TASK 2.3.2.1.1.1 Test Case for UCD 2.3.2.1

LL Sep 18, 2025 - Oct 03, 2025

Done

+

Closed ▼ #441 - APC_2025_2026_T1_...

TASK 2.3.2.1.2 Use Case Fully Dressed
for UCD 2.3.2.1

LL

Jun 06, 2025 - Oct 06, 2025

Closed ▼ #434 - APC_2025_2026_T1_...

TASK 2.3.1.1 Context Diagram

GC

Closed ▼ #436 - APC_2025_2026_T1_...

TASK 2.3.2.1 Use Case Diagram

LB

📅 Jun 06, 2025 - Oct 06, 2025

Closed ▼ #438 - APC_2025_2026_T1_...

TASK 2.3.1.3.1 Dataflow Diagram
Level 2: 1.0 - Manage Account

LL

Closed ▼ #435 - APC_2025_2026_T1_...

TASK 2.3.1.2 Dataflow Diagram Level
1

LB

Closed ▼ #431 - APC_2025_2026_T1_...

TASK 2.3.3 Entity Relationship
Diagrams

LB

All open

Create

Include projects 1

Baseline

Filter 1

ID	TYPE	SUBJECT	STATUS	START DATE	FINISH DATE	2025 Q2 Q3 Q4 May Jun Jul Aug Sep Oct Nov Dec Jan												
396	PHASE	3.0 Executing Phase	To be scheduled	05/30/2025	10/06/2025	10/06/2025	10/06/2025 3.0 Executing Phase											
401	EPIC	3.3 Epic 01	In progress	05/30/2025	10/06/2025	10/06/2025	10/06/2025 3.3 Epic 01											
423	USER STORY	3.1.1 User Story 1: User Account Management	New	05/30/2025	10/06/2025	10/06/2025	10/06/2025 3.1.1 User Story 1: User Account Management											
433	FEATURE	3.1.1.1 Feature: Credentials Login	New	05/30/2025	10/06/2025	10/06/2025	10/06/2025 3.1.1.1 Feature: Credentials Login											
2654	TASK	3.1.1.1.3 Task: Handling Errors for Login	New	05/30/2025	10/06/2025	10/06/2025	10/06/2025 3.1.1.1.3 Task: Handling Errors for Login											
2652	TASK	3.1.1.1.2 Task: Validate User Inputs for Login	New	05/30/2025	06/03/2025	10/06/2025	06/03/2025 3.1.1.1.2 Task: Validate User Inputs for Login											
2598	TASK	3.1.1.1.1 Task: Develop a Login Form	New	09/18/2025	10/06/2025	10/06/2025	09/18/2025 3.1.1.1.1 Task: Develop a Login Form											
2600	FEATURE	3.1.1.4 Feature: Register Account	New	09/18/2025	10/06/2025	10/06/2025	09/18/2025 3.1.1.4 Feature: Register Account											
2651	TASK	3.1.1.4.3 Task: Handling Errors for Registration	New	09/18/2025	10/06/2025	10/06/2025	09/18/2025 3.1.1.4.3 Task: Handling Errors for Registration											
2650	TASK	3.1.1.4.2 Task: Validate User Inputs for Registration	New	09/18/2025	10/06/2025	10/06/2025	09/18/2025 3.1.1.4.2 Task: Validate User Inputs for Registration											
2622	TASK	3.1.1.4.1 Task: Create Register Form	New	09/18/2025	10/06/2025	10/06/2025	09/18/2025 3.1.1.4.1 Task: Create Register Form											
2587	FEATURE	3.1.1.3 Feature: Edit Profile	New	09/18/2025	10/06/2025	10/06/2025	09/18/2025 3.1.1.3 Feature: Edit Profile											
2614	TASK	3.1.1.3.1 Task: Setup Edit Profile Functionality	New	09/18/2025	10/06/2025	10/06/2025	09/18/2025 3.1.1.3.1 Task: Setup Edit Profile Functionality											
2585	FEATURE	3.1.1.2 Feature: Google OAuth	New	09/18/2025	10/06/2025	10/06/2025	09/18/2025 3.1.1.2 Feature: Google OAuth											
2606	TASK	3.1.1.2.1 Task: Implement Google OAuth Login	New	09/18/2025	10/06/2025	10/06/2025	09/18/2025 3.1.1.2.1 Task: Implement Google OAuth Login											
2571	USER STORY	3.1.4 User Story 4: Manage User	New	09/18/2025	10/06/2025	10/06/2025	09/18/2025 3.1.4 User Story 4: Manage User											

Stage 1: Empathize

In the first stage of Design Thinking, our group, QuadThink, aims to achieve the goal of gaining a deeper understanding of the needs, wants, and circumstances of our client, together with the customers. In order to achieve this goal, our group conducted several online interviews via Zoom together with our client and the IRAD (Information Resource and Analysis Division) department of DOST-STII (Science and Technology Information Institute). This allowed us to directly gather relevant ideas even though we are not physically present in various meetings.

Whenever our group meets with the client and customers, we ensure that we gather correct and accurate information regarding their concerns and perspectives to provide a suitable solution for their challenges. Our group made use of various guidelines that were presented during class discussions in order to stay right on track. Moreover, our group made use of the 5 Whys to dig into the main cause of the problem. In addition, our group also asked open-ended questions to gather more relevant information about the problem, as well as to document the client and customers' detailed and authentic responses. The recorded sessions have helped our group to create customer personas that match the perspectives of the customers involved in order to visualize and organize the information gathered. Lastly, our group made an empathy map and pain-gain analysis to recognize their behaviors, feelings, and pinpoint their frustrations and opportunities for development.

With the help of these activities, our group was able to better understand the issues and problems of the IRAD department and to prepare for addressing all of their needs in the next steps of the design thinking process.

Interview with the Client

(5 whys):

- Why is the sharing of ideas across teams challenging with your current system?
 - “We don’t have a system.”
- Why don’t you have a system?
 - “Well, new, di sya new pero how can I say it, it's not common for government agencies to analyze sentiments or ung comments. It's not common for agencies to analyze deeply ung mga text data.”
- Why is it not common?
 - “So AI is new, not everyone, not all agencies can adjust or adapt to AI. Advent din talaga ng AI yung trigger nyo.”
- Why can’t they adapt/adjust with AI?
 - “Of course, the limitation of resources includes technical skills. Without APC mahihirapan kami i-build yan.”
- Why is there a limit of resources?
 - “Limitation on resources? Budget noh? Ano bang klaseng resource? Human resources? Financial resources? If we limit the resources to technical skills? Mas madali, or budget-wise kasi, poor answer kasi yun kapag wala kang budget eh. Sa limitation of resources siguro (technical skills), and then yung limitation na yon ai is new. Advent ng ai siguro, yung limitation natin sa skills in-house is dahil very new pa yung ai.”

Open-ended Questions

o What do you think a sentiment analysis tool would do to assist your IT team in decision-making or service improvement?

▪ “Much faster processing time, with better, faster processing data, faster recommendations. Service would improve service based on the data if it is faster.”

o Have you tried using similar technologies or tools in the past? If so, what worked and what didn’t?

- “None, manual.”
- o What does a successful outcome for this project look like from your perspective?
 - “A working model, with a 70% accuracy for the system. For organizational: we can tweak services to serve the needs of the client.”
- o What concerns or potential risks do you think we should be mindful of when implementing this project?
 - “System security and data privacy since we are handling personal data, since it's client respondents.”
- o How often would you like to review progress, and what from should those updates be?
 - “Best is quarterly, in terms of reports and presentation.

Customer Personas

Customer: Arjay Escondo

Biography: Arjay Escondo is a data analyst who evaluates the performance of DOST STII IRAD's research programs by cleaning data, analyzing feedback sentiments, and creating visual reports manually.

Motivations: 1. To make our work easier and faster, 2. To deliver more accurate insights, 3. To automate current workflow

Goals: 1. Ensure consistency among reports, 2. Save time and effort of our people, 3. Automate sentiment classification

Frustrations: 1. Manual work takes too long, 2. Prone to human errors, 3. Overwhelmed by large data volumes

ARJAY ESCONDO

PROFILE

Age : 39
Role : Researcher / Data Analyst
Education : Statistics / Data Science
Tech Savvy : Moderate



Mr. Arjay Escondo

BIOGRAPHY

This persona is Arjay Escondo, a data analyst who specializes in evaluating the performance of DOST's research programs. Daily tasks involve cleaning data, analyzing feedback sentiments, and preparing visual reports in manual ways. However, handling unstructured public feedback like survey comments can be time-consuming, especially doing it manually, and the current workflow may often miss sentiment nuances. This person would really value a tool that automate repetitive work so more time can be spent on deeper analysis and providing meaningful insights for decision-making.

MOTIVATIONS

- To make our work easier and faster
- To deliver accurate insights
- To automate current workflow

GOALS

- Ensure consistency among reports
- Save time and effort of our people
- Automate sentiment classification

FRUSTRATIONS

- Manual work takes too long
- Prone to human errors
- Overwhelmed by large data volumes

Customer: Chester Francisco

Biography: Chester Francisco is a Senior Research Specialist in Management Information Systems at DOST-STII who ensures digital platforms run smoothly and securely so staff can work efficiently without technical disruptions.

Motivations: 1. To automate current workflow, 2. To improve operational efficiency, 3. To support data-driven decision-making

Goals: 1. Ensure seamless integration of CitiSense into existing DOST systems, 2. Maintain system stability and security, 3. Provide reliable tech support for staff using the tool

Frustrations: 1. Inefficient manual processes, 2. Slow turnaround of data reports, 3. Frequent human errors in data handling

CHESTER FRANCISCO

PROFILE

Age : 27
Role : IT Support / Systems Administrator
Education : Computer Science
Tech Savvy : Very High



Mr. Chester Francisco

BIOGRAPHY

This is Chester Francisco, works as an IT staff member at DOST-STII and is responsible for ensuring that digital platforms run smoothly and securely. Most of the time is spent troubleshooting errors and maintaining databases. Although the work is technical and often behind the scenes, the main drive is to enable other staff to focus on their tasks without worrying about technical failures.

MOTIVATIONS

- To improve operational efficiency
- To automate current workflow
- To support data-driven decision-making


GOALS

- Ensure seamless integration of CitiSense into existing DOST systems
- Maintain system stability and security
- Provide reliable tech support for staff using the tool

FRUSTRATIONS

- Inefficient manual processes
- Slow turnaround of data reports
- Frequent human errors in data handling

Empathy Map

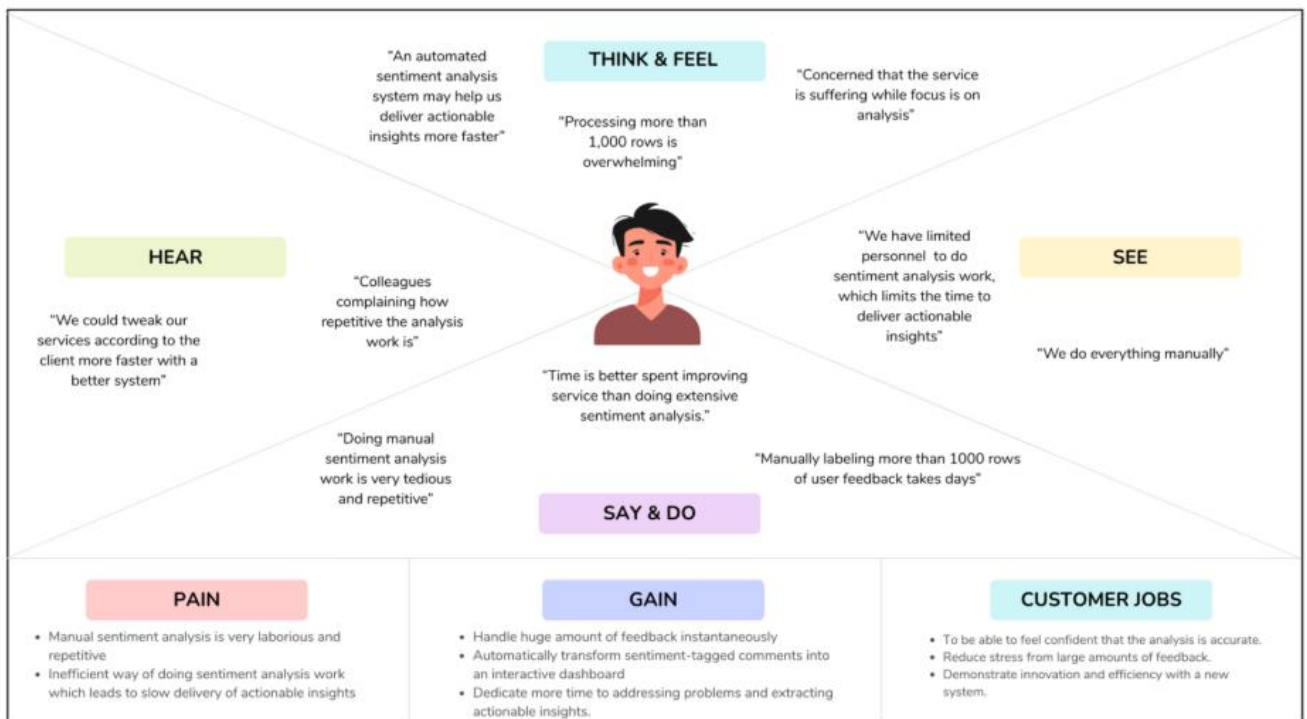

Stage 2: Define

Introduction

For the second stage of the design thinking process, our group utilized all the information gathered during the first stage, Empathize, where we conducted several interviews with our client and customers. Utilizing all the collected information, our group carefully analyzed the perspectives, insights, and challenges of each person involved in this project in order to determine a clear point of view (POV) and problem statement. Establishing a proper and organized structure was crucial for our group since it would serve as a guide in preparing for the other stages of the design thinking process.

The first stage of design thinking generated a huge amount of information with the use of interviews and user experiences, and with this, it is necessary for the team to organize and synthesize the findings. This will allow the team to categorize all the user experiences and challenges. With the help of this process, we transformed all the gathered information into structured and organized insights, ensuring clarity and harmony among the team members.

Clustering Problem Ideas

As you can see in this figure, our group lists challenges with the current manual sentiment analysis of the DOST-STII IRAD department and categorizes them into four main categories, namely: Inefficiency Problems, Technology Gaps, and Time Optimization. These categorizations were consolidated through a group discussion in order to highlight the root causes and issues that affect the efficiency, innovation, and productivity of the said department.

Inefficiency Problems

The current manual sentiment analysis of the DOST-STII IRAD department consumes a lot of time and effort to execute the process effectively. This inefficiency affects productivity and makes it difficult for data analysts to handle and analyze large amounts of data. In addition, there is a high chance of uncertainty for the accuracy of results, and this may lead to doubts about the reliability of the insights that came from the feedback. Moreover, these challenges limit the ability of the department to make haste for data improvements.

Technology Gaps

The third cluster of issues is about the absence of technology and system integration. Currently, the DOST-STII IRAD department has no automated system for its sentiment analysis, for them to upload and analyze feedback, which then results in a delayed or slower processing of sentiments with several inconsistencies. There is a lack of tools for properly managing and processing large amounts of data, which leads to difficulty in making scalable operations. Furthermore, the absence of an integrated visualization dashboard also prevents users from easily identifying and analyzing trends and interpreting results accurately and strategically.

Time optimization

The manual sentiment analysis process creates an excessive amount of workload for employees, specifically when it comes to handling large amounts of feedback from people who experience the services of DOST-STII. Tasks such as reading, categorizing, and interpreting customer feedback are some of the primary examples of repetitive work that DOST-STII employees face every day. These tasks take up valuable time that could be used for other priorities and innovations.

Problem Statements

1. Doing manual sentiment analysis work is tedious and repetitive
2. Data analysts could be doing a lot more tasks involving the betterment of the services rather than focusing much of their time on manual sentiment analysis.
3. There is a need for an automated sentiment analysis system that can handle both English and Tagalog languages.

How Might We Questions

After identifying the problem statements, our group then proceeds to create “How Might We” questions. These questions will turn the identified issues into new opportunities for innovation, guiding our group to generate effective and innovative solutions. The problem statements serve as a stepping stone for developing these types of questions and to ensure that our group is aligned with the needs of our client and customers.

Here are the How Might We questions that our team initiated:

1. How might we reimagine helping IRAD employees to transform raw feedback data into actionable insights that directly improve service delivery automatically?
2. How might we reimagine helping IRAD employees in streamlining their current manual sentiment analysis workflow?
3. How might we reimagine enabling IRAD employees to deliver greater value by focusing more on improving service delivery, instead of spending excessive time on manual sentiment analysis?

Conclusion

There is a need for improvement regarding the manual process of the sentiment analysis of the DOST-STII IRAD department. The clustered problems identified in the paper highlight the need to have an automated sentiment analysis system. In order for the team to be aligned and guided, we formulate clear problem statements. The “How Might We” questions serve as a guide to create possible innovative solutions that should address efficiency and accuracy of the process. In addition, implementing automation and visualization tools would reduce employee workload and improve the accuracy of insights. To sum it all up, the analysis emphasizes the importance of

integrating and adopting technology-driven solutions in order to enhance productivity, innovation, and service quality within the department.

Stage 3: Ideate

Introduction


At this stage of the design thinking process, our group gathered together to identify each of our own ideas to integrate into the website application. This stage allows us to combine different ideas and make sure that the goals of this project are met.

Brainstorming Session

Brainstorming

- We will design an automated sentiment analysis system that can process large volumes of feedback quickly and accurately, reducing employee workload.
- The system will also provide real-time insights and visual dashboards, enabling IRAD employees to make faster and more informed decisions.
- Web application/system that can automatically output sentiment labels on English, Tagalog, and Taglish datasets
- Automated data to dashboard visualization
- Provide IRAD staff with real-time visuals without requiring manual analysis by developing a bilingual AI-powered dashboard that automatically categorizes feedback into positive, neutral, and negative sentiments.
- Integrate keyword clustering and trend detection so IRAD employees can instantly see which feedbacks are most common, helping them prioritize improvements faster.
- Sentiment Timelines
- Able to detect both English and Tagalog


Our group gathered in an online meeting to discuss our opinions on addressing the client's needs and solving challenges regarding their system.




In this session, each member contributed their ideas for the making of the Crazy 8. We included features that we want to integrate in the website application and explained what each drawing represents.

Post-It Voting

Post-it voting

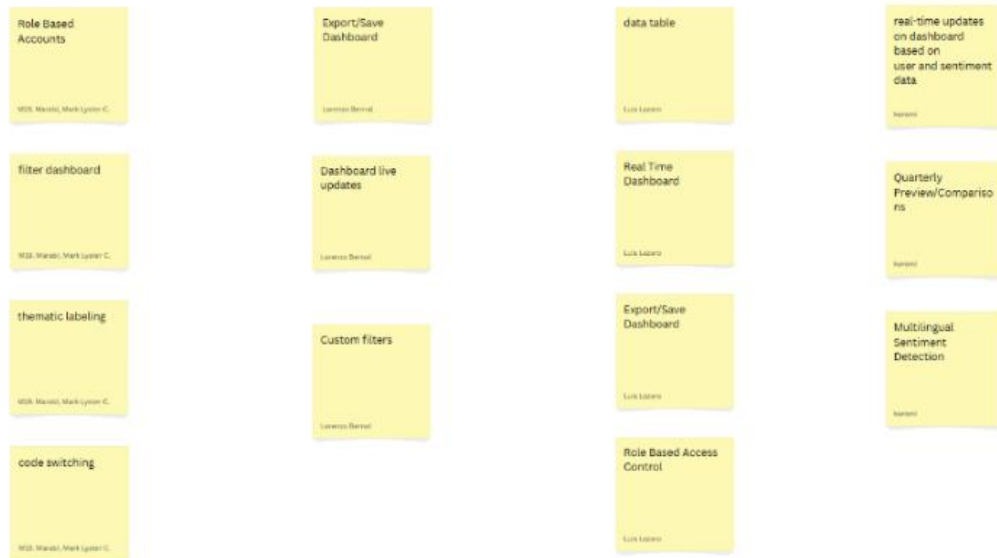

Post-it voting



After discussing and finalizing the Crazy 8, our team, Quadthink proceeded with a post-it voting assessment. Each member had an opportunity to vote for the ideas that were most innovative and aligned with the project's objectives

Feasibility-Viability-Desirability Analysis

D-F-V Analysis



After the post-it voting, our group proceeded with the Feasibility-Viability-Desirability Analysis to further evaluate the selected ideas. By utilizing this framework, our group was able to narrow down our options and prioritize ideas that demonstrated the strongest qualities for the website application.

For the functionality that encapsulates the three categories of the Venn diagram, we have:

- Filters
- Role-Based Access Control
- Dashboard
- Multilingual AI Model

These are the functionalities that our customers desire most, are feasible with current technologies, and are viable as they provide long-term value for our clients in the context of service delivery.

As for Feasible and Viable only, we have:

- Data Table
- Generate Reports


These are only at the feasible and viable level, as these functionalities can be done outside our system, such as editing the data in Google Sheets. As for Generate Reports, our clients can make inferences and generate reports according to what they are currently seeing in the dashboard and data table outside of our proposed system.

Stage 4: Prototype

Introduction


At this stage of the Design Thinking process, our group, QuadThink, focused on creating prototypes that demonstrate the core features of our system solution. Each prototype highlights how users will interact with the system to ensure usability and efficiency. Our group conducted several meetings with our clients to demonstrate and simulate real user experiences. Furthermore, through this scenario, we were able to visualize how our system could operate in practice. Overall, these prototypes will serve as a foundation for future development, providing our group with a clear direction for enhancing the system's functionality.

Storyboard of the current manual workflow of our client (to visualize what our system aims to solve, which is the automation of the manual sentiment analysis workflow):

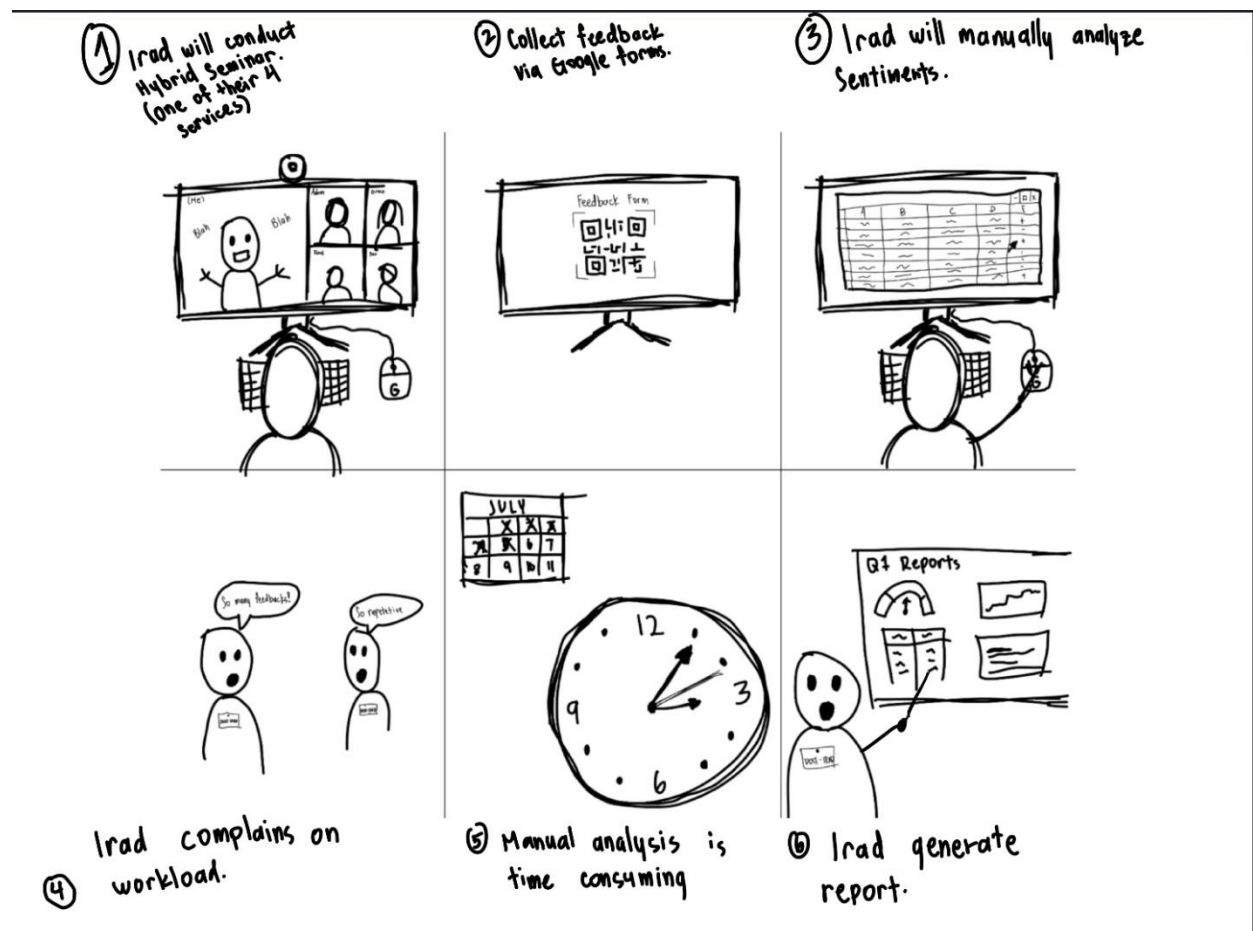

Storyboard for our proposed system, along with the benefits of using it:


1 automatic data transfer
from gsheets to system
database




2 Cleaning & pre-
processing
of raw data for accuracy &
consistency



3 running sentiment analysis
to categorize data



4 Dashboard shows
insights clearly. Data can be
exported by sentiment.



5 Exported data is turned
into detailed reports
for conclusions and
decision making



6 Faster work, smarter
insights, better decisions





Department
of
Science
and
Technology

DOST-CitiSense

First Name

Last Name

Email

Password

Register

Already have an account? [Login](#)



Department
of
Science
and
Technology

DOST-CitiSense

Email

Password

Login



[Forgot Password?](#)

 Sign in with Google



Preview data

Service										Edit	Save
Services	Session	Timestamp	Sex	Category	Type of Library	Region	What are your key takeaways	Comments	Were there any aspects of the library	Sentiment	
Hybrid Seminar	The Art and Science of Collection Devote	8/20/2024 15:57:44	Male	Librarian Staff	Academic Library	REGION XI	-	-		Positive	
Hybrid Seminar	The Art and Science of Collection Devote	8/20/2024 15:58:12	Female	Librarian Staff	Academic Library	REGION XI	-	-		Neutral	
Hybrid Seminar	The Art and Science of Collection Devote	8/20/2024 16:00:07	Male	Librarian Staff	School Library	REGION IV-A	NA			Negative	
Hybrid Seminar	The Art and Science of Collection Devote	8/20/2024 16:00:16	Female	Librarian Staff	School Library	REGION XI	NA	NA		Positive	
Hybrid Seminar	The Art and Science of Collection Devote	8/20/2024 16:00:16	Female	Librarian Staff	Academic Library	REGION IV-A	-			Negative	
Hybrid Seminar	The Art and Science of Collection Devote	8/20/2024 16:00:19	Female	Librarian Staff	School Library	REGION VIII	key performance indicators			Negative	
Hybrid Seminar	The Art and Science of Collection Devote	8/20/2024 16:00:23	Female	Students	Non-library Institution	REGION X	NA	NA		Negative	
Hybrid Seminar	The Art and Science of Collection Devote	8/20/2024 16:00:23	Female	Professors/Instructors/	Non-library Institution	REGION IV-A	Many			Neutral	
Hybrid Seminar	The Art and Science of Collection Devote	8/20/2024 16:00:24	Male	Librarian Staff	Special Library	REGION IV-A	thank you for the collection	thank you for the		Neutral	
Hybrid Seminar	The Art and Science of Collection Devote	8/20/2024 16:00:24	Male	Professors/Instructors/	School Library	REGION IV-A	NA			Neutral	
Hybrid Seminar	The Art and Science of Collection Devote	8/20/2024 15:59:33	Female	Librarian Staff	Special Library	REGION X	My key takeaways from the	The hybrid format		Neutral	
Hybrid Seminar	The Art and Science of Collection Devote	8/20/2024 15:59:38	Female	Librarian Staff	Public Library	REGION XI	-			Neutral	
Hybrid Seminar	The Art and Science of Collection Devote	8/20/2024 15:59:40	Female	Professors/Instructors/	School Library	NCR	VERY INTERESTING TOPIC	NONE		Neutral	
Hybrid Seminar	The Art and Science of Collection Devote	8/20/2024 15:59:46	Male	Librarian Staff	School Library	NCR	Collection development is a	NA		Neutral	
Hybrid Seminar	The Art and Science of Collection Devote	8/20/2024 15:59:46	Male	Private Employee	Non-library Institution	REGION X	To review the collection	Hopefully, in the		Negative	
Hybrid Seminar	The Art and Science of Collection Devote	8/20/2024 15:59:46	Female	Librarian Staff	Special Library	NCR	NA			Negative	
Hybrid Seminar	The Art and Science of Collection Devote	8/20/2024 15:59:47	Male	Librarian Staff	Academic Library	REGION IV-A	Prioritize community needs			Positive	

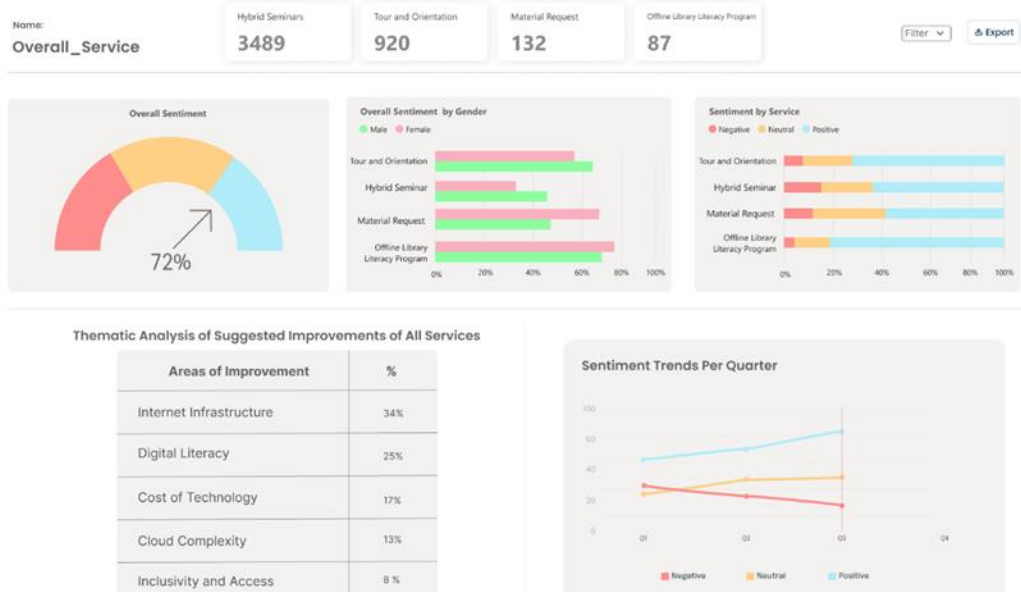

Stage 5: Testing

Introduction


For the fifth stage of the Design Thinking process, our group, QuadThink, presented the prototype of our automated sentiment analysis system to our client for testing as well as feedback. Our group demonstrated how to use the system, which includes properly addressing the

challenges of the manual sentiment analysis system, such as providing a visualization dashboard for feedback analysis. The prototype is carefully designed to align with the goals and objectives of our client and was guided by references from tools to cater to the needs of the client. Aside from the minor adjustments to the system, the client appreciated the overall functionality of the system and is positive that this project would be beneficial for the decision-making process of the DOST-STII IRAD department.

Meeting Link: [video1342409374.mp4](#)


Client Comment:

- The client noted that they will add a column in the Google Sheets source data to reflect quarterly information. Once this column has been included, our group, QuadThink, will receive the updated data, enabling the system to incorporate a new filter in the dashboard for quarterly analysis alongside the existing per-service filter (e.g., January, February, March – Quarter 1). A total of 4 Quarters for the filter.

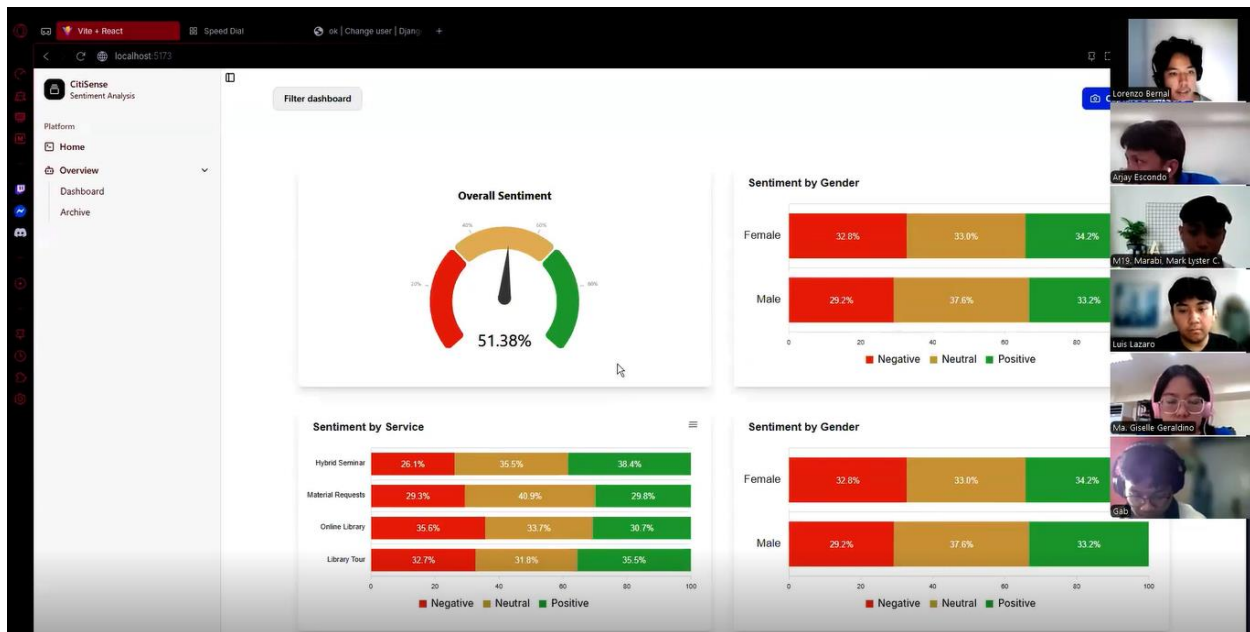


Data Flow Diagram


Level 0 – Context Diagram

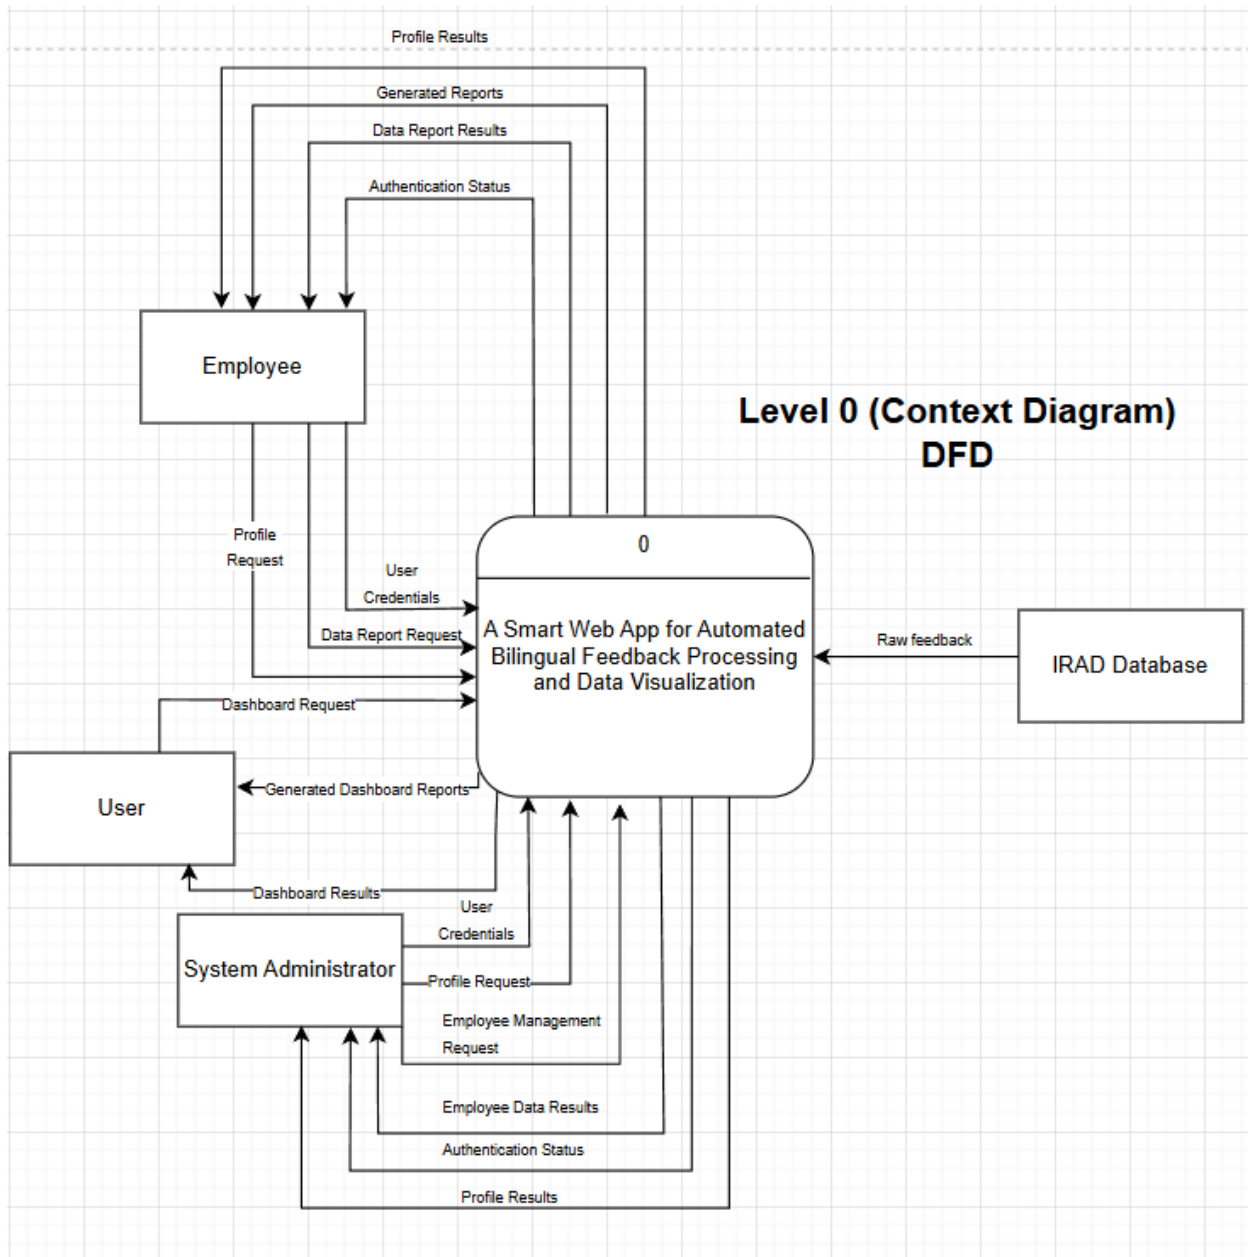


Level 1 DFD

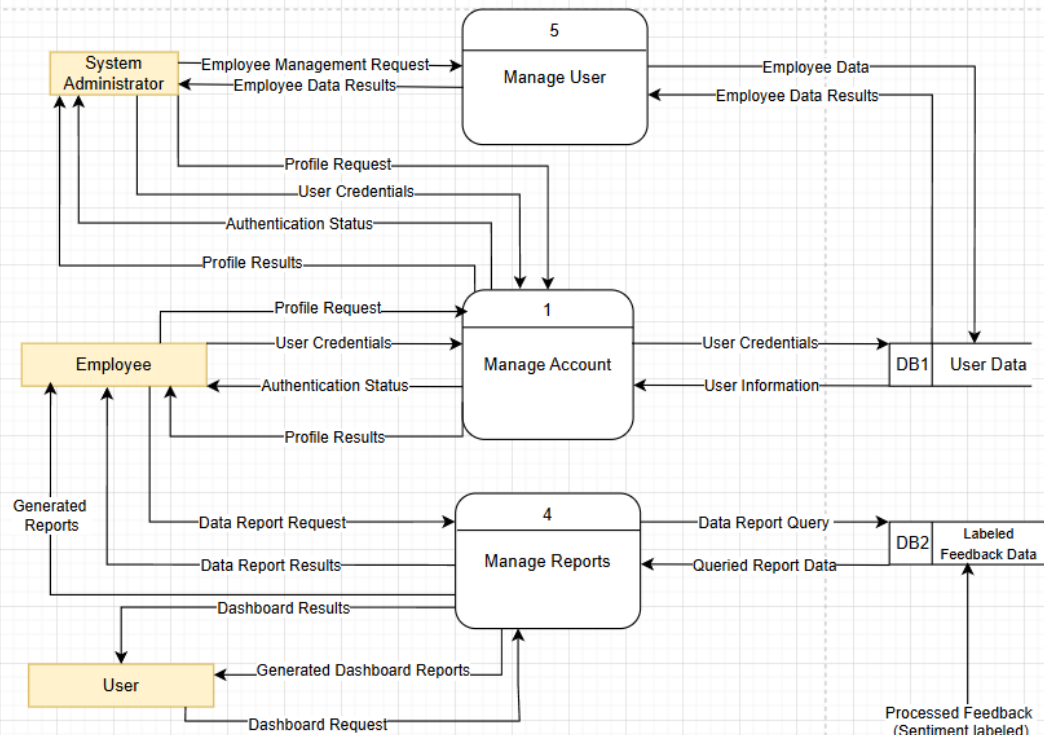


Level 1 DFD




Level 2 – 1.0 Manage Account

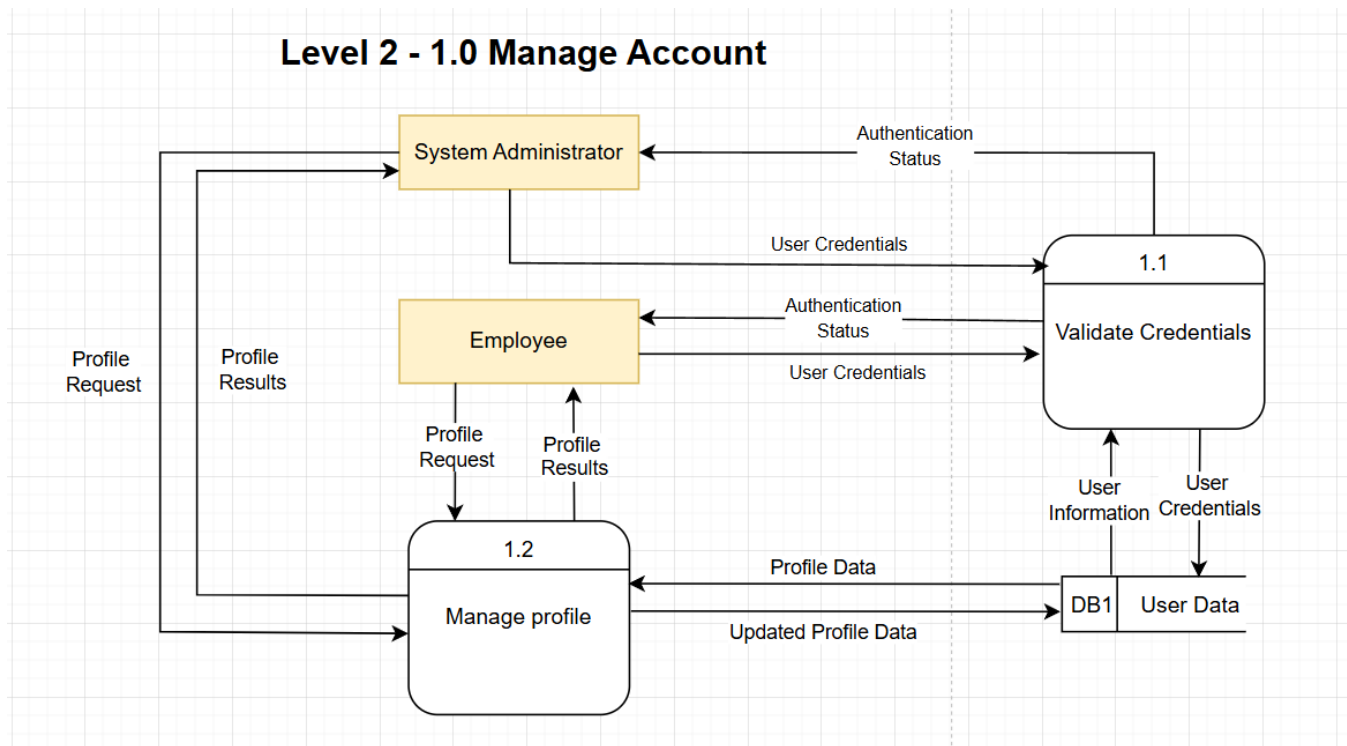


Level 2 – 2.0 Clean Data

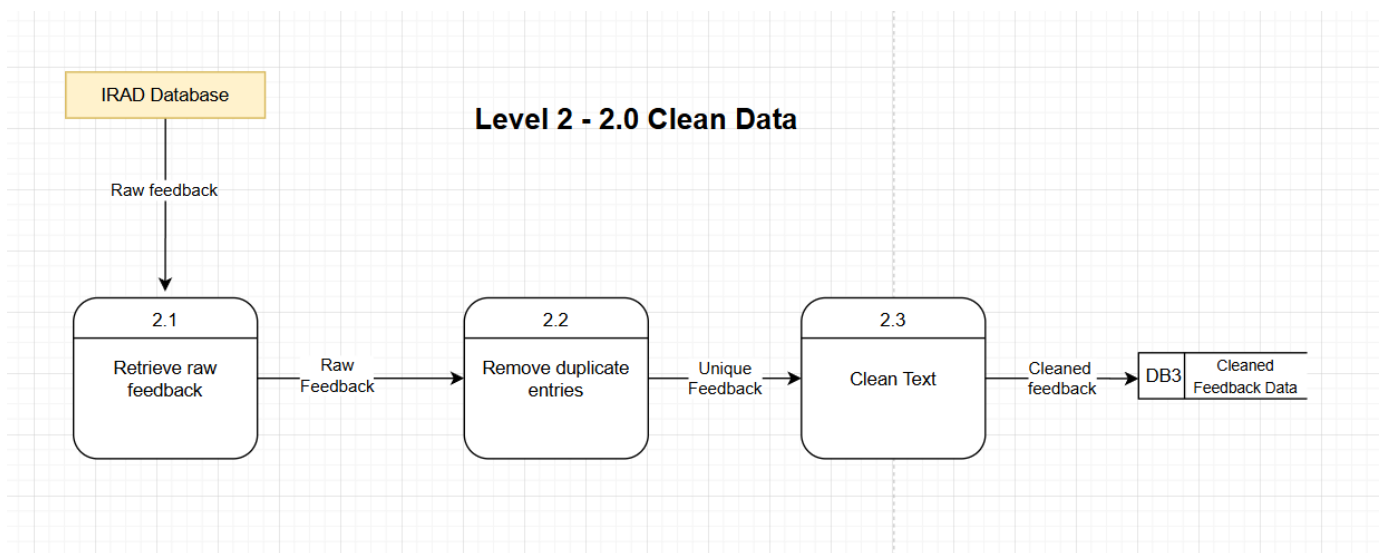


Level 2 – 3.0 Perform Sentiment Analysis

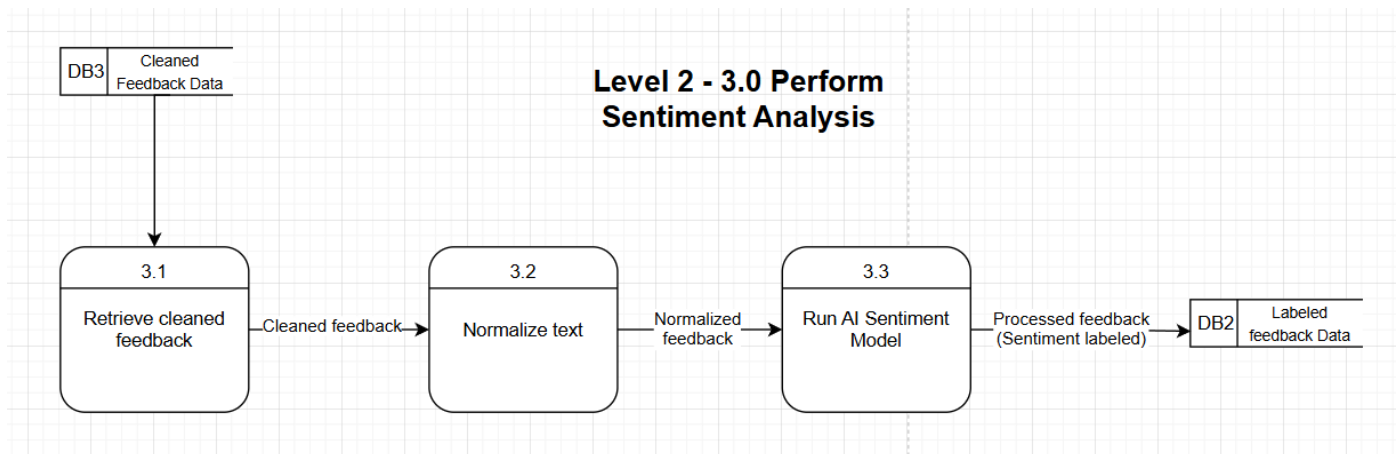


Level 2 – 4.0 Manage Reports

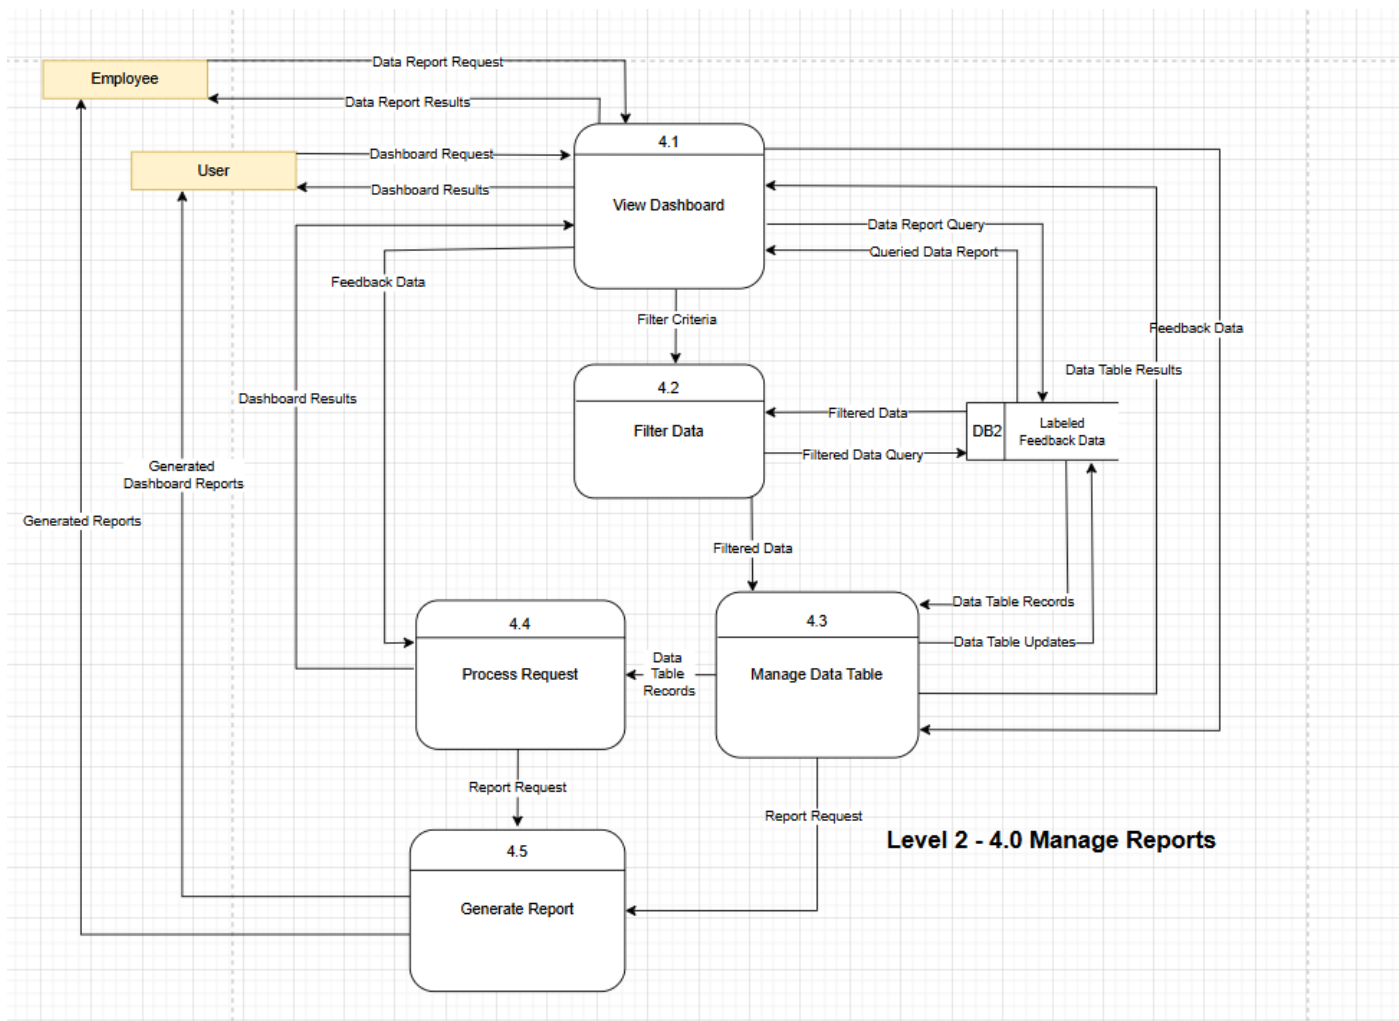

Level 2 – 5.0 Manage User

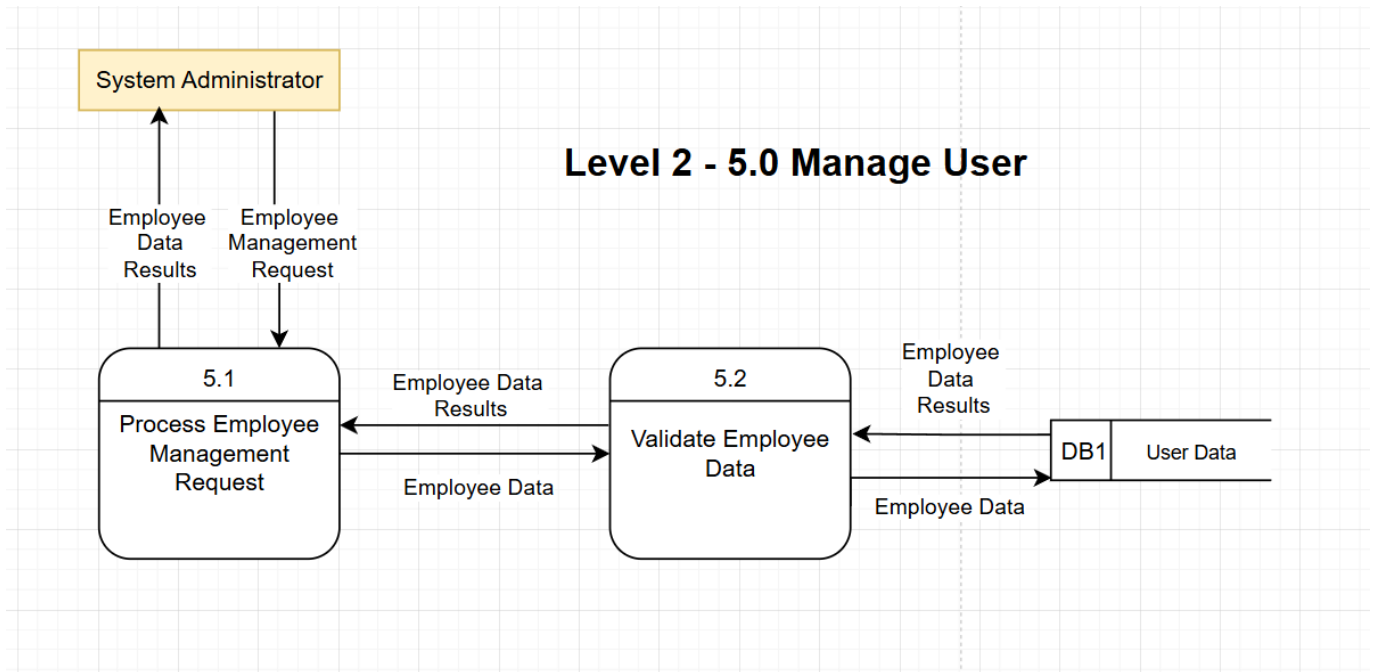

Use Case Diagram

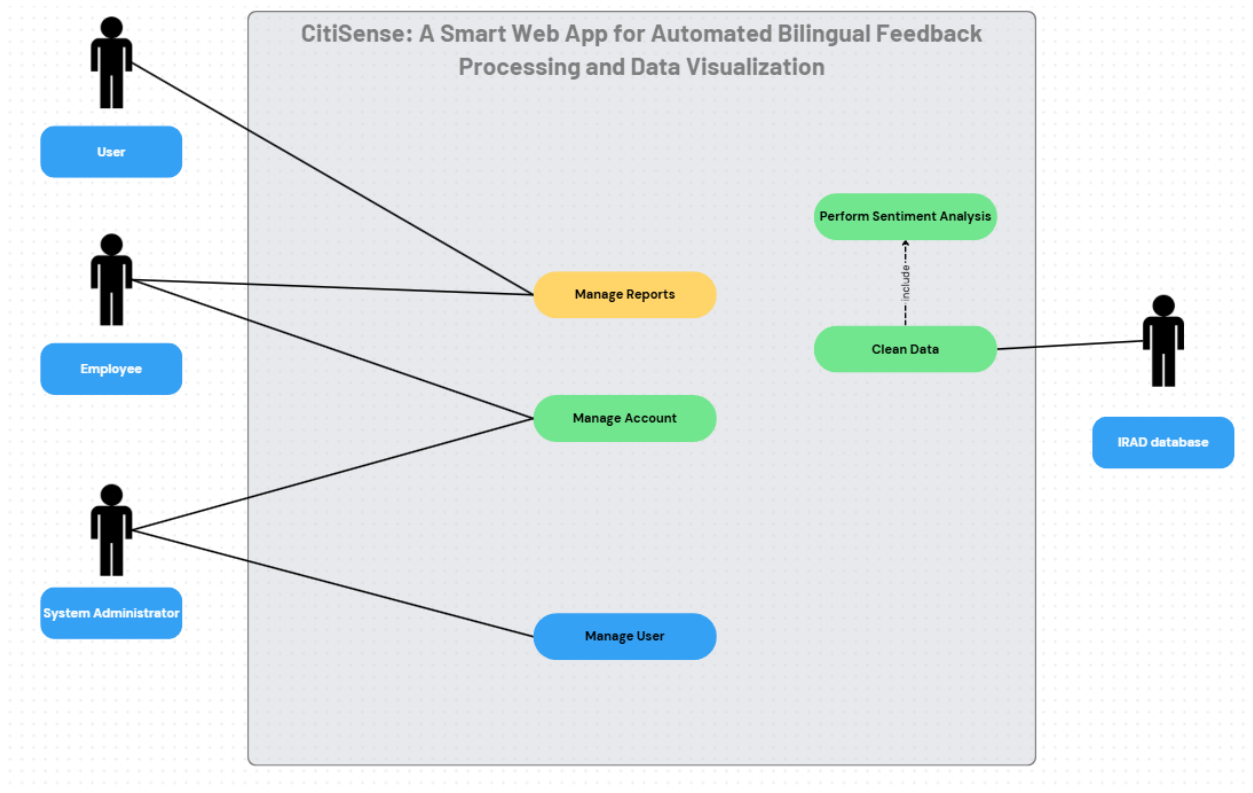


Use Case Fully Dressed


[Fully Dressed Use Case - QuadThink.docx](#)

Activity Diagrams


Activity Diagram for UC-01 (Register)

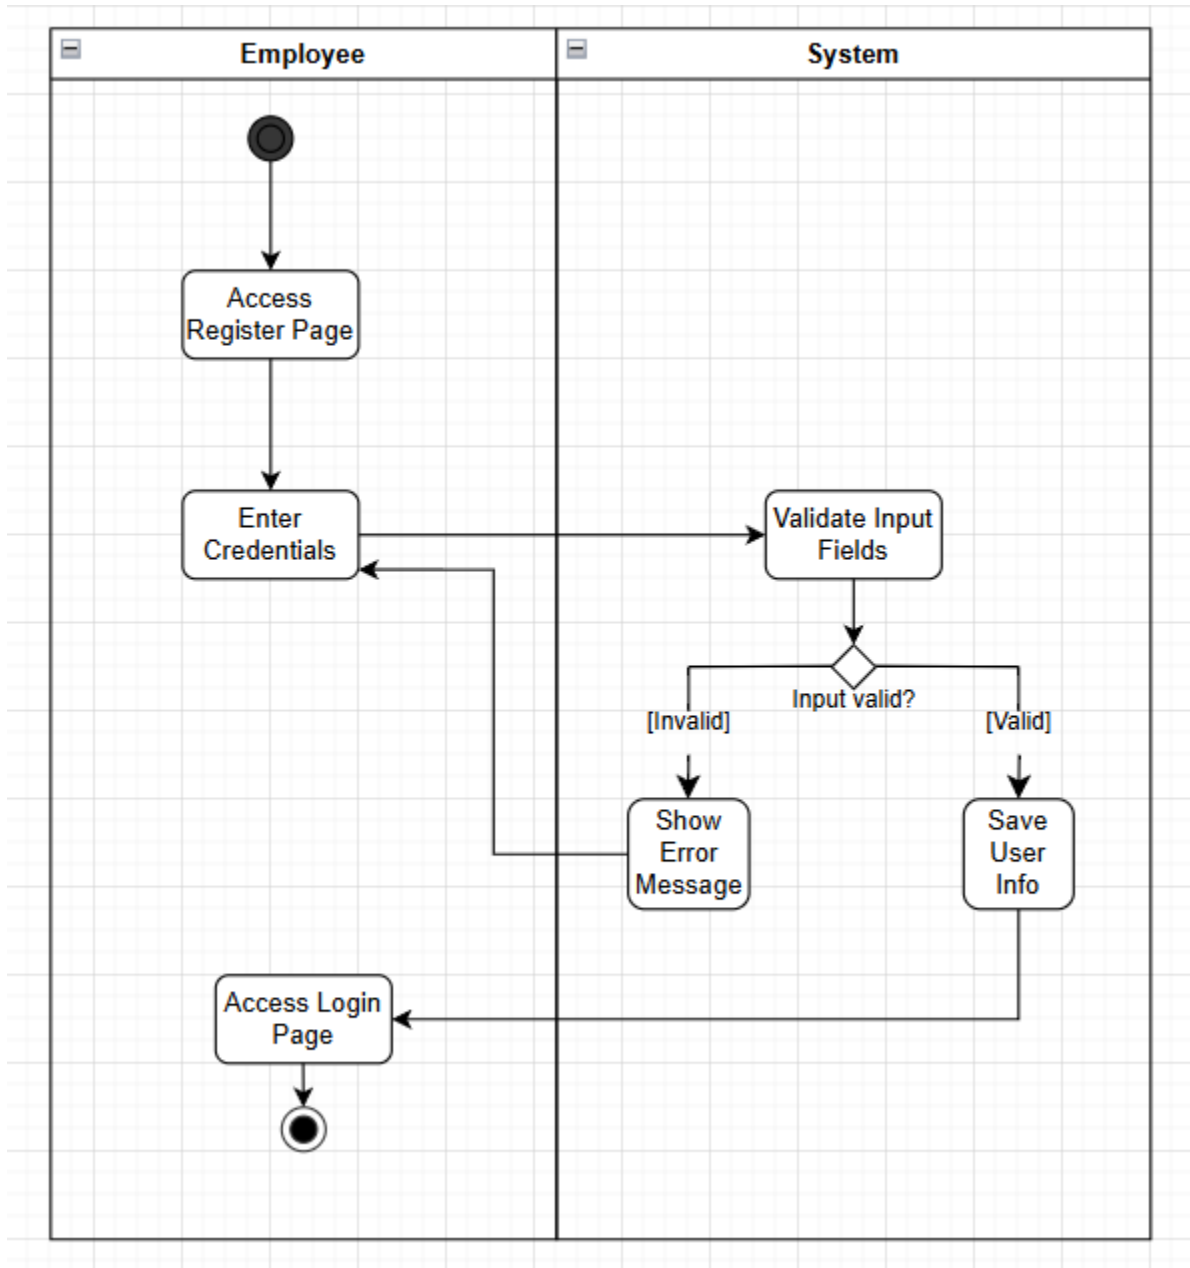


Activity Diagram for UC-02 (Login)

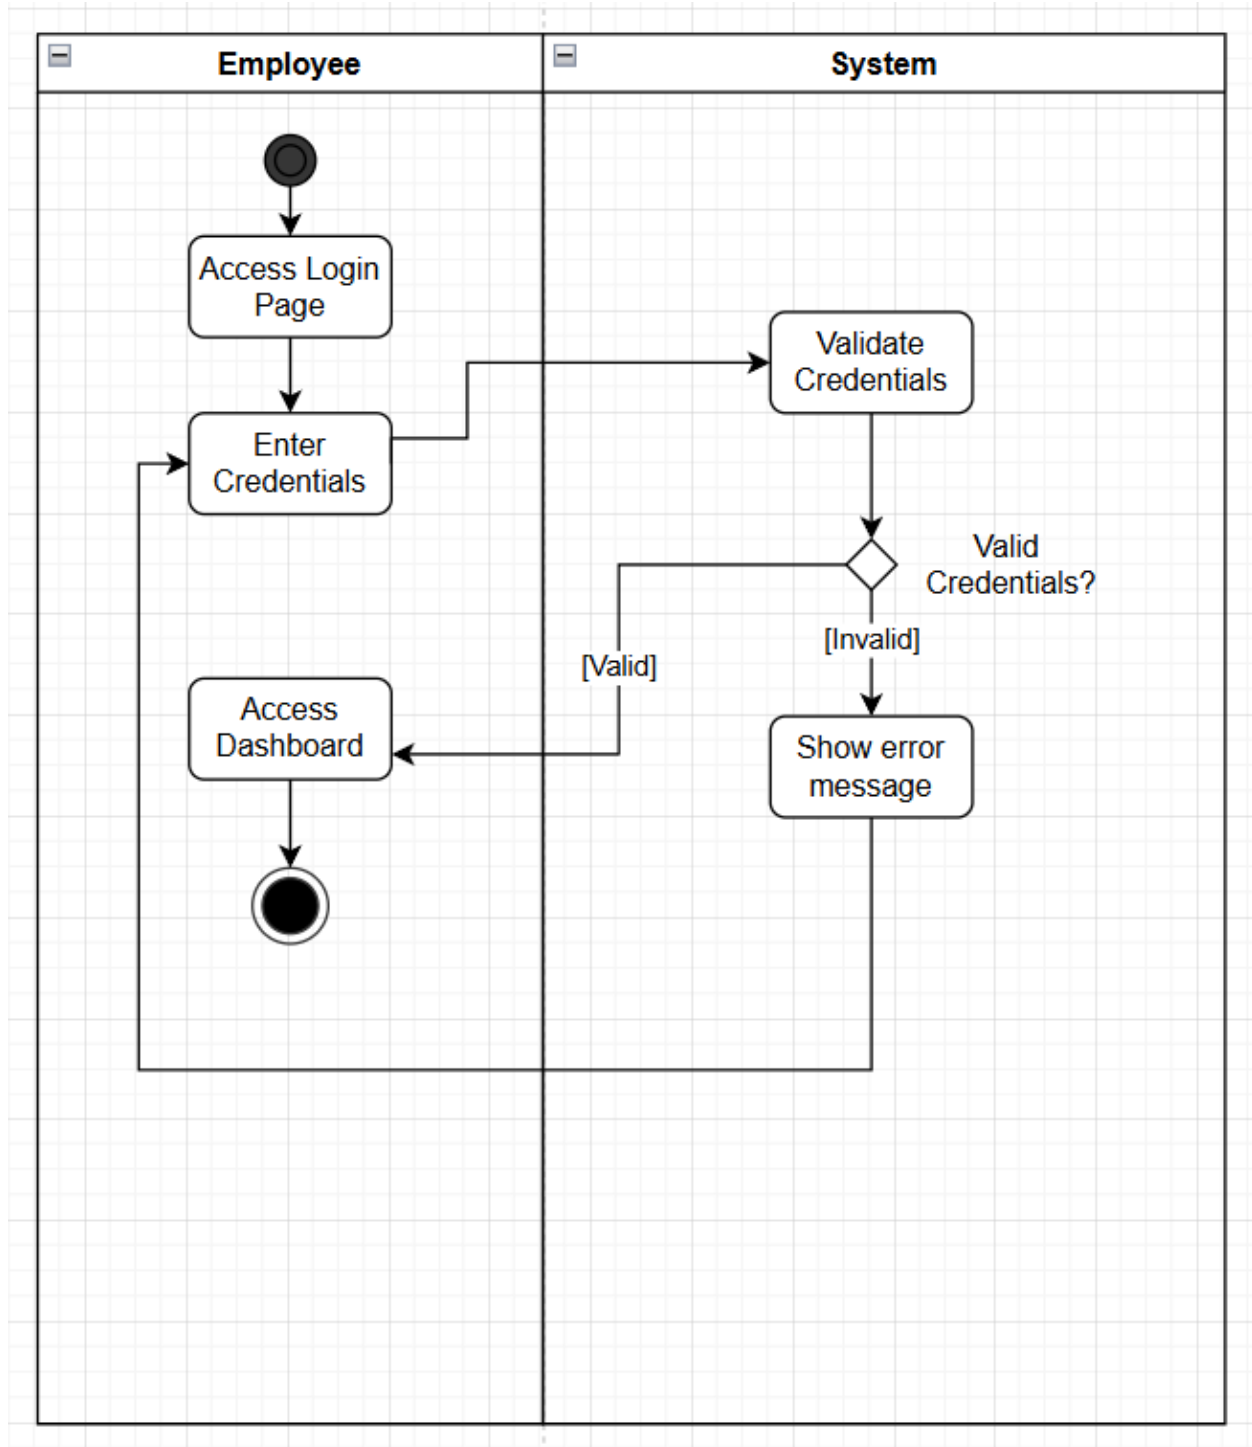


Activity Diagram for UC-03 (Edit User Profile - Employee)

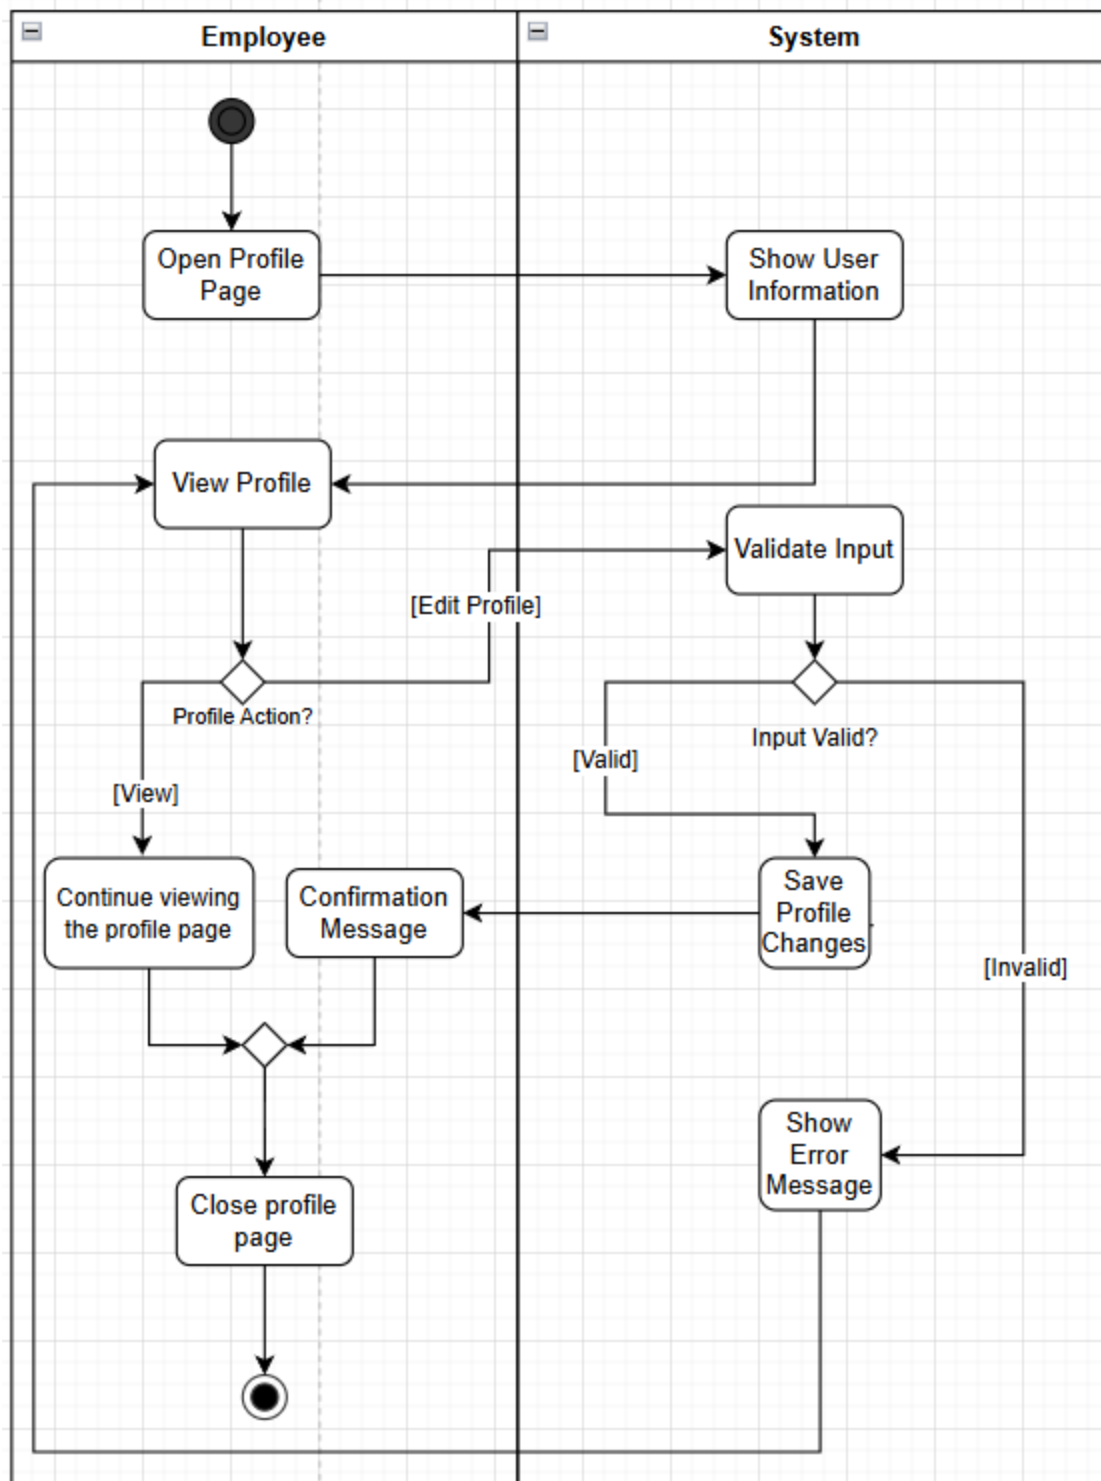


Activity Diagram for UC-04 (View Dashboard - User)

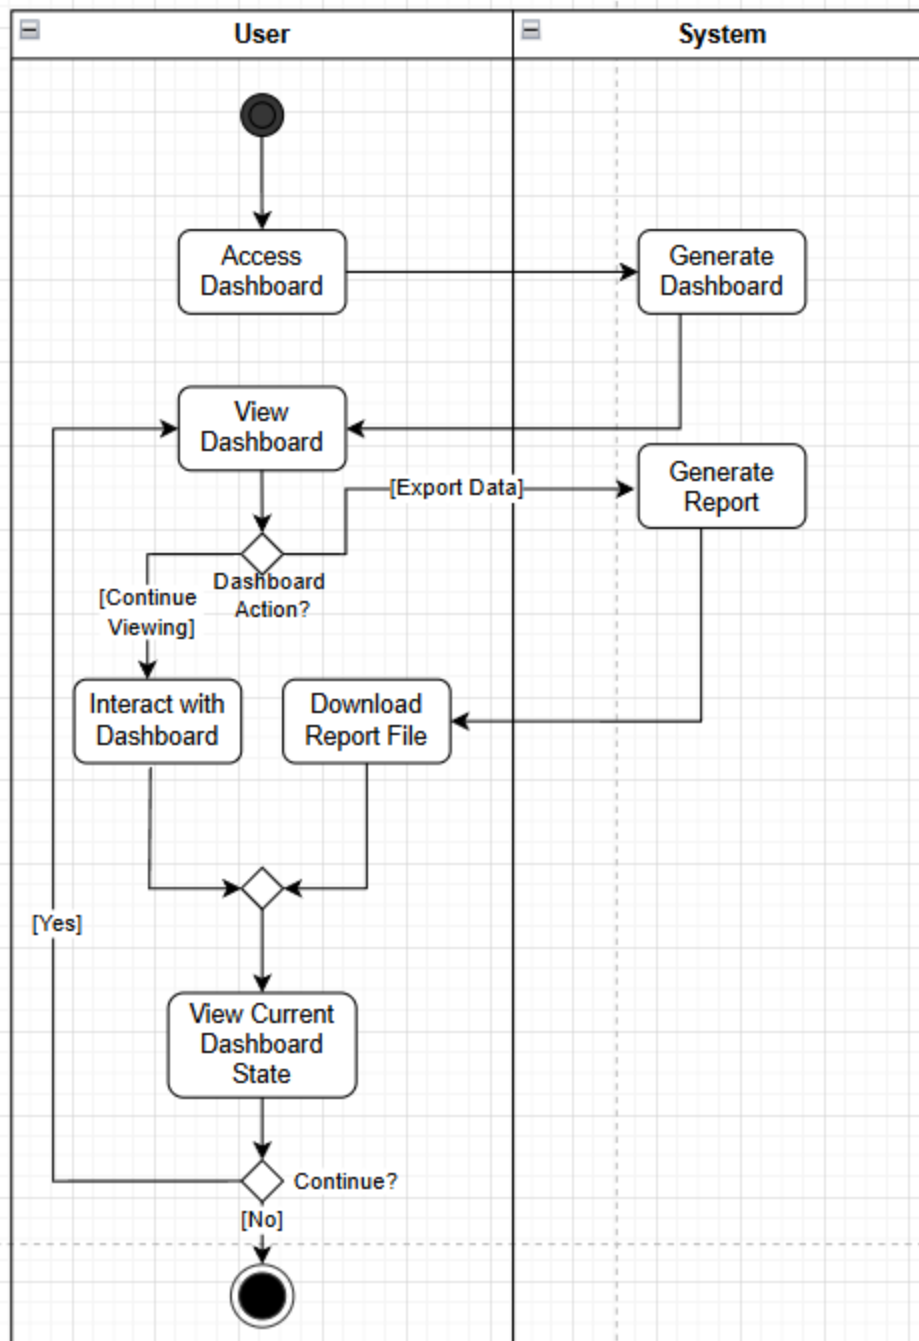


Activity Diagram for UC-05 (Manage Data Table)

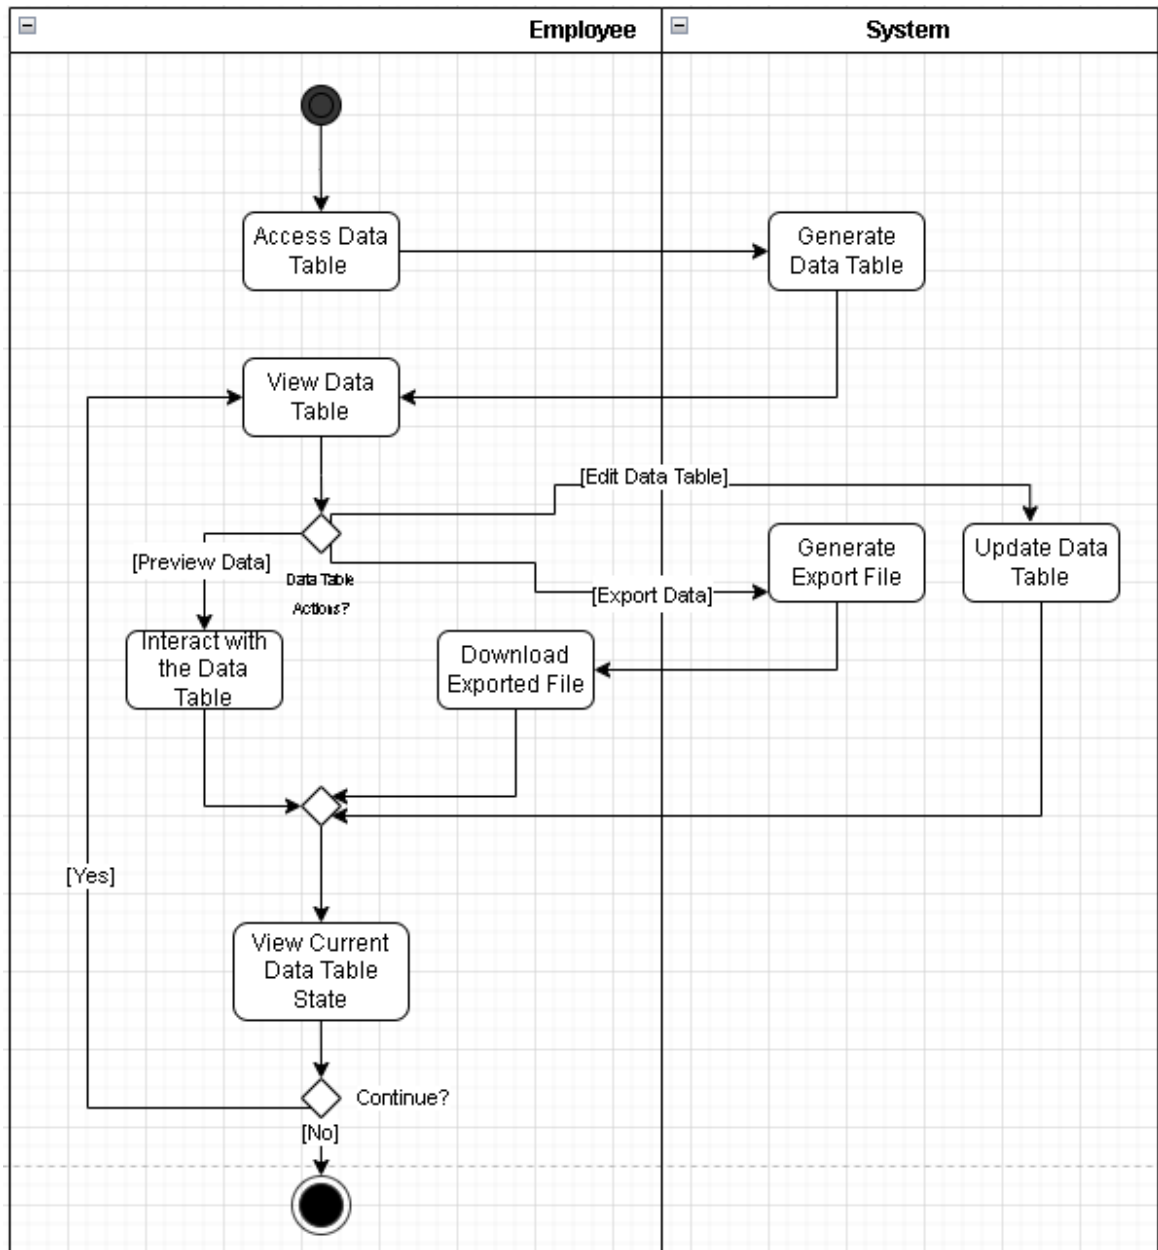


Activity Diagram for UC-06 (Perform Sentiment Analysis)

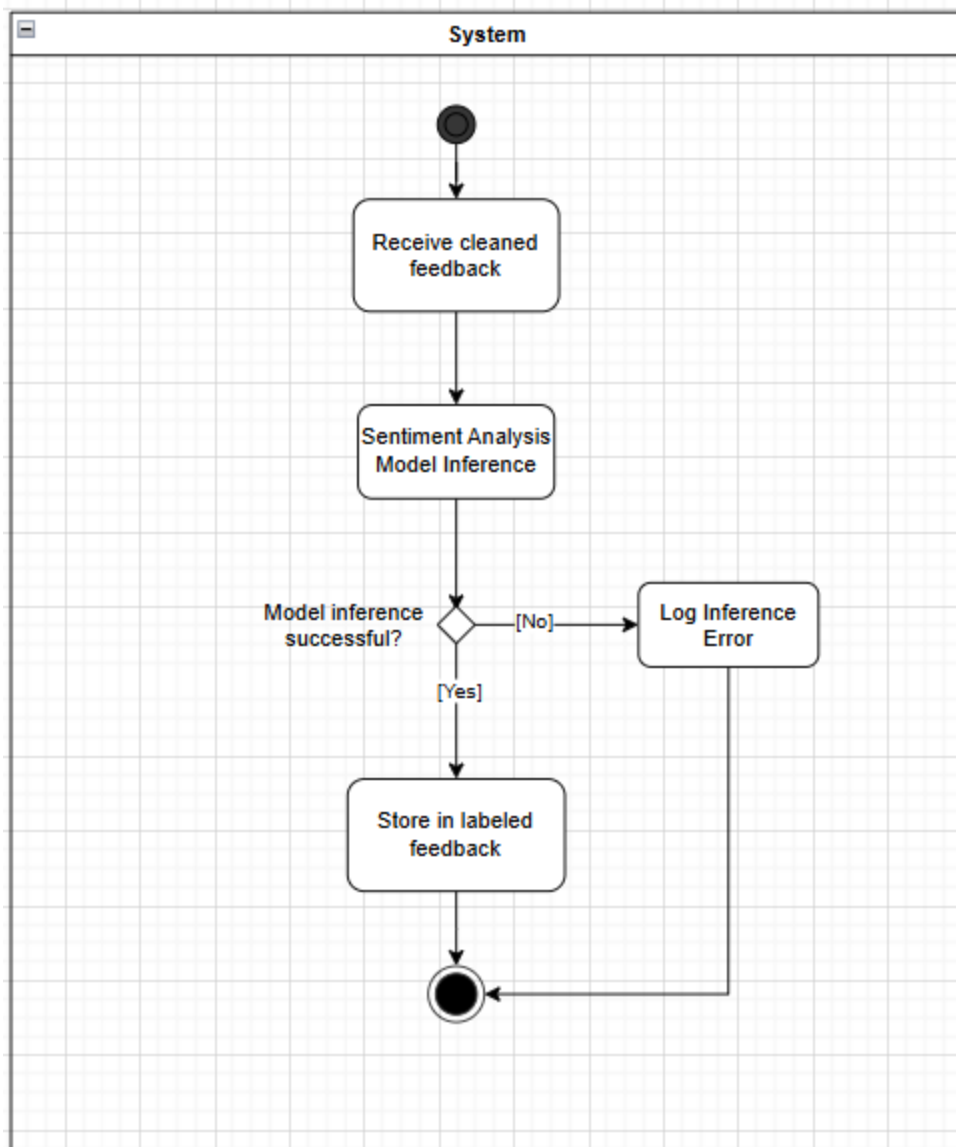


Activity Diagram for UC-07 (Administrator Panel Login)

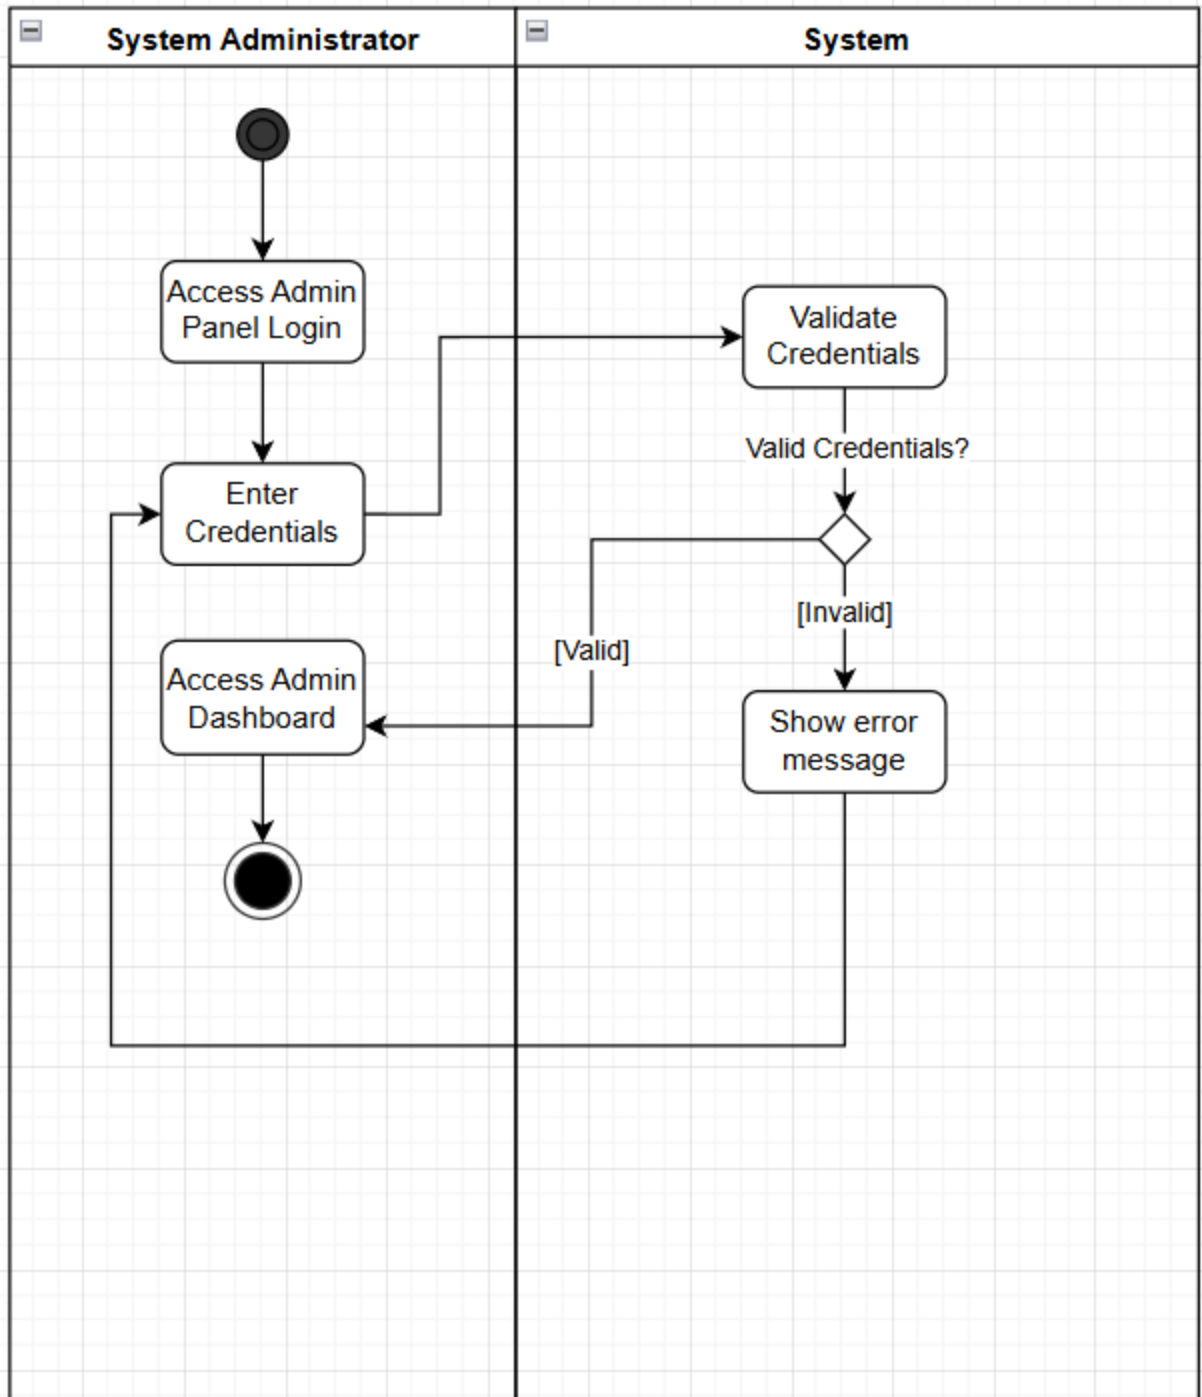


Activity Diagram for UC-08 (Assign Roles)

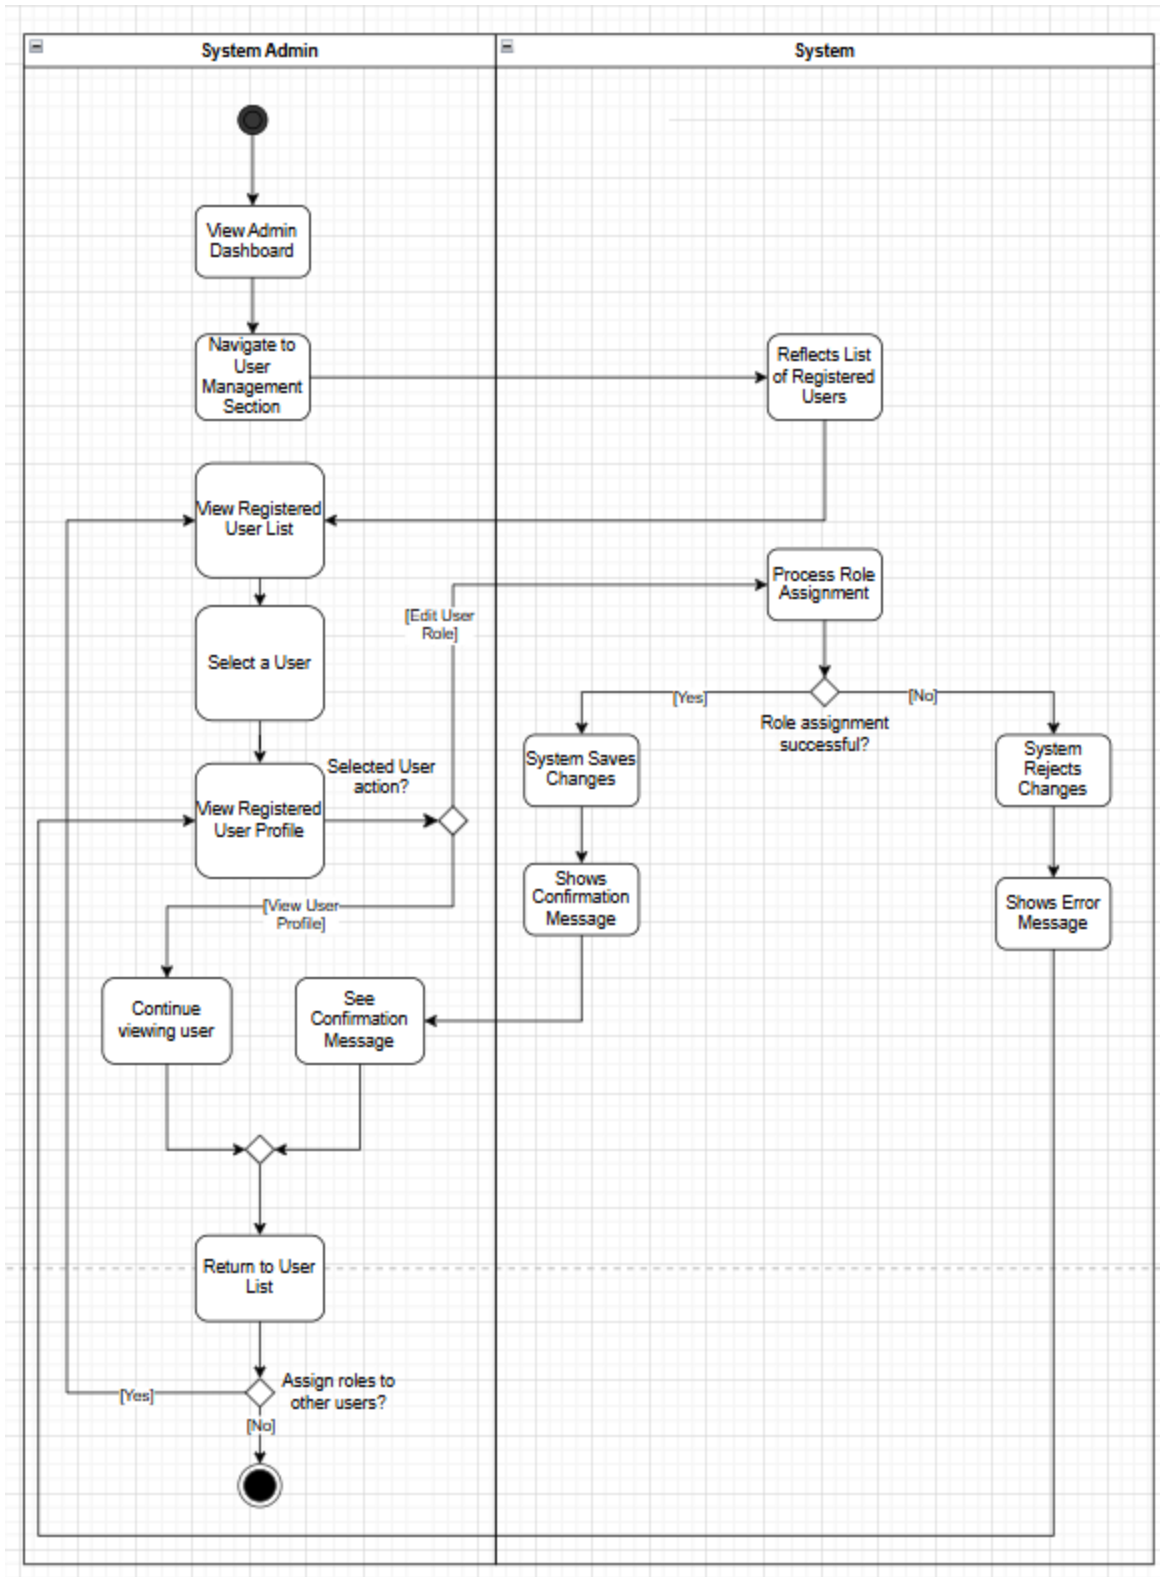


Activity Diagram for UC-09 (Manage User Details)

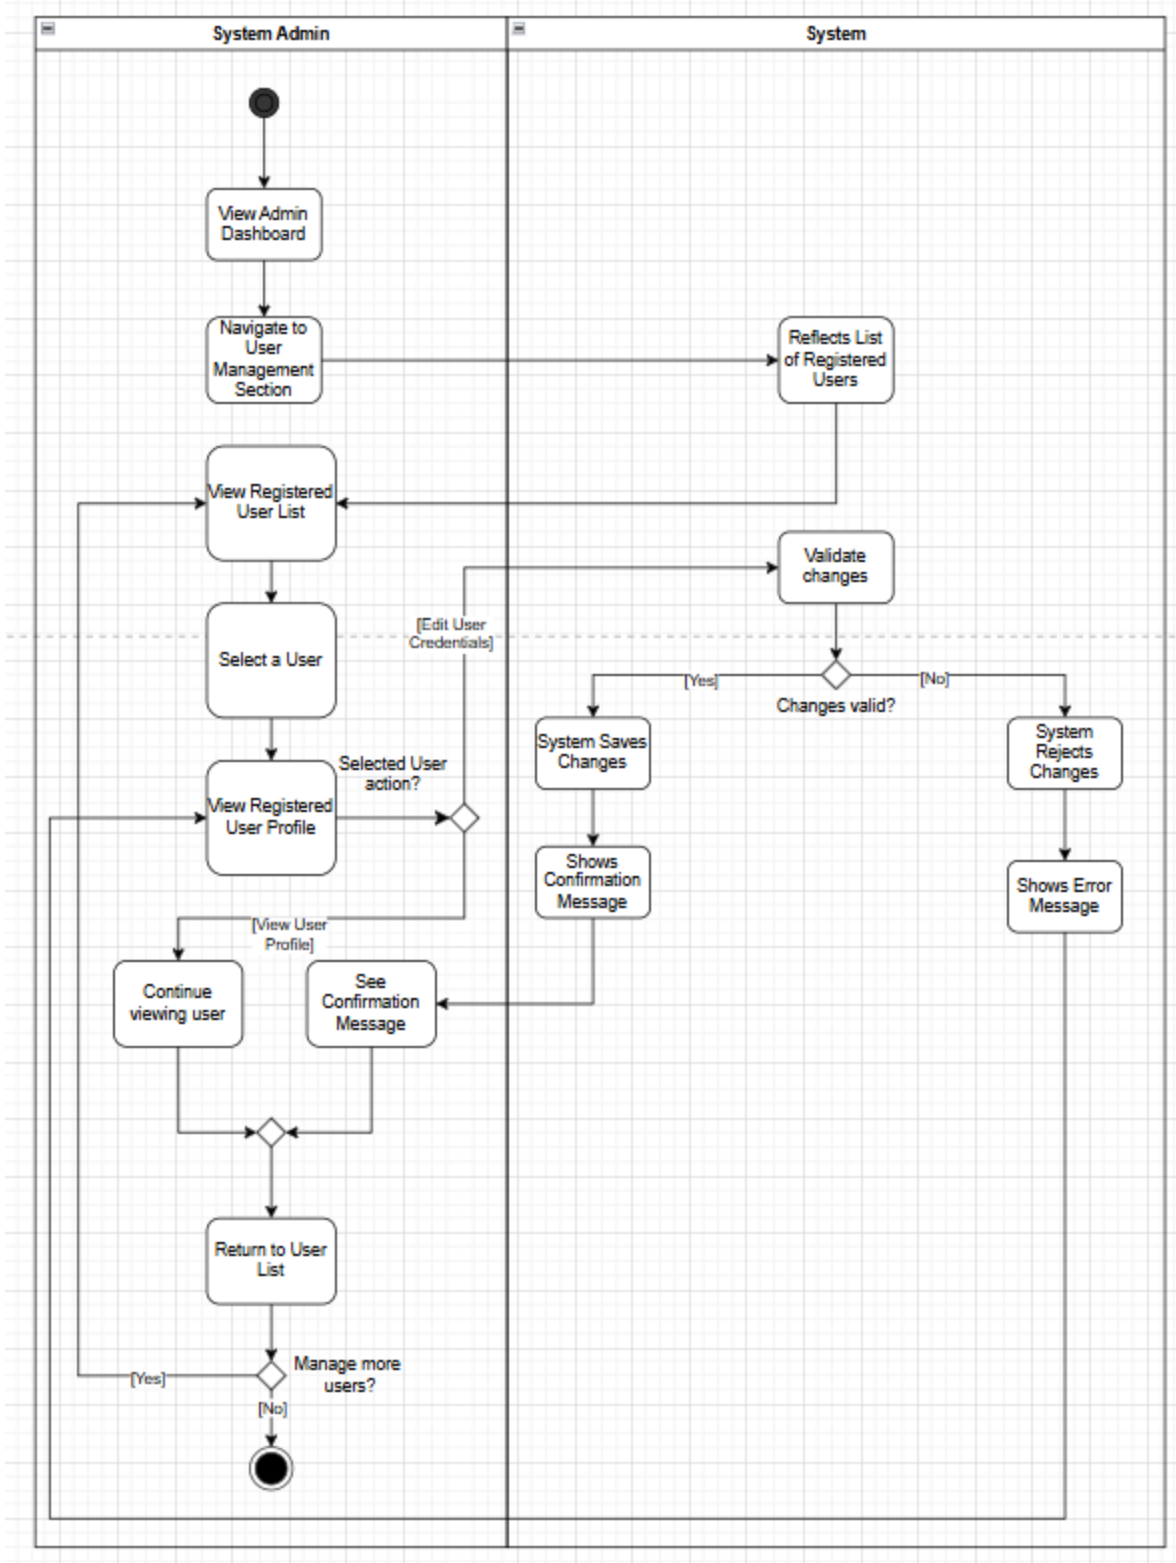


Activity Diagram for UC-13 (Clean Data)

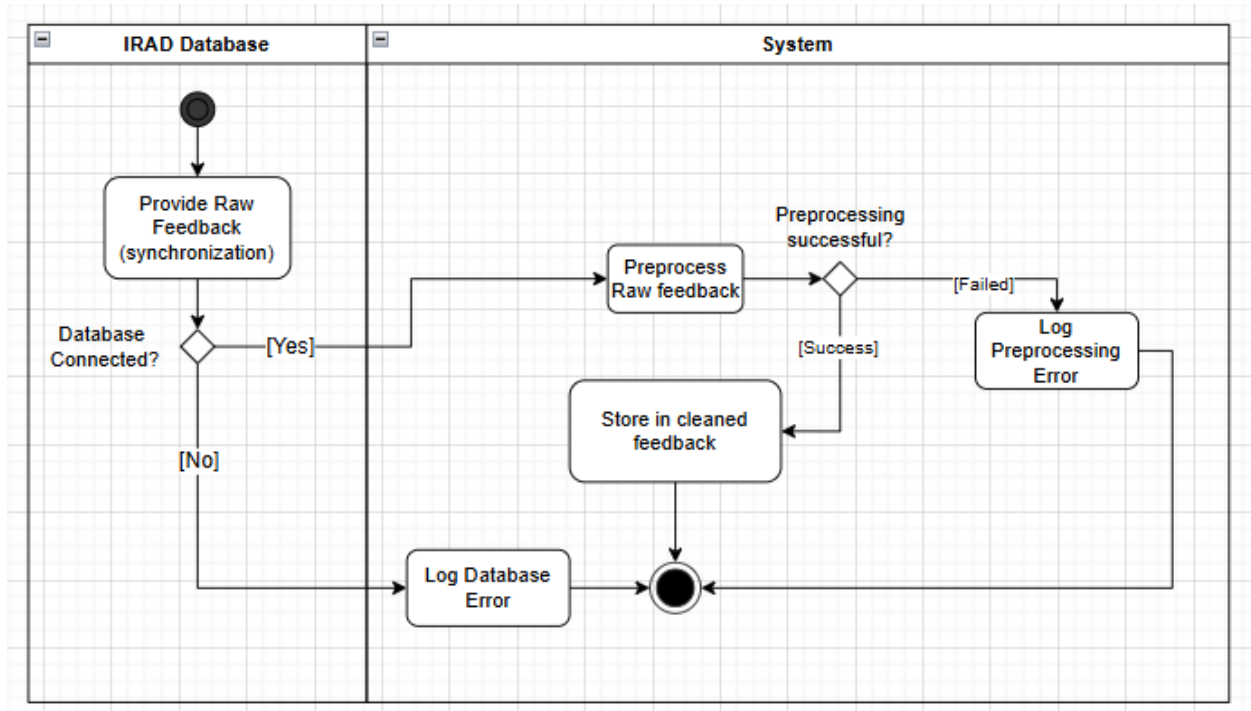

Activity Diagram for UC-14 (View Dashboard – Employee)

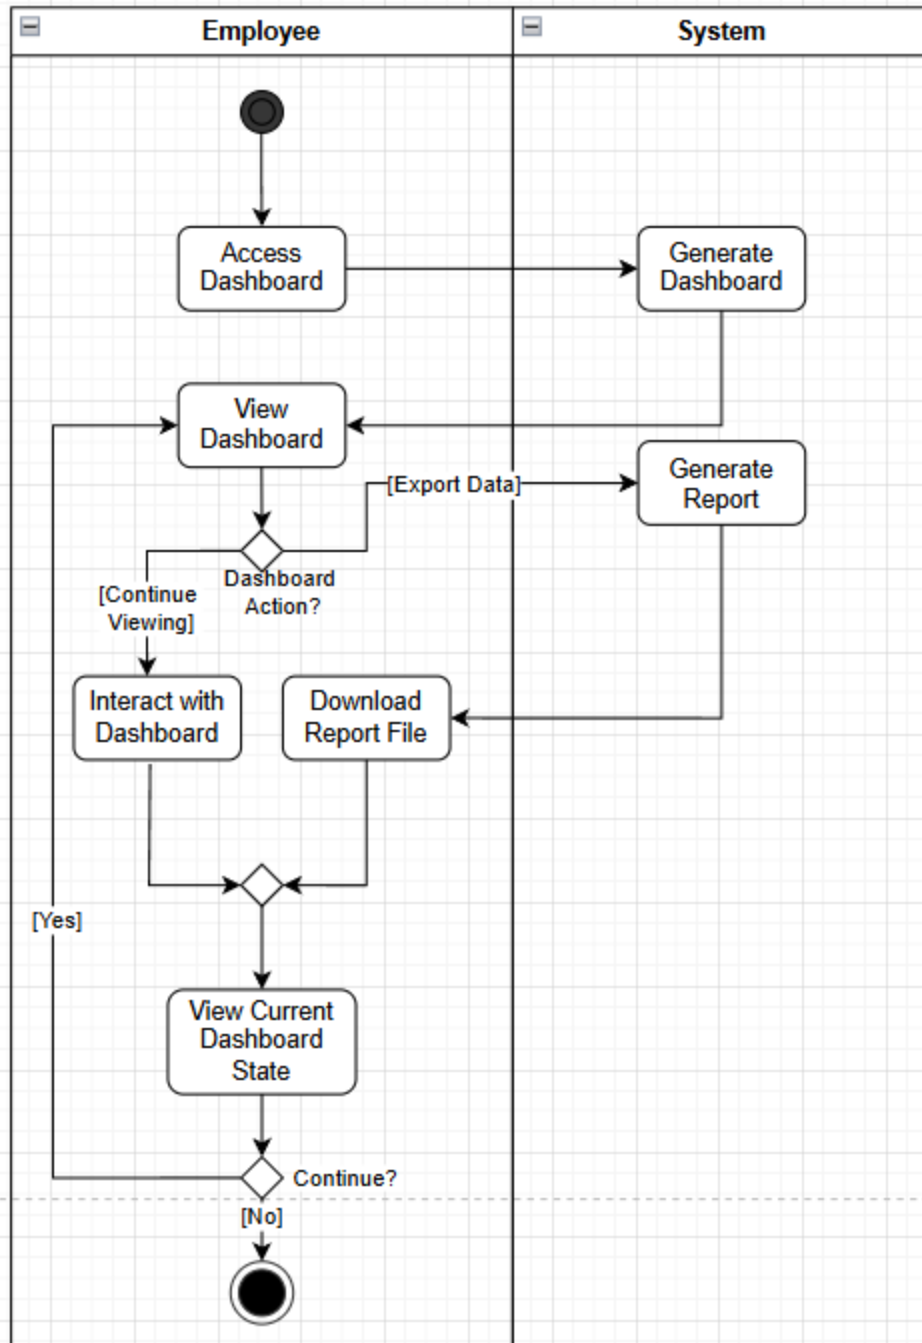


Activity Diagram for UC-15 (Edit User Profile – System Administrator)

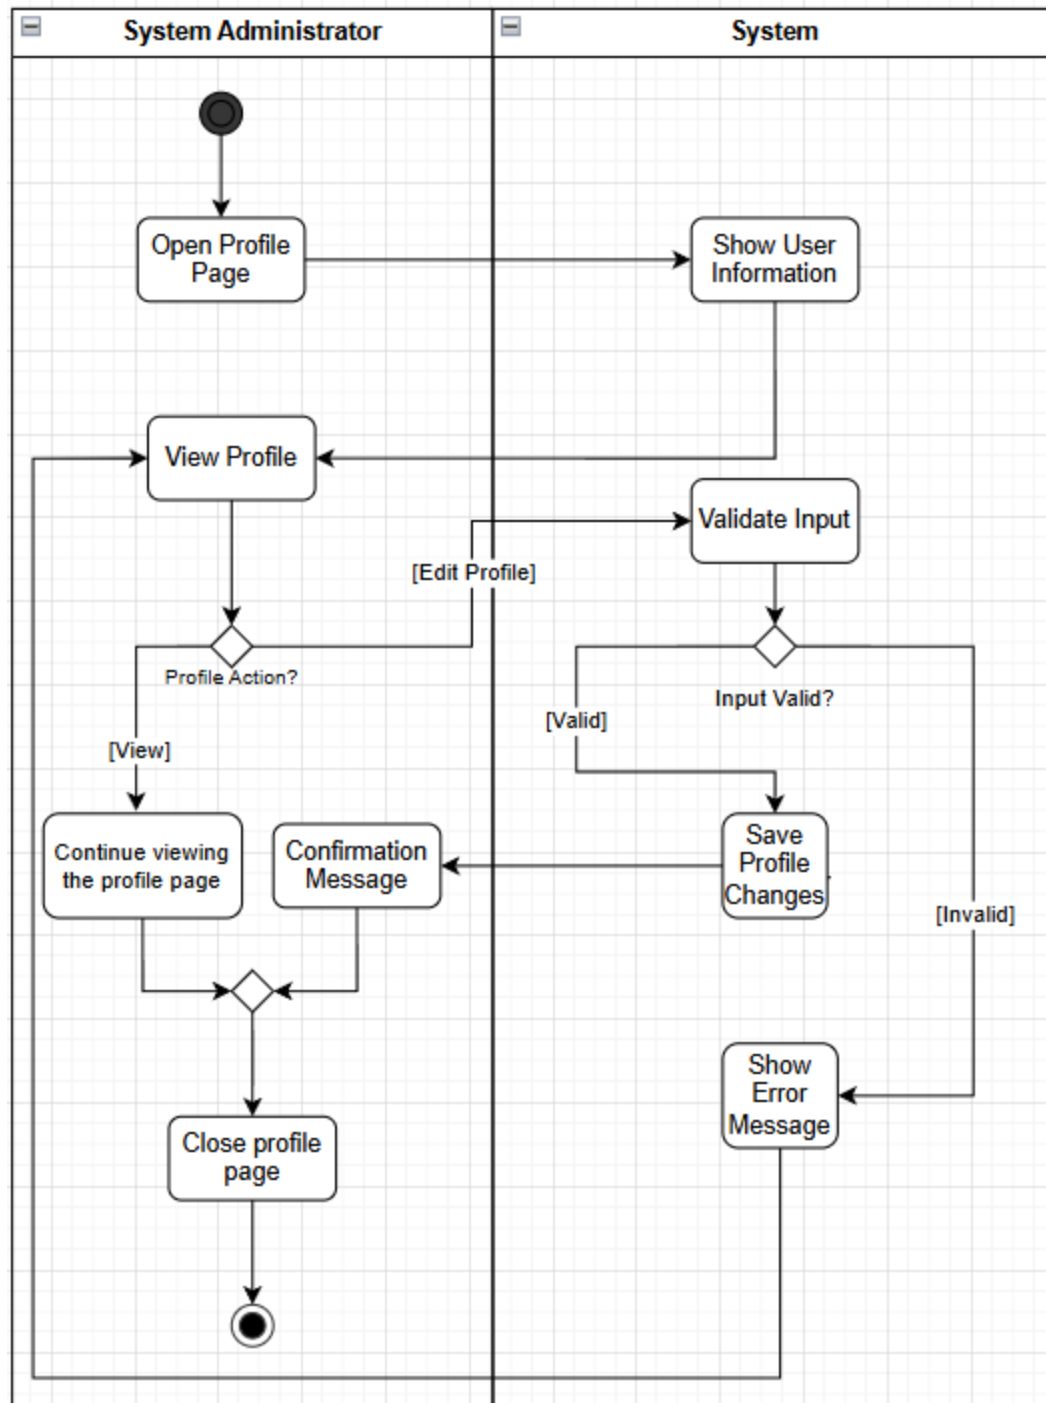

Updated Test Cases

- [QuadThink_TestCaseTables.xlsx](#)

Entity Relationship Diagram



Technology Stack


- Frontend Framework
 - **React**: Connects with the backend via APIs to display sentiment results.
- Backend Framework
 - **Django**: Handles data processing, sentiment model integration, and API services
- Realtime Cloud database
 - **MySQL**: Stores and manages all user, feedback, and sentiment data.
- Frontend/ Backend communication
 - **RESTful API**: Enables real-time communication between React and Django.

Cloud Hosted Prototype

Prototype Link: <https://fork-dost-citi-sense.vercel.app/>

- Credentials:
 - Username: user@example.com
 - Password: password123

Vercel Dashboard

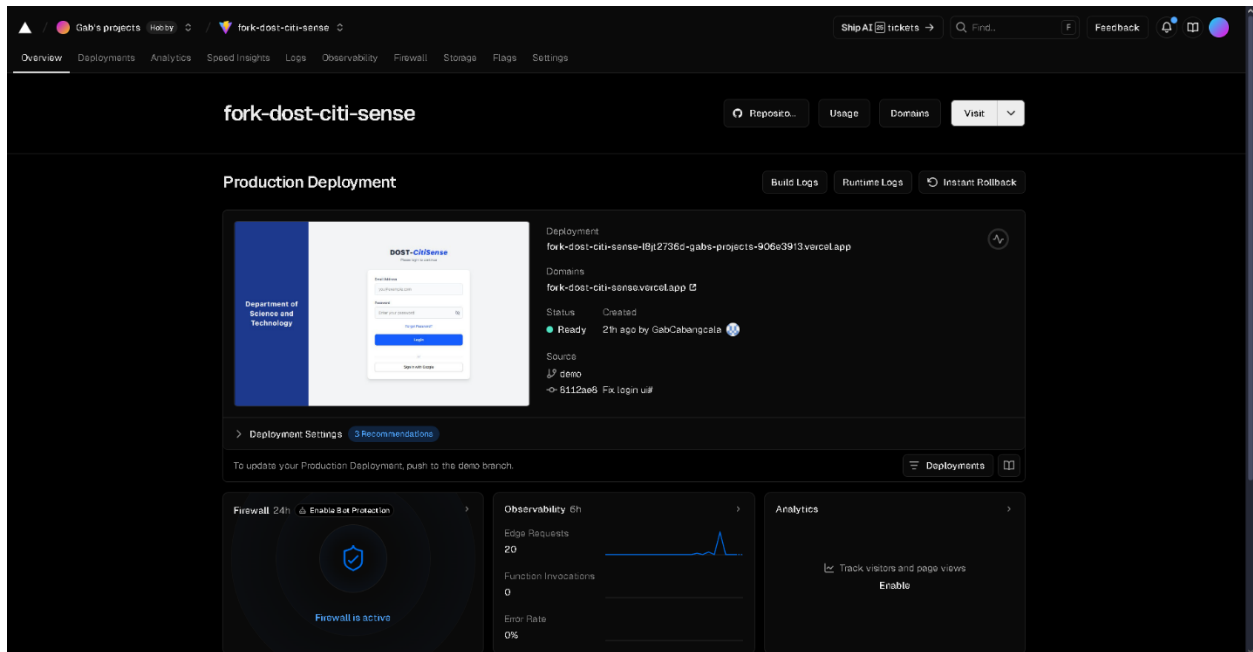

Links


Github APC-SoCIT project repository URL Link: https://github.com/APC-SoCIT/APC_2025_2026_T1_MI232_G07-DOST-CitiSense

Openproject Team Site URL Link: [Overview](#) | [APC_2025_2026_T1_MI232_G07_QuadThinkCitiSense DOST: Sentiment Analysis System](#) | [OpenProject](#)

Sprint 1 Ceremonies

Sprint Planning [\[Meeting Link\]](#)


- Product Backlog

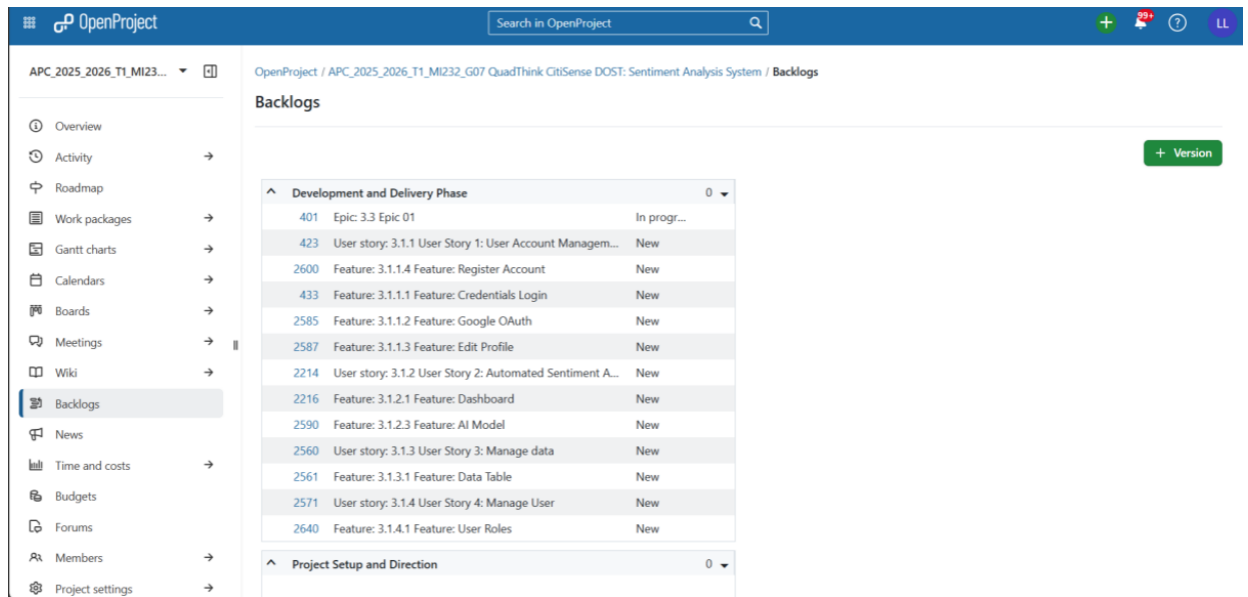

The screenshot shows the OpenProject interface with the 'Backlogs' view selected. The left sidebar contains a navigation menu with options like Overview, Activity, Roadmap, Work packages, Gantt charts, Calendars, Boards, Meetings, Wiki, Backlogs (selected), News, Time and costs, Budgets, Forums, Members, and Project settings. The main area displays the 'Backlogs' for the project 'APC_2025_2026_T1_Mi232_G07 QuadThink CitiSense DOST: Sentiment Analysis System'. It shows two backlog sections: 'Development and Delivery Phase' and 'Project Setup and Direction'. The 'Development and Delivery Phase' backlog contains 14 items, including Epics, User Stories, and Features, with their status (e.g., 'In progress', 'New'). A '+ Version' button is visible in the top right corner of the backlog area.

Item ID	Item Name	Status
401	Epic: 3.3 Epic 01	In progress
423	User story: 3.1.1 User Story 1: User Account Managem...	New
2600	Feature: 3.1.1.4 Feature: Register Account	New
433	Feature: 3.1.1.1 Feature: Credentials Login	New
2585	Feature: 3.1.1.2 Feature: Google OAuth	New
2587	Feature: 3.1.1.3 Feature: Edit Profile	New
2214	User story: 3.1.2 User Story 2: Automated Sentiment A...	New
2216	Feature: 3.1.2.1 Feature: Dashboard	New
2590	Feature: 3.1.2.3 Feature: AI Model	New
2560	User story: 3.1.3 User Story 3: Manage data	New
2561	Feature: 3.1.3.1 Feature: Data Table	New
2571	User story: 3.1.4 User Story 4: Manage User	New
2640	Feature: 3.1.4.1 Feature: User Roles	New

- Sprint Board

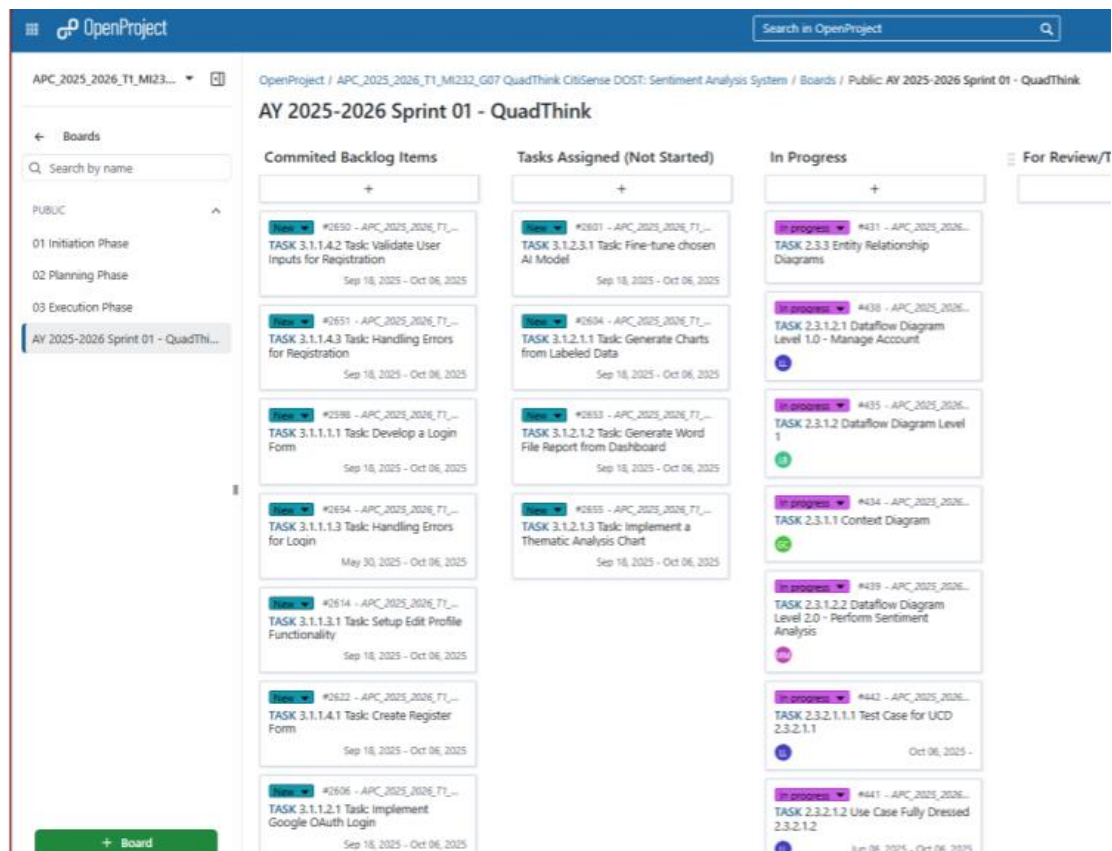

The screenshot shows the OpenProject interface with the 'Sprint Board' view selected. The left sidebar shows the 'Boards' section with a search bar and a list of boards, including 'AY 2025-2026 Sprint 01 - QuadThink' (selected). The main area displays the 'AY 2025-2026 Sprint 01 - QuadThink' board. It is divided into four columns: 'Committed Backlog Items', 'Tasks Assigned (Not Started)', 'In Progress', and 'For Review/T'. Each column contains a list of tasks with their IDs, names, and due dates. The 'In Progress' column also shows task progress bars. A '+ Board' button is visible in the bottom left corner.

Column	Task ID	Task Name	Due Date
Committed Backlog Items	#0630	TASK 3.1.1.4.2 Task: Validate User Inputs for Registration	Sep 18, 2025 - Oct 06, 2025
	#0651	TASK 3.1.1.4.3 Task: Handling Errors for Registration	Sep 18, 2025 - Oct 06, 2025
	#0598	TASK 3.1.1.1.1 Task: Develop a Login Form	Sep 18, 2025 - Oct 06, 2025
	#0654	TASK 3.1.1.1.3 Task: Handling Errors for Login	May 30, 2025 - Oct 06, 2025
	#0614	TASK 3.1.1.3.1 Task: Setup Edit Profile Functionality	Sep 18, 2025 - Oct 06, 2025
	#0622	TASK 3.1.1.4.1 Task: Create Register Form	Sep 18, 2025 - Oct 06, 2025
Tasks Assigned (Not Started)	#0601	TASK 3.1.2.3.1 Task: Fine-tune chosen AI Model	Sep 18, 2025 - Oct 06, 2025
	#0604	TASK 3.1.2.1.1 Task: Generate Charts from Labeled Data	Sep 18, 2025 - Oct 06, 2025
In Progress	#0633	TASK 3.1.2.1.2 Task: Generate Word File Report from Dashboard	Sep 18, 2025 - Oct 06, 2025
	#0655	TASK 3.1.2.1.3 Task: Implement a Thematic Analysis Chart	Sep 18, 2025 - Oct 06, 2025
For Review/T	#431	TASK 2.3.3 Entity Relationship Diagrams	
	#438	TASK 2.3.1.2.1 Dataflow Diagram Level 1.0 - Manage Account	
	#435	TASK 2.3.1.2 Dataflow Diagram Level 1	
	#434	TASK 2.3.1.1 Context Diagram	
	#439	TASK 2.3.1.2.2 Dataflow Diagram Level 2.0 - Perform Sentiment Analysis	
	#442	TASK 2.3.2.1.1.1 Test Case for UCD 2.3.2.1.1	Oct 06, 2025 -
	#441	TASK 2.3.2.1.2 Use Case Fully Dressed 2.3.2.1.2	Jun 06, 2025 - Oct 06, 2025


Backlog Refinement [Meeting Link](#)

- Product Backlog


Development and Delivery Phase			0
2216	Feature: 3.1.2.1 Feature: Dashboard	In progr...	
2590	Feature: 3.1.2.3 Feature: AI Model	In progr...	
2585	Feature: 3.1.1.2 Feature: Google OAuth	New	
2600	Feature: 3.1.1.4 Feature: Register Account	New	
433	Feature: 3.1.1.1 Feature: Credentials Login	New	
2640	Feature: 3.1.4.1 Feature: User Roles	New	
2587	Feature: 3.1.1.3 Feature: Edit Profile	New	
2561	Feature: 3.1.3.1 Feature: Data Table	New	

Sprint Review [Meeting Link](#)

- Product Demo

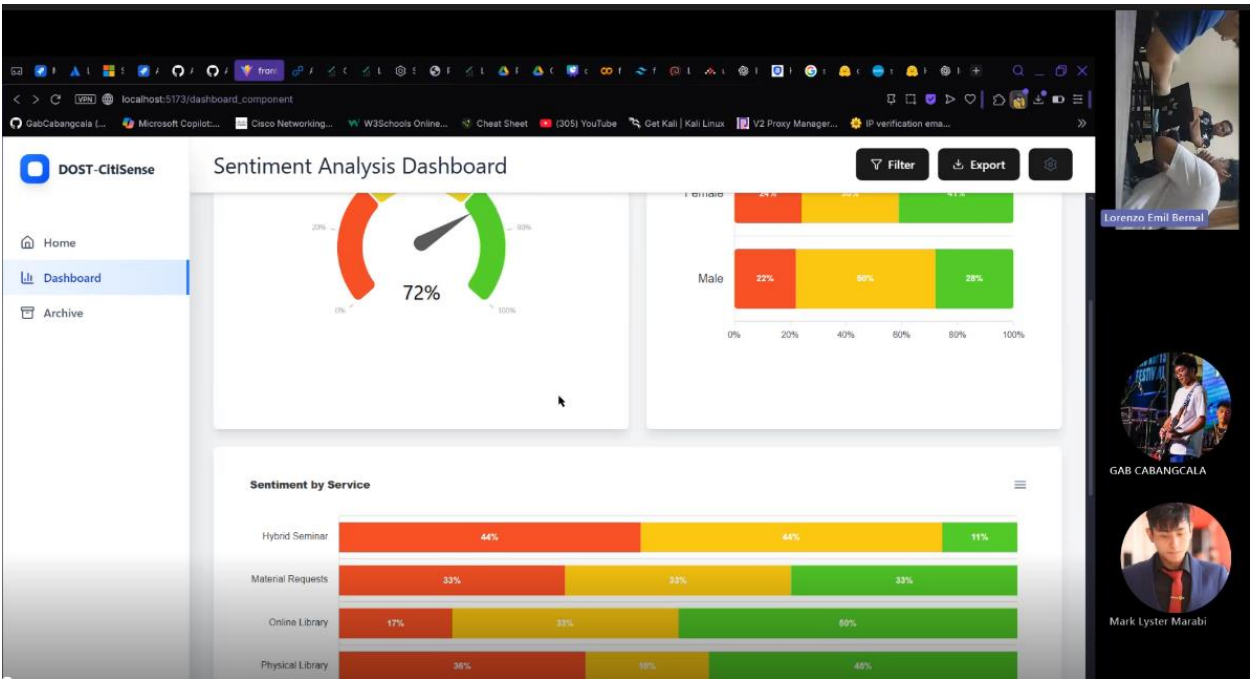


Sprint Board

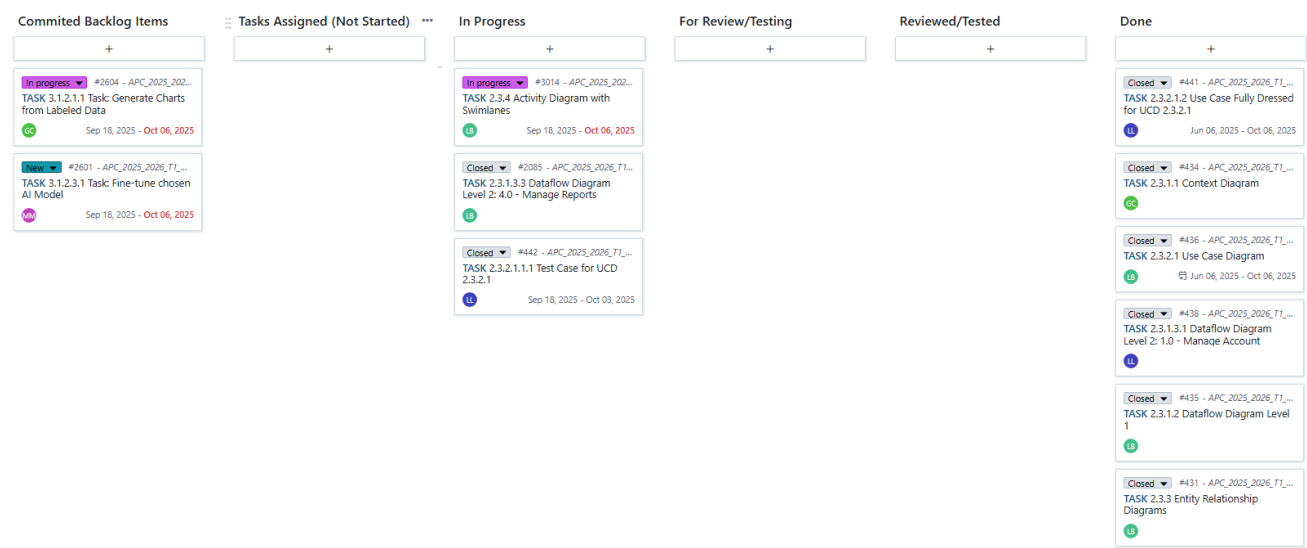


Sprint retrospective [Meeting Link](#)

- Glad, Sad, Mad, Items

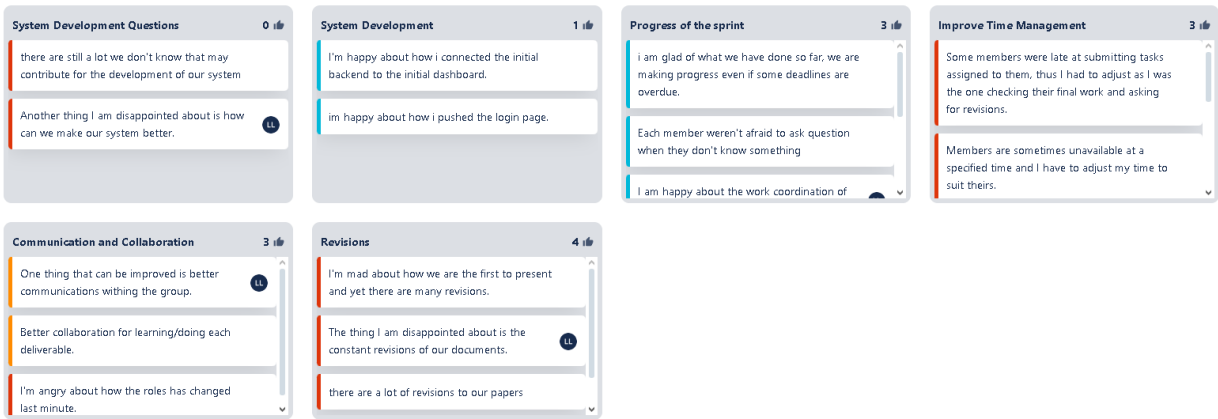

Action Items

Action list



- OpenProject Work Packages

▼ 3.4 Sprint Retrospective	SUMMARY TASK	New	LB	Lorenzo Bernal
▼ 3.4.1 Sprint 01: Retrospective	TASK	New	LB	Lorenzo Bernal
3.4.1.1 Have agreed upon time to meet, and schedule meetings for scrum artifacts and/or meetings for deliv...	SUB TASK	In progress	LL	Luis Lazaro
3.4.1.2 Prioritize PBL deliverables tasks first, and don't do them at the end of the day.	SUB TASK	Closed	GC	Gabrielle Cabangcala
3.4.1.3 Utilize research tools and resources to produce quality work, to lessen the need for multiple revisions.	SUB TASK	In progress	LB	Lorenzo Bernal
3.4.1.4 Prioritize each work and then consult with our superiors after completion.	SUB TASK	In progress	MM	Mark Marabi

OpenProject Daily Scrum Outputs

OpenProject Daily Scrum Reports for Sprint 1 Week 1

Daily Scrum Report Day 01

- **OpenProject:** [Sprint 1 Week 1 Day 01 Daily Scrum Meeting Individual Updated Report](#)
- Scrum Report Video recording link from Group channel: [|Link|](#)

LB RE: Sprint 1 Week 1 Day 01 Daily Scrum Meeting Individual Updated Report - Added by Lorenzo Bernal 23 days ago

1. What did I do yesterday? - I moved our project's private repository to the APC org repository
2. What will I do today? - I will check the members' updated diagrams (e.g., UCD, DFD) after they have done it today.
3. Anything blocking my progress? - None, as of now.

LL RE: Sprint 1 Week 1 Day 01 Daily Scrum Meeting Individual Updated Report - Added by Luis Lazaro 22 days ago

1. What did I do yesterday? - Did Minutes of the Meeting for that day.
2. What will I do today? - Will start to revise fully dressed use case, watch and learn about front end coding.
3. Anything blocking I progress? - None.

GC RE: Sprint 1 Week 1 Day 01 Daily Scrum Meeting Individual Updated Report - Added by Gabrielle Cabangcala 22 days ago

1. What did I do yesterday? - Compiled youtube tutorials on react
2. What will I do today? - Watch the tutorials
3. Anything blocking I progress? - Errands

Daily Scrum Report Day 02

- **OpenProject:** [Sprint 1 Week 1 Day 02 Daily Scrum Meeting Individual Updated Report](#)
- Scrum Report Video recording link from Group channel: [|Link|](#)

LB RE: Sprint 1 Week 1 Day 02 Daily Scrum Meeting Individual Updated Report - Added by Lorenzo Bernal 22 days ago

1. What did I do yesterday? - I connected each (cardinality) of the database entities with one another in the ERD, and checking of members' work inside the ERD.
2. What will I do today? - Make some final changes in the ERD (e.g., put an external symbol in the IRAD database, and add relationships in the connection of each database entity).
3. Anything blocking I progress? - None, as of now.

MM RE: Sprint 1 Week 1 Day 02 Daily Scrum Meeting Individual Updated Report - Added by Mark Marabi 22 days ago

1. What did I do yesterday? Reviewed and Revised the ERD
2. What will I do today?, Install Node.js
3. Anything blocking I progress? As of now None

GC RE: Sprint 1 Week 1 Day 02 Daily Scrum Meeting Individual Updated Report - Added by Gabrielle Cabangcala 22 days ago

1. What did I do yesterday? - Finalized the my part on the ERD
2. What will I do today? - download node.js module
3. Anything blocking I progress? - Errands

LL RE: Sprint 1 Week 1 Day 02 Daily Scrum Meeting Individual Updated Report - Added by Luis Lazaro 22 days ago

1. What did I do yesterday? - ERD and frontend coding in github repository.
2. What will I do today? - Download node.js module.
3. Anything blocking I progress? - None.

OpenProject Daily Scrum Reports for Sprint 1 Week 2

Daily Scrum Report Day 01

- **OpenProject:** [Sprint 1 Week 2 Day 01 Daily Scrum Meeting Individual Updated Report](#)
- Scrum Report Video recording link from Group channel: [|Link|](#)

LB RE: Sprint 1 Week 2 Day 01 Daily Scrum Meeting Individual Updated Report - Added by Lorenzo Bernal 19 days ago

1. What did I do yesterday? - I set up two instances of MySQL databases. One is connected to Django, and the other one is the external database.
2. What will I do today? - I set up GitHub Codespaces; that's where everyone will work on and code in.
3. Anything blocking I progress? - None, as of now

MM RE: Sprint 1 Week 2 Day 01 Daily Scrum Meeting Individual Updated Report - Added by Mark Marabi 19 days ago

1. What did I do yesterday? Did the installation code and ERD
2. What will I do today? set a meeting with the adviser, review the meeting to make the necessary revisions for the ERD
3. Anything blocking I progress? internet connection due to the typhoon

GC RE: Sprint 1 Week 2 Day 01 Daily Scrum Meeting Individual Updated Report - Added by Gabrielle Cabangcala 19 days ago

1. What did I do yesterday? Installation of modules, pillow, faker, django_cleanup
2. What will I do today? setup of tailwindcss on vscode
3. Anything blocking I progress? errands

LL RE: Sprint 1 Week 2 Day 01 Daily Scrum Meeting Individual Updated Report - Added by Luis Lazaro 19 days ago

1. What did I do yesterday? Installation of modules, pillow, faker, django_cleanup
2. What will I do today? start with coding of the frontend
3. Anything blocking I progress? none

Daily Scrum Report Day 02

- **OpenProject:** [Sprint 1 Week 2 Day 02 Daily Scrum Meeting Individual Updated Report](#)
- Scrum Report Video recording link from Group channel: [|Link|](#)

LB RE: Sprint 1 Week 2 Day 02 Daily Scrum Meeting Individual Updated Report - Added by Lorenzo Bernal 19 days ago

1. What did I do yesterday? - Assigned tasks for members for the revision of ERD and DFD
2. What will I do today? - Activity Diagram with swim lanes
3. Anything blocking I progress? - None

LL RE: Sprint 1 Week 2 Day 02 Daily Scrum Meeting Individual Updated Report - Added by Luis Lazaro 19 days ago

1. What did I do yesterday? - Started coding for frontend
2. What will I do today? - Test Case Tables and put DFD in MySQL Workbench
3. Anything blocking I progress? - Cannot open my OpenProject

GC RE: Sprint 1 Week 2 Day 02 Daily Scrum Meeting Individual Updated Report - Added by Gabrielle Cabangcala 13 days ago

1. What did I do yesterday? revision for DFD
2. What will I do today? Test Case table
3. Anything blocking I progress? none

MM RE: Sprint 1 Week 2 Day 02 Daily Scrum Meeting Individual Updated Report - Added by Mark Marabi 5 days ago

1. What did I do yesterday? - Studied the ERD and the necessary revisions
2. What will I do today? - Study the installation code
3. Anything blocking I progress? - Internet connection

Daily Scrum Report Day 03

- **OpenProject:** [Sprint 1 Week 2 Day 03 Daily Scrum Meeting Individual Updated Report](#)
- Scrum Report Video recording link from Group channel: [|Link|](#)

LB RE: Sprint 1 Week 2 Day 03 Daily Scrum Meeting Individual Updated Report - Added by Lorenzo Bernal 18 days ago

1. What did I do yesterday? - Started the creation and design of the Activity Diagram deliverable.
2. What will I do today? - I will check the updated ERD from the MySQL workbench made by Luis, continue the creation of the Activity Diagram, and create test cases for the use cases.
3. Anything blocking I progress? - None.

MM RE: Sprint 1 Week 2 Day 03 Daily Scrum Meeting Individual Updated Report - Added by Mark Marabi 5 days ago

1. What did I do yesterday? - Made the Product Backlog Refinement, depending on their priority level
2. What will I do today? - Started the Activity Diagram
3. Anything blocking my progress? - Brownout due to typhoon

GC RE: Sprint 1 Week 2 Day 03 Daily Scrum Meeting Individual Updated Report - Added by Gabrielle Cabangcala 3 days ago

1. What did I do yesterday? Learn and watch how to make activity diagram
2. What will I do today? revise parts on activity diagram
3. Anything blocking I progress? brownout

Entity Relationship Diagram |[Link](#)|

Corresponding Github repository commit | [Link](#) |

The screenshot shows the VS Code Explorer sidebar on the left and the main editor area on the right. In the Explorer sidebar, the file tree is expanded to show the following structure:

- docs/MSYADD1
 - 01 Analysis and design doc...
 - QuadThink_ERD.pdf
 - 03 Midterm Deliverables
 - 034 Dataflow Diagrams - I...
 - QuadThink - DFD.docx
 - QuadThink - DFD.pdf
 - 035 MNTSDEV output
 - Fully Dressed Case_QUA...
 - QuadThink_MNTSDEV Fl...
 - 036 Midterm Output
 - QuadThink - MYSADD1 ...

The file 'QuadThink_ERD.pdf' is highlighted with a red box, and a red arrow points to it from the right. The main editor area on the right shows a list of files and folders, with the following structure:

- 6 files changed +0 -0 lines changed
 - docs/MSYADD1/01 Analysis and design documents/015 Entity Relationship Diagrams/QuadThink_ERD.pdf
 - Binary file not shown.
 - docs/MSYADD1/03 Midterm Deliverables/034 Dataflow Diagrams - Initial draft/QuadThink - DFD.docx
 - Binary file not shown.
 - docs/MSYADD1/03 Midterm Deliverables/034 Dataflow Diagrams - Initial draft/QuadThink - DFD.pdf
 - Binary file not shown.
 - docs/MSYADD1/03 Midterm Deliverables/035 MNTSDEV output/Fully Dressed Case_QUADTHINK (1).pdf
 - Binary file not shown.
 - docs/MSYADD1/03 Midterm Deliverables/035 MNTSDEV output/QuadThink_MNTSDEV Final Paper (5).pdf
 - Binary file not shown.
 - docs/MSYADD1/03 Midterm Deliverables/036 Midterm Output/QuadThink - MYSADD1 Midterms PPT.pdf
 - Binary file not shown.

Activity Diagram with Swimlanes [Link](#)

Hierarchy: 2.0 Planning Phase ▶ 2.3 Requirements and Analysis Design Diagrams ▶ X

← TASK 2.3.4 Activity Diagram with Swimlanes

In progress ▼

#3014: Created by Lorenzo Bernal. Last updated on 09/30/2025 2:28 PM.

This outlines the Activity Diagram with Swimlane activity following the format of the Use Case Diagram with three main actors: User, Employee, and System Administrator

PEOPLE

Assignee	LB Lorenzo Bernal	Responsible*	GC Gabrielle Cabangcala
			MM Mark Marabi
			LB Lorenzo Bernal
			LL Luis Lazaro
Accountable	LB Lorenzo Bernal	Consulted	-
Informed	-		

ESTIMATES AND PROGRESS

Work	8h	Remaining work	0h
% Complete	100%	Spent time	9h

DETAILS

Priority *	Normal	Date	09/18/2025 - 10/06/2025
------------	-------------------	------	-------------------------

+ Create

🗨️ 🔄 📄 📁 ⚙️

ACTIVITY FILES RELATIONS (1) WATCHERS (1) GITHUB

📄

LB

 Lorenzo Bernal 09/27/2025 11:52 PM
% Complete changed from 10% to 80%
Remaining work changed from 7.2h to 1.6h

📄

LB

 Lorenzo Bernal 09/28/2025 12:51 PM
Assignee set to Lorenzo Bernal
Start date changed from 06/06/2025 to 09/18/2025
Duration changed from 87 days to 13 days

📄

LB

 Lorenzo Bernal 10/01/2025 01:12 AM
Activity Diagram Commit

📄

LB

Corresponding GitHub repository commit [Link](#)

Commit 1b697ef

ldiazaro2 committed 2 days ago

Update 01 Analysis and Design Docs

1 parent 9d98cec commit 1b697ef

7 files changed +0 -9 lines changed

docs/MSYAD01/01 Analysis and design documents/011 Use Case Diagrams/Use Case Diagram - QuadThink.pdf 137 KB

docs/MSYAD01/01 Analysis and design documents/012 Fully dressed Use Cases/Fully Dressed Use Case - QuadThink.pdf 716 KB

docs/MSYAD01/01 Analysis and design documents/012 Fully dressed Use Cases/Fully Dressed Use Case_QuadThink.pdf -485 KB

docs/MSYAD01/01 Analysis and design documents/013 Activity diagrams with swim-lanes/Activity Diagram - QuadThink .pdf 931 KB

docs/MSYAD01/01 Analysis and design documents/013 Activity diagrams with swim-lanes/Activity Diagram - QuadThink.pdf -545 KB

docs/MSYAD01/01 Analysis and design documents/014 Test Cases/QuadThink_TestCaseTable.xlsx -22.3 KB

Test Case Tables [\[Link\]](#)

hierarchy: <u>Planning phase</u> >> <u>Requirements and Analysis</u> Design Diagrams >> <u>2.3.2 Use Cases</u> >> <u>2.3.2.1 Use Case Diagram</u> >> <u>2.3.2.1.1 Documents for Test Cases</u> >> >>

TASK 2.3.2.1.1 Test Case for UCD 2.3.2.1

Closed #442: Created by Joe Gene Quesada APC. Last updated on 10/12/2025 1:30 PM.

WBS:	2.3.2.1.1.1
Work Package:	2.3.2.1.1.1 Test Case for UCD
Package Owner:	QuadThink
Owner Organization:	DOST-STII IRAD
Participants:	- Mark Lyster Marabi - Lorenzo Emil Bernal - Gab Cabangcala - Luis Lorenzo Lazaro
Description:	A test case for a Use Case Diagram describes how a particular use case will be tested to ensure that the system behaves as expected. Each test case links back to a specific use case and includes details about inputs, steps, and expected outcomes.
Completion State:	Completed test cases mapped to each of the use cases.

PEOPLE

Assignee

LL

Luis Lazaro

Responsible*

CC

Gabrielle Cabangcala

LL

Luis Lazaro

MM

Mark Marabi

LB

Lorenzo Bernal

+ Create



ACTIVITY

FILES (1)

RELATIONS (1)

WATCHERS (1)

GITHU

Description changed (Details)

Lorenzo Bernal

09/27/2025 11:52 PM

Subject changed from 2.3.2.1.1.1 Test Case for UCD 2.3.2.1.1 to 2.3.2.1.1.1 Test Case for UCD 2.3.2.1

Accountable set to Lorenzo Bernal

Lorenzo Bernal

09/27/2025 11:58 PM

Finish date set to 10/03/2025

Start date changed from 10/06/2025 to 09/18/2025

Duration set to 12 days

Lorenzo Bernal

09/30/2025 02:30 PM

Test Case Table Commit

Lorenzo Bernal

10/07/2025 03:07 AM

Responsible* set to Gabrielle Cabangcala, Luis Lazaro, Mark Marabi, Lorenzo Bernal

Lorenzo Bernal

10/08/2025 01:09 PM

Status changed from In progress to Closed

Mark Marabi

10/12/2025 01:35 PM

Test Case Table Commit

Corresponding Github repository commit [\[Link\]](#)

Commit 1b697ef

idlazaro2 committed 2 days ago

Update 01 Analysis and Design Docs

1 parent [8998ccc](#) commit 1b697ef

Filter files...

docs/MSYADD1/01 Analysis ...

011 Use Case Diagrams

Use Case Diagram - Quad...

012 Fully dressed Use Cases

Fully Dressed Use Case - Q...

Fully Dressed Use Case_Q...

013 Activity diagrams with s...

Activity Diagram - QuadTh...

Activity Diagram - QuadTh...

014 Test Cases

QuadThink_TestCaseTable...

Test Case Tables - QuadThi...

7 files changed +0 -0 lines changed

docs/MSYADD1/01 Analysis and design documents/011 Use Case Diagrams/Use Case Diagram - QuadThink.pdf

137 KB

Binary file not shown.

...001/01 Analysis and design documents/012 Fully dressed Use Cases/Fully Dressed Use Case - QuadThink.pdf

716 KB

Binary file not shown.

...YADD1/01 Analysis and design documents/012 Fully dressed Use Cases/Fully Dressed Use Case_QUADTHINK.pdf

-485 KB

Binary file not shown.

...1 Analysis and design documents/013 Activity diagrams with swim-lanes/Activity Diagram - QuadThink .pdf

931 KB

Binary file not shown.

...01 Analysis and design documents/013 Activity diagrams with swim-lanes/Activity Diagram - QuadThink.pdf

-545 KB

Binary file not shown.

Fully Dressed Use Case [Link](#)

←

TASK 2.3.2.1.2 Use Case Fully Dressed for UCD 2.3.2.1

+ Create

Closed

#441: Created by Joe Gene Quesada APC. Last updated on 10/12/2025 1:27 PM.

WBS	2.3.2.1.2
Work Package:	2.3.2.1.2 Use Case Fully Dressed
Package Owner:	Quadthink
Owner Organization:	DOST-STII IRAD
Participants:	- Lorenzo Bernal - Gab Cabangcala - Luis Lazaro - Mark Marabi
Description:	A comprehensive use case that defines actors, preconditions, main and alternate flows, exceptions, and postconditions to clearly describe system behavior.
Completion State:	Completed fully dressed use case with all flows and conditions, ensuring a detailed reference for system design, testing, and stakeholder alignment.

PEOPLE

Assignee

LL

Luis Lazaro

Responsible*

LB

Lorenzo Bernal

LL

Luis Lazaro

MM

Mark Marabi

GC

Gabrielle Cabangcala

Accountable

LB

Lorenzo Bernal

Consulted

ACTIVITY

FILES (1)

RELATIONS (1)

WATCHERS (1)

GITHUB

Fully Dressed Use Case Commit

Lorenzo Bernal

10/01/2025 01:11 AM

...

Revised the Fully Dressed Use case

- added the parent use cases included in the UCD to the fully dressed use case

Lorenzo Bernal

10/01/2025 08:13 AM

...

Status changed from On hold to In progress

Lorenzo Bernal

10/08/2025 01:03 PM

...

Status changed from In progress to Closed

Luis Lazaro

10/12/2025 01:27 PM

...

Fully Dressed Use Case

Lorenzo Bernal

10/14/2025 06:30 AM

...

Accountable set to Lorenzo Bernal

Responsible* set to Gabrielle Cabangcala, Luis Lazaro, Mark Marabi, Lorenzo Bernal

Corresponding Github repository commit [Link](#)

Commit 1b697ef

ldiazaro2 committed 2 days ago

Update 01 Analysis and Design Docs

1 parent b98b3ec commit 1b697ef

Filter files...

docs/MSYADD1/01 Analysis ...

011 Use Case Diagrams

Use Case Diagram - Quad...

012 Fully dressed Use Cases

Fully Dressed Use Case - Q...

Fully Dressed Use Case_Q...

013 Activity diagrams with s...

Activity Diagram - QuadTh...

Activity Diagram - QuadTh...

014 Test Cases

QuadThink_TestCaseTable...

Test Case Tables - QuadThi...

7 files changed +0 lines changed

docs/MSYADD1/01 Analysis and design documents/011 Use Case Diagrams/Use Case Diagram - QuadThink.pdf 137 KB

Binary file not shown.

...D01/01 Analysis and design documents/012 Fully dressed Use Cases/Fully Dressed Use Case - QuadThink.pdf 716 KB

Binary file not shown.

...YADD1/01 Analysis and design documents/012 Fully dressed Use Cases/Fully Dressed Use Case_QuadTHINK.pdf -485 KB

Binary file not shown.

...1 Analysis and design documents/013 Activity diagrams with swim-lanes/Activity Diagram - QuadThink .pdf 931 KB

Binary file not shown.

...01 Analysis and design documents/013 Activity diagrams with swim-lanes/Activity Diagram - QuadThink.pdf -545 KB

Binary file not shown.

Solo work:

- Lorenzo Emil S. Bernal**

Use Case Diagram [\[Link\]](#)

Hierarchy: 2.0 Planning Phase > 2.3 Requirements and Analysis Design Diagrams > 2.3.2 Use Cases > 2.3.2.1 Use Case Diagram > X

TASK 2.3.2.1.2 Use Case Fully Dressed for UCD 2.3.2.1 + Create 🔍 🔄 🔒 📄 📁 ⋮

Closed #441: Created by Joe Gene Quesada APC. Last updated on 10/12/2025 1:27 PM.

WBS	2.3.2.1.2
Work Package:	2.3.2.1.2 Use Case Fully Dressed
Package Owner:	Quadthink
Owner Organization:	DOST-STII IRAD
Participants:	- Lorenzo Bernal - Gab Cabangcala - Luis Lazaro - Mark Marabi
Description:	A comprehensive use case that defines actors, preconditions, main and alternate flows, exceptions, and postconditions to clearly describe system behavior.
Completion State:	Completed fully dressed use case with all flows and conditions, ensuring a detailed reference for system design, testing, and stakeholder alignment.

PEOPLE

Assignee	Responsible*
Luis Lazaro	Lorenzo Bernal
	Luis Lazaro
	Mark Marabi
	Gabrielle Cabangcala

Accountable	Consulted
Lorenzo Bernal	-

ACTIVITY **FILES (1)** **RELATIONS (1)** **WATCHERS (1)** **GITHUB**

Fully Dressed Use Case Commit

Lorenzo Bernal 10/01/2025 01:11 AM

Revised the Fully Dressed Use case

- added the parent use cases included in the UCD to the fully dressed use case

Lorenzo Bernal 10/01/2025 08:13 AM

Status changed from On hold to In progress

Lorenzo Bernal 10/08/2025 01:03 PM

Status changed from In progress to Closed

Luis Lazaro 10/12/2025 01:27 PM

Fully Dressed Use Case

Lorenzo Bernal 10/14/2025 06:30 AM

- Accountable set to Lorenzo Bernal
- Responsible* set to Gabrielle Cabangcala, Luis Lazaro, Mark Marabi, Lorenzo Bernal

Corresponding Github repository commit [\[Link\]](#)

Commit **1b697ef** 🔍 Browse files

ldlazaroz committed 2 days ago

Update 01 Analysis and Design Docs

[Demo](#) 1 parent [5d8f6ec](#) commit 1b697ef

Filter files...

7 files changed +0 -0 lines changed

Search within code

- docs/MSYAD01/01 Analysis and design documents/011 Use Case Diagrams/Use Case Diagram - QuadThink.pdf 137 KB
- Binary file not shown.
- ...001/01 Analysis and design documents/012 Fully dressed Use Cases/Fully Dressed Use Case - QuadThink.pdf 716 KB
- Binary file not shown.
- ...YAD01/01 Analysis and design documents/012 Fully dressed Use Cases/Fully Dressed Use Case_QuadTHINK.pdf -405 KB
- Binary file not shown.
- ...1 Analysis and design documents/013 Activity diagrams with swim-lanes/Activity Diagram - QuadThink .pdf 931 KB
- Binary file not shown.
- ...01 Analysis and design documents/013 Activity diagrams with swim-lanes/Activity Diagram - QuadThink.pdf -545 KB
- Binary file not shown.
- docs/MSYAD01/01 Analysis and design documents/014 Test Cases/QuadThink_TestCaseTable.xlsx -39.1 KB

Stakeholder Analysis [Link](#)

1.2.4 Create Stakeholder Analysis

Closed #1833: Created by Mark Marabi. Last updated on 09/28/2025 1:40 PM.

WBS:	1.2.4
Work Package:	Create Stakeholder Analysis
Package Owner:	QuadThink
Owner Organization:	DOST-STII IRAD
Participants:	- Mark Lyster Marabi - Lorenzo Emil Bernal - Gab Cabangcala - Luis Lorenzo Lazaro
Description:	This work package identifies and analyzes stakeholders relevant to the CitSense project. Using the stakeholder mapping diagram, the team categorizes stakeholders based on their influence and interest (e.g., high influence-high interest, low influence-high interest). The objective is to document stakeholder needs, expectations, influence levels, and communication strategies to ensure engagement and alignment throughout the project lifecycle.
Completion State:	A validated stakeholder register and analysis document, including stakeholder classification (interest/influence matrix), expectations, potential impact on the project, and recommended communication strategies.
Assumptions:	Stakeholders will be available for consultation and validation.
Risks:	- Misclassification of stakeholder influence could lead to poor engagement. - Incomplete information on external stakeholders may weaken analysis.
Risk Mitigation:	- Establish clear communication protocols to manage conflicts. - Revisit and update stakeholder analysis periodically.
Budget:	

Create

ACTIVITY 5 FILES RELATIONS (1) WATCHERS (1) GITHUB >

Mark Marabi 08/24/2025 07:03 AM

Description set (Details)

Mark Marabi 08/31/2025 10:24 AM

Consulted set to a@jayscondo @stii.dost.gov.ph

Informed set to a@jayscondo @stii.dost.gov.ph

Lorenzo Bernal 09/01/2025 07:27 AM

Status changed from New to Closed

Lorenzo Bernal 09/01/2025 11:41 AM

Description changed (Details)

Lorenzo Bernal 09/02/2025 10:42 AM

Version set to Project Setup and Direction

Lorenzo Bernal 09/02/2025 10:54 AM

Budget set to 1. Initiation Phase Budget

Project phase set to Initiating

Mark Marabi 09/08/2025 12:34 AM

Assignee changed from Mark Marabi to Lorenzo Bernal

Luis Lazaro 09/28/2025 01:40 PM

Stakeholder Analysis Commit

Corresponding Github repository commit [Link](#)

APC-SoCIT / APC_2025_2026_T1_M1232_G07-DOST-CitSense

Type to search

<> Code Issues Pull requests Actions Projects Security Insights Settings

Commit a7bc65f

GabCabangcala committed 2 weeks ago

add PH Docs Chapter 2 files

1 parent 28e738c commit a7bc65f

Filter files...

docs/MSYADD01/03 Miterm D...

QuadThink_Charter.pdf

QuadThink_Objectives.pdf

QuadThink_Scope.pdf

QuadThink_Stakeholder An...

4 files changed -0 -0 lines changed

docs/MSYADD01/03 Miterm Deliverables/031 PH Docs Chapter 2/QuadThink_Charter.pdf 189 KB

Binary file not shown.

docs/MSYADD01/03 Miterm Deliverables/031 PH Docs Chapter 2/QuadThink_Objectives.pdf 143 KB

Binary file not shown.

docs/MSYADD01/03 Miterm Deliverables/031 PH Docs Chapter 2/QuadThink_Scope.pdf 276 KB

Binary file not shown.

docs/MSYADD01/03 Miterm Deliverables/031 PH Docs Chapter 2/QuadThink_Stakeholder Analysis.xlsx 38.9 KB

Binary file not shown.

Comments 0

Lock conversation

Comment

Dataflow Diagram Level 2 – 4.0 Manage Reports [Link](#)

←

TASK 2.3.1.3.3 Dataflow Diagram Level 2: 4.0 - Manage Reports

Closed

#2085 Created by Gabriele Cabangcala. Last updated on 10/12/2025 11:29 AM.

WBS:	2.3.1.2.3
Work Package:	Dataflow Diagram Level 3.0 - Manage Reports
Package Owner:	QuadThink
Owner Organization:	DOST-STII IRAD
Participants:	- Mark Lyster Marabi - Lorenzo Emil Bernal - Gab Cabangcala - Luis Lorenzo Lazaro
Description:	This level 2 diagram outlines how the system will retrieve data from the system's database and then serve it to the employee as results (e.g., dashboard, data table). Additionally, generate reports on the dashboard and export the data table.

PEOPLE

Assignee	LB Lorenzo Bernal	Responsible*	LB Lorenzo Bernal
Accountable	LB Lorenzo Bernal	Consulted	-
Informed	-		

ESTIMATES AND PROGRESS

Work	2h	Remaining work	2h
% Complete	0%	Spent time	6h

+ Create

ACTIVITY

FILES (1)

RELATIONS (1)

WATCHERS (1)

GITHUB

Description changed (Details)

LB

Lorenzo Bernal

09/18/2025 01:22 PM

Status changed from Closed to In progress

LB

Lorenzo Bernal

09/27/2025 11:43 PM

Subject changed from 2.3.1.2.3 Dataflow Diagram Level 2: 3.0 - Manage Reports to 2.3.1.2.3 Dataflow Diagram Level 2: 3.0 - Manage Reports

% Complete set to 0%

Work set to 2h

Remaining work set to 2h

LB

Lorenzo Bernal

09/28/2025 12:35 PM

Subject changed from 2.3.1.2.3 Dataflow Diagram Level 2: 3.0 - Manage Reports to 2.3.1.3.3 Dataflow Diagram Level 2: 3.0 - Manage Reports

Parent changed from 2.3.1.2 Dataflow Diagram Level 1 to 2.3.1.3 Dataflow Diagram Level 2

LB

Lorenzo Bernal

10/12/2025 01:39 PM

...

Dataflow Diagram Commit

LB

Lorenzo Bernal

10/08/2025 01:03 PM

Status changed from In progress to Closed

LB

Lorenzo Bernal

10/12/2025 11:29 AM

Subject changed from 2.3.1.3.3 Dataflow Diagram Level 2: 3.0 - Manage Reports to 2.3.1.3.3 Dataflow Diagram Level 2: 4.0 - Manage Reports

Add a comment. Type @ to notify people.

Corresponding Github repository commit [Link](#)

APC-SoCIT / APC_2025_2026_T1_MI232_G07-DOST-CitiSense

Q Type to search

<> Code Issues Pull requests Actions Projects Security Insights Settings

Commit 8875d7b

Isbernal committed 2 days ago

Update dataflow diagrams docs

1 parent 3d697ef commit 8875d7b

Filter files...

docs/MSYADD1/03 Mitem D...

- QuadThink - DFD.pdf

1 file changed

+0 -0 lines changed

docs/MSYADD1/03 Mitem Deliverables/034 Dataflow Diagrams - Initial draft/QuadThink - DFD.pdf -90.1 KB

Binary file not shown.

Comments

Lock conversation

Comment

Subscribe You're not receiving notifications from this thread.

- **Gabrielle Cabangcala**

PM Docs |[Link](#)|

The screenshot shows the OpenProject web interface. The top navigation bar includes a search bar and user avatars. The left sidebar contains a 'Work packages' section with a search bar and a list of filters like 'All Budgets and Costs' and 'All Work Packages'. The main content area displays a 'SUMMARY TASK' for '1.2 PM Foundations Ch 2 Initiate a project'. It includes a description, a list of people (Assignee, Responsible, Accountable), and a section for 'ESTIMATES AND PROGRESS' showing work, remaining work, and completion percentage. The bottom section shows project details like priority, phase, and version. On the right, an 'ACTIVITY' feed shows recent updates and comments from users like Lorenzo Bernal and Gabrielle Cabangcala.

Corresponding Github repository commit |[Link](#)|

The screenshot shows a GitHub repository page for the commit 'a7bc65f' by user 'GabiCabangcala'. The commit message is 'add PM Docs Chapter 2 files'. The file diff section shows four files changed: 'docs/MSVAD01/03 Mitem D.../QuadThink_Charter.pdf', 'docs/MSVAD01/03 Mitem Deliverables/031 PM Docs Chapter 2/QuadThink_Objectives.pdf', 'docs/MSVAD01/03 Mitem Deliverables/031 PM Docs Chapter 2/QuadThink_Scope.pdf', and 'docs/MSVAD01/03 Mitem Deliverables/031 PM Docs Chapter 2/QuadThink_Stakeholder Analysis.xlsx'. The comments section is empty, and there is a 'Subscribe' button at the bottom.

Dataflow Diagrams: Level 0 Context Diagram |[Link](#)|

APC_2025_2026_T1_M023...

← Work packages

Q Search by name

FAVORITE

All Budgets and Costs

All Work Packages

DEFAULT

All open

Latest activity

Recently created

Overdue

Summary

Created by me

Assigned to me

Shared with users

Shared with me

Hierarchy: 2.0 Planning Phase > 2.3 Requirements and Analysis Design Diagrams > 2.3.2 Use Cases > 2.3.2.1 Use Case Diagram > 2.3.2.1.1 Documents for Test Cases

←

TASK 2.3.2.1.1.1 Test Case for UCD 2.3.2.1

×

Closed

#442 Created by Joe Gene Quesada APC. Last updated on 10/12/2025 1:00 PM.

WBS:	2.3.2.1.1.1
Work Package:	2.3.2.1.1.1 Test Case for UCD
Package Owner:	QuadThink
Owner Organization:	DOST-STII IRAD
Participants:	- Mark Lyster Marabi - Lorenzo Emil Bernal - Gab Cabangcala - Luis Lorenzo Lazaro
Description:	A test case for a Use Case Diagram describes how a particular use case will be tested to ensure that the system behaves as expected. Each test case links back to a specific use case and includes details about inputs, steps, and expected outcomes.
Completion State:	Completed test cases mapped to each of the use cases.

PEOPLE

Assignee

Luis Lazaro

Responsible

Gabrielle Cabangcala

Luis Lazaro

Mark Marabi

Create

🗨️

🔒

🔍

📄

📁

🔖

ACTIVITY

FILES (0)

RELATIONS (0)

WATCHERS (0)

GITHUB

Subject changed from 2.3.2.1.1.1 Test Case for UCD 2.3.2.1.1 to 2.3.2.1.1.1 Test Case for UCD 2.3.2.1

Accountable set to Lorenzo Bernal

📅

Lorenzo Bernal

09/27/2025 11:58 PM

Finish date set to 10/01/2025

Start date changed from 10/06/2025 to 09/18/2025

Duration set to 12 days

📅

Lorenzo Bernal

09/30/2025 01:30 PM

Test Case Table Commit

📅

Lorenzo Bernal

10/07/2025 09:07 AM

Responsible set to Gabrielle Cabangcala, Luis Lazaro, Mark Marabi, Lorenzo Bernal

📅

Lorenzo Bernal

10/06/2025 01:00 PM

Status changed from in progress to Closed

📅

Mark Marabi

10/12/2025 01:05 PM

Test Case Table Commit

Add a comment. Type @ to notify people.

Corresponding Github repository commit |[Link](#)|

Filter files...

docs/MSYADD1/01 Analysis a...

011 Use Case Diagrams

Use Case Diagram - Quad...

012 Fully dressed Use Cases

Fully Dressed Use Case - Q...

Fully Dressed Use Case_Q...

013 Activity diagrams with s...

Activity Diagram - QuadTh...

Activity Diagram - QuadTh...

014 Test Cases

QuadThink_TestCaseTable...

Test Case Tables - QuadTh...

7 files changed

7 files changed

docs/MSYADD1/01 Analysis and design documents/011 Use Case Diagrams/Use Case Diagram - QuadThink.pdf

137 KB

Binary file not shown.

... Analysis and design documents/012 Fully dressed Use Cases/Fully Dressed Use Case - QuadThink.pdf

716 KB

Binary file not shown.

...01 Analysis and design documents/012 Fully dressed Use Cases/Fully Dressed Use Case_QUADTHINK.pdf

-405 KB

Binary file not shown.

...ysis and design documents/013 Activity diagrams with swim-lanes/activity Diagram - QuadThink .por

931 KB

Binary file not shown.

...ysis and design documents/013 Activity diagrams with swim-lanes/activity Diagram - QuadThink.pdf

-545 KB

Binary file not shown.

docs/MSYADD1/01 Analysis and design documents/014 Test Cases/QuadThink_TestCaseTable.xlsx

-22.1 KB

Binary file not shown.

docs/MSYADD1/01 Analysis and design documents/014 Test Cases/Test Case Tables - QuadThink.xlsx

25.1 KB

Binary file not shown.

Comments 0

Lock conversation

Comment

Subscribe

Activity Diagram with Swimlanes [\[Link\]](#)

APC_2025_2026_T1_M23...

Hierarchy: 2.0 Planning Phase > 2.3 Requirements and Analysis Design Diagrams > TASK 2.3.4 Activity Diagram with Swimlanes

In progress #3014 Created by Lorenzo Bernal. Last updated on 10/12/2025 1:29 PM.

This outlines the Activity Diagram with Swimlane activity following the format of the Use Case Diagram with three main actors: User, Employee, and System Administrator

PEOPLE

Assignee 18 Lorenzo Bernal **Responsible** 05 Gabrielle Cabangcala 01 Mark Marabi 18 Lorenzo Bernal 10 Luis Lazaro

Accountable 18 Lorenzo Bernal **Consulted** -

Informed -

ESTIMATES AND PROGRESS

Work 8h **Remaining work** 0h

% Complete 100% **Spent time** 10h

DETAILS

Priority Normal **Date** 09/18/2025 - 10/06/2025

Project phase Planning **Category** Design

Version Project Setup and Direction

COSTS

ACTIVITY FILES RELATIONS (1) WATCHERS (1) GITHUB >

Commit History:

- Lorenzo Bernal 10/01/2025 01:12 AM
Activity Diagram Commit
- Lorenzo Bernal 09/30/2025 02:39 PM
The work is now complete with the final "Manage Data Table" being finished by the team and just awaiting for approval.
% Complete changed from 100% to 100%
Remaining work changed from 1.0h to 0h
- Lorenzo Bernal 10/08/2025 01:04 PM
The changes were retracted.
- Gabrielle Cabangcala 10/12/2025 01:29 PM
Activity Diagram Commit

Add a comment. Type @ to notify people.

Corresponding Github repository commit [\[Link\]](#)

Filter files...

7 files changed +0 lines changed

- .../MSYAD01/01 Analysis and design documents/01 Use Case Diagrams/Use Case Diagram - QuadThnk.pdf 137 KB
- ... Analysis and design documents/012 Fully dressed Use Cases/Fully Dressed Use Case - QuadThnk.pdf 716 KB
- ...01 Analysis and design documents/012 Fully dressed Use Cases/Fully Dressed Use Case_QuadThnk.pdf -405 KB
- ...ysis and design documents/013 Activity diagrams with swim-lanes/Activity Diagram - QuadThnk.pdf 921 KB
- ...ysis and design documents/013 Activity diagrams with swim-lanes/Activity Diagram - QuadThnk.pdf -545 KB
- docs/MSYAD01/01 Analysis and design documents/014 Test Cases/QuadThnk_TestCaseTable.xlsx -22.1 KB
- docs/MSYAD01/01 Analysis and design documents/014 Test Cases/Test Case Tables - QuadThnk.xlsx 25.1 KB

Comments 0 Lock conversation

Comment

Subscribe You're not receiving notifications from this thread.

Entity Relationship Diagrams [|Link|](#)

The screenshot displays a Jira task page for "2.3.3 Entity Relationship Diagrams". The task is in a "Closed" state, created by Joe Gene Quesada APC, and last updated on 10/09/2025 1:01 PM.

Description: This ER is a specification of our databases. It demonstrates our arrangement of data on the user accounts and feedback. All the user information is contained in the user table. The labeled feedback table contains the cleaned feedback that is detailed. Our raw data is sourced from the IRAD database, which is an external source. There are numerous feedback entries, which can be modified by a user, and every record of the external database is converted to one record in our feedback table, and will then be processed to the labeled and stored in the labeled table. This configuration guarantees an effective and clear flow of data coming from the source, through our team, and into a structured format to be analyzed.

PEOPLE

Role	Assignee
Assignee	Lorenzo Bernal
Responsible	Lorenzo Bernal, Gabrielle Cabangcala, Mark Marabi, Luis Lazaro
Accountable	Lorenzo Bernal
Informed	-
Consulted	-

ESTIMATES AND PROGRESS

Field	Value
Work	4h
% Complete	100%
Remaining work	0h
Spent time	7h

DETAILS

Field	Value
Priority	Normal
Date	no start date - no finish date
Project phase	Planning
Category	-

ACTIVITY

- Gabrielle Cabangcala 09/23/2025 12:28 AM: Description set (Details)
- Luis Lazaro 09/23/2025 01:33 AM: Status changed from On hold to In progress
- Lorenzo Bernal 09/23/2025 12:02 PM: Description changed (Details)
- Lorenzo Bernal 10/12/2025 01:27 PM: Entity Relationship Diagram Commit
- Lorenzo Bernal 09/29/2025 01:57 PM: Description changed (Details)
- Lorenzo Bernal 09/29/2025 02:02 PM: Assignee set to Lorenzo Bernal
- Lorenzo Bernal 09/10/2025 02:45 PM: Description changed (Details)
- Lorenzo Bernal 10/08/2025 01:03 PM: Status changed from In progress to Closed

Corresponding Github repository commit [|Link|](#)

- **Luis Lorenzo Lazaro**

Project Charter [\[Link\]](#)

OpenProject

Search in OpenProject

Hierarchy: 1.0 Initiation Phase ▶ 1.2 PM Foundations Ch 2 Initiate a project ✕

← TASK 1.2.1 Create Charter

+ Create

Closed #1830: Created by Mark Marabi. Last updated on 09/28/2025 1:38 PM.

WBS:	1.2.1
Work Package:	Create Charter
Package Owner:	QuadThink
Owner Organization:	DOST-STII IRAD
Participants:	- Mark Lyster Marabi - Lorenzo Emil Bernal - Gab Cabangala - Luis Lorenzo Lazaro
Description:	Develop the CitiSense Project Charter by defining objectives, scope, milestones, stakeholders, and responsibilities. The charter will serve as the foundation for aligning the team and stakeholders, ensuring clarity in project direction, resource allocation, and deliverables for the smart bilingual sentiment analysis and visualization system.
Completion State:	A completed and approved project charter that clearly defines the CitiSense project scope, purpose, timeline, and stakeholder roles. This document provides the guiding framework for the next project phases.

ACTIVITY 11 FILES RELATIONS (1) WATCHERS (1) GITHUB >

Lorenzo Bernal 09/02/2025 10:48 AM
Version set to Project Setup and Direction

Lorenzo Bernal 09/02/2025 10:53 AM
Project phase set to Initiating

Mark Marabi 09/08/2025 12:34 AM
Assignee changed from Mark Marabi to Luis Lazaro

Lorenzo Bernal 09/27/2025 11:47 PM
Work changed from 6h to 2h

Luis Lazaro 09/28/2025 01:38 PM
Charter Commit

Add a comment. Type @ to notify people.

Corresponding Github repository commit [\[Link\]](#)

APC-SoCIT / APC_2025_2026_T1_M1232_G07-DOST-CitiSense

Code Issues Pull requests Actions Projects Security Insights Settings

Files

demo

Go to file

backend

docs

INTSDEV

MSYADD1

01 Analysis and design docu...

02 Technology Stack Definitio...

03 Mitem Deliverables

031 PM Docs Chapter 2

QuadThink_Charter.pdf

QuadThink_Objectives.pdf

QuadThink_Scope.pdf

QuadThink_Stakeholder An...

README

032 Openproject Activities

033 Design Thinking output

034 Dataflow Diagrams - Int...

035 MINTSDEV output

036 Mitem Output

README

04 Finals Deliverables

readme.md

APC_2025_2026_T1_M1232_G07-DOST-CitiSense / docs / MSYADD1 / 03 Mitem Deliverables / 031 PM Docs Chapter 2 / QuadThink_Charter.pdf

GabCabangala add PM Docs Chapter 2 files

189 KB

Project Management Foundations
with Bonnie Biafore

Project Charter

Project Name: CitiSense: A SMART Web Application for Automated Bilingual Feedback Processing with Sentiment Analysis and Data Visualization

Purpose

The purpose of the CitiSense project is to address the time-consuming, manual processing of feedback data currently handled by the IRAD department of the Department of Science and Technology – Science and Technology Information Institute (DOST-STII). The project responds to the growing need for automated sentiment analysis tools that support both English and Tagalog inputs, enabling faster, data-driven decisions. This initiative aligns with DOST-STII's strategic goal to enhance public science communication and increase responsiveness to stakeholder feedback.

High-level project description

CitiSense is a web-based system that leverages Natural Language Processing (NLP) to automatically analyze and classify textual feedback in English, Tagalog, or a mix of both. The system processes sentiment as positive, neutral, or negative and presents the results in a real-time interactive dashboard. Key features include:

Fully Dressed Use Case [\[Link\]](#)

OpenProject

Search in OpenProject

Hierarchy: 2.0 Planning Phase ▶ 2.3 Requirements and Analysis Design Diagrams ▶ 2.3.2 Use Cases ▶ 2.3.2.1 Use Case Diagram

TASK 2.3.2.1.2 Use Case Fully Dressed for UCD 2.3.2.1

#441: Created by Joe Gene Quesada APC. Last updated on 10/14/2025 6:30 AM.

WBS	2.3.2.1.2
Work Package:	2.3.2.1.2 Use Case Fully Dressed
Package Owner:	Quadthink
Owner Organization:	DOST-STII IRAD
Participants:	- Lorenzo Bernal - Gab Cabangcala - Luis Lazaro - Mark Marabi
Description:	A comprehensive use case that defines actors, preconditions, main and alternate flows, exceptions, and postconditions to clearly describe system behavior.
Completion State:	Completed fully dressed use case with all flows and conditions, ensuring a detailed reference for system design, testing, and stakeholder alignment.

ACTIVITY 14 FILES (1) RELATIONS (1) WATCHERS (1) GITHU >

Lorenzo Bernal 10/01/2025 08:13 AM
Status changed from On hold to In progress

Lorenzo Bernal 10/08/2025 01:03 PM
Status changed from In progress to Closed

Luis Lazaro 10/12/2025 01:27 PM
Fully Dressed Use Case

Lorenzo Bernal 10/14/2025 06:30 AM
Accountable set to Lorenzo Bernal
Responsible* set to Gabrielle Cabangcala, Luis Lazaro, Mark Marabi, Lorenzo Bernal

Add a comment. Type @ to notify people.

Corresponding Github repository commit [\[Link\]](#)

7 files changed

docs/MSYAD01/01 Analysis and design documents/011 Use Case Diagrams/Use Case Diagram - Quadthink.pdf 137 KB

Binary file not shown.

...SYAD01/01 Analysis and design documents/012 Fully dressed Use Cases/Fully Dressed Use Case - Quadthink.pdf 716 KB

Binary file not shown.

...MSYAD01/01 Analysis and design documents/012 Fully dressed Use Cases/Fully Dressed Use Case_QUADTHINK.pdf -495 KB

Binary file not shown.

...I/01 Analysis and design documents/013 Activity diagrams with swim-lanes/Activity Diagram - Quadthink .pdf 933 KB

Binary file not shown.

...DL/01 Analysis and design documents/013 Activity diagrams with swim-lanes/Activity Diagram - Quadthink.pdf -545 KB

Binary file not shown.

docs/MSYAD01/01 Analysis and design documents/014 Test Cases/Quadthink_TestCaseTable.xlsx -22.1 KB

Binary file not shown.

docs/MSYAD01/01 Analysis and design documents/014 Test Cases/Test Case Tables - Quadthink.xlsx 25.1 KB

Binary file not shown.

Comments 0 Lock conversation

Comment

Subscribe You're not receiving notifications from this thread.

Test Case Tables [\[Link\]](#)

OpenProject

Search in OpenProject

Hierarchy: 2.0 Planning Phase > 2.3 Requirements and Analysis Design Diagrams > 2.3.2 Use Cases > 2.3.2.1 Use Case Diagram > 2.3.2.1.1 Documents for Test Cases

TASK 2.3.2.1.1.1 Test Case for UCD 2.3.2.1

Closed #442: Created by Joe Gene Quesada APC. Last updated on 10/12/2025 1:30 PM.

WBS:	2.3.2.1.1.1
Work Package:	2.3.2.1.1.1 Test Case for UCD
Package Owner:	QuadThink
Owner Organization:	DOST-STII IRAD
Participants:	- Mark Lyster Marabi - Lorenzo Emil Bernal - Gab Cabangcala - Luis Lorenzo Lazaro
Description:	A test case for a Use Case Diagram describes how a particular use case will be tested to ensure that the system behaves as expected. Each test case links back to a specific use case and includes details about inputs, steps, and expected outcomes.
Completion State:	Completed test cases mapped to each of the use cases.

ACTIVITY 15 FILES (1) RELATIONS (1) WATCHERS (1) GITHU >

Lorenzo Bernal 09/30/2025 02:30 PM

Test Case Table Commit

Lorenzo Bernal 10/07/2025 03:07 AM

Responsible* set to Gabrielle Cabangcala, Luis Lazaro, Mark Marabi, Lorenzo Bernal

Lorenzo Bernal 10/08/2025 01:03 PM

Status changed from In progress to Closed

Mark Marabi 10/12/2025 01:35 PM

Test Case Table Commit

Add a comment. Type @ to notify people.

Corresponding Github repository commit |[Link](#)|

7 files changed

docs/MSYAD01/01 Analysis and design documents/011 Use Case Diagrams/Use Case Diagram - QuadThink.pdf 137 KB

docs/MSYAD01/01 Analysis and design documents/012 Fully dressed Use Cases/Fully Dressed Use Case - QuadThink.pdf 716 KB

docs/MSYAD01/01 Analysis and design documents/012 Fully dressed Use Cases/Fully Dressed Use Case - QuadThink.pdf -485 KB

docs/MSYAD01/01 Analysis and design documents/013 Activity diagrams with swim-lanes/Activity Diagram - QuadThink.pdf 913 KB

docs/MSYAD01/01 Analysis and design documents/013 Activity diagrams with swim-lanes/Activity Diagram - QuadThink.pdf -545 KB

docs/MSYAD01/01 Analysis and design documents/014 Test Cases/QuadThink_TestCaseTable.xlsx -22.1 KB

docs/MSYAD01/01 Analysis and design documents/014 Test Cases/Test Case Tables - QuadThink.xlsx 25.3 KB

Comments 0

Lock conversation

Comment

Subscribe You're not receiving notifications from this thread.

Activity Diagram with Swimlanes |[Link](#)|

OpenProject

Search in OpenProject

Hierarchy: 2.0 Planning Phase > 2.3 Requirements and Analysis Design Diagrams

TASK 2.3.4 Activity Diagram with Swimlanes

In progress #3014: Created by Lorenzo Bernal. Last updated on 10/12/2025 1:29 PM.

This outlines the Activity Diagram with Swimlane activity following the format of the Use Case Diagram with three main actors: User, Employee, and System Administrator

PEOPLE

Assignee	LB Lorenzo Bernal	Responsible*	GC Gabrielle Cabangcala
			MM Mark Marabi
			LB Lorenzo Bernal
			LL Luis Lazaro
Accountable	LB Lorenzo Bernal	Consulted	-
Informed	-		

ESTIMATES AND PROGRESS

Work	8h	Remaining work	0h
% Complete	100%	Spent time	10h

ACTIVITY FILES RELATIONS (1) WATCHERS (1) GITHUB

The work is now complete with the final "Manage Data Table" being finished by the team and just awaiting for approval.

% Complete changed from 80% to 100%
Remaining work changed from 1.6h to 0h

LB Lorenzo Bernal 10/08/2025 01:04 PM
The changes were retracted.

GC Gabrielle Cabangcala 10/12/2025 01:29 PM
Activity Diagram Commit

Add a comment. Type @ to notify people.

Corresponding Github repository commit [\[Link\]](#)

7 files changed

docs/MSYAD01/01 Analysis and design documents/011 Use Case Diagrams/Use Case Diagram - Quadthink.pdf 137 KB

docs/MSYAD01/01 Analysis and design documents/012 Fully dressed Use Cases/Fully Dressed Use Case - Quadthink.pdf 716 KB

docs/MSYAD01/01 Analysis and design documents/012 Fully dressed Use Cases/Fully Dressed Use Case - QUADTHINK.pdf 485 KB

docs/MSYAD01/01 Analysis and design documents/013 Activity diagrams with swim-lanes/Activity Diagram - Quadthink.pdf 915 KB

docs/MSYAD01/01 Analysis and design documents/013 Activity diagrams with swim-lanes/Activity Diagram - Quadthink.pdf 545 KB

docs/MSYAD01/01 Analysis and design documents/014 Test Cases/Quadthink_TestCaseTable.xlsx 22.3 KB

docs/MSYAD01/01 Analysis and design documents/014 Test Cases/Test Case Tables - Quadthink.xlsx 25.3 KB

Comments

Comment

Subscribe You're not receiving notifications from this thread.

Dataflow Diagram Level 2: 1.0 - Manage Account [\[Link\]](#)

OpenProject

Search in OpenProject

Hierarchy: 2.0 Planning Phase ▶ 2.3 Requirements and Analysis Design Diagrams ▶ 2.3.1 Dataflow Diagrams ▶ 2.3.1.3 Dataflow Diagram Level 2 ✎ ✕

TASK 2.3.1.3.1 Dataflow Diagram Level 2: 1.0 - Manage Account

Closed #438: Created by Joe Gene Quesada APC. Last updated on 10/12/2025 1:40 PM.

WBS:	2.3.1.2.1
Work Package:	Level 2.0 Manage Account
Package Owner:	QuadThink
Owner Organization:	DOST-STII IRAD
Participants:	- Mark Lyster Marabi - Lorenzo Emil Bernal - Gab Cabangala - Luis Lorenzo Lazaro
Description:	This diagram is to outline the account management system that the user can do such as register, login, and edit their profile

PEOPLE

Accinnee

Reconnaisable*

Lorenzo Bernal

ACTIVITY 6 FILES (1) RELATIONS (1) WATCHERS (1) GITHU >

Subject changed from 2.3.1.2.1 Dataflow Diagram Level 2: 2 1.0 - Manage Account to 2.3.1.3.1 Dataflow Diagram Level 2: 2 1.0 - Manage Account

Parent changed from 2.3.1.2 Dataflow Diagram Level 1 to 2.3.1.3 Dataflow Diagram Level 2

Lorenzo Bernal 09/28/2025 12:43 PM

Dataflow Diagram Commit

Lorenzo Bernal 10/08/2025 01:03 PM

Status changed from in progress to Closed

Lorenzo Bernal 10/12/2025 01:40 PM

Subject changed from 2.3.1.3.1 Dataflow Diagram Level 2: 2 1.0 - Manage Account to 2.3.1.3.1 Dataflow Diagram Level 2: 1.0 - Manage Account

Add a comment. Type @ to notify people.

Corresponding Github repository commit [|Link|](#)

APC-SoCIT / APC_2025_2026_T1_Mi232_G07-DOST-CitiSense

Code Issues Pull requests Actions Projects Security Insights Settings

Files

514235f

Go to file

backend

docs

INTSDEV

MSYADD1

01 Analysis and design docu...

02 Technology Stack Definitio...

03 Mitem Deliverables

031 PM Docs Chapter 2

032 Openproject Activities

033 Design Thinking output

034 Dataflow Diagrams - Init...

QuadThink - DFD.pdf

README.MD

035 MINTSDEV output

036 Midterm Output

README.MD

04 Finals Deliverables

readme.md

frontend

.gitignore

README.md

APC_2025_2026_T1_Mi232_G07-DOST-CitiSense / docs / MSYADD1 / 03 Mitem Deliverables / 034 Dataflow Diagrams - Initial draft / QuadThink - DFD.pdf

lbernal Add MINTSDEV, Midterm, and Dataflow Diagrams docs

514235f - last month History

417 KB

Use Case Diagram

CitiSense: A Smart Web App for Automated Bilingual Feedback Processing and Data Visualization

- **Mark Lyster Marabi**

Design Thinking Stage 2: Define [Link](#)

The screenshot shows the OpenProject web interface. The top navigation bar includes the OpenProject logo, a search bar, and user avatars. The left sidebar contains a 'Work packages' section with a search bar and a list of filters: FAVORITE, All Budgets and Costs, All Work Packages (selected), DEFAULT, All open, Latest activity, Recently created, Overdue, Summary, Created by me, Assigned to me, Shared with users, and Shared with me. The main content area displays a task titled '2.1 Design Thinking Stage 2: Define' with a status of 'Closed'. The task details include: WBS: 2.1, Work Package: 2.1 Design Thinking Stage 2: Define, Package Owner: QuadThink, Owner Organization: DOST-STII IRAD, Participants: Mark Lyster Marabi, Lorenzo Emil Bernal, Gab Cabangcala, Luis Lorenzo Lazaro, Description: Identify the problems and pain points of the client to better see the bigger picture of the overall problem, Completion State: Completed main problem statements and "How Might We" statements. This will guide us for the ideation process in Design Thinking Stage 3, and Stakeholders (IRAD – DOST-STII) can adopt a full working automated system in. The right sidebar shows the 'ACTIVITY' tab with a list of recent activities: Version set to Project Setup and Direction, Budget set to 2. Planning Phase Budget, Description changed (Details), Status changed from On hold to Closed, and Work changed from 1h to 6h. Below the activity list is a comment by Mark Marabi dated 09/28/2025 01:52 PM, titled 'Design Thinking Stage 2 Commit'.

Field	Value
WBS:	2.1
Work Package:	2.1 Design Thinking Stage 2: Define
Package Owner:	QuadThink
Owner Organization:	DOST-STII IRAD
Participants:	- Mark Lyster Marabi - Lorenzo Emil Bernal - Gab Cabangcala - Luis Lorenzo Lazaro
Description:	Identify the problems and pain points of the client to better see the bigger picture of the overall problem.
Completion State:	Completed main problem statements and "How Might We" statements. This will guide us for the ideation process in Design Thinking Stage 3. Stakeholders (IRAD – DOST-STII) can adopt a full working automated system in

Corresponding Github repository commit [Link](#)

The screenshot shows a Github repository page for the repository 'APC-SoCIT / APC_2025_2026_T1_MI232_G07-DOST-CitiSense'. The commit page displays the commit 'cadb0cf' by user 'GabCabangcala' committed last month. The commit message is 'add Design Thinking Output Files'. The file changes section shows two files changed: '...gn Thinking output/quadThink_Design Thinking Stages Final Documentation.docx' (2.9 MB) and '...ign Thinking output/quadThink_Design Thinking Stages Final Documentation.pdf' (1.83 MB). Both files are marked as 'Binary file not shown.' The page also includes a search bar for code, a 'Lock conversation' button, and a 'Comments' section with 0 comments.

Test Case Tables [Link](#)

OpenProject

Search in OpenProject

Hierarchy: 2.0 Planning Phase ▶ 2.3 Requirements and Analysis Design Diagrams ▶ 2.3.2 Use Cases ▶ 2.3.2.1 Use Case Diagram ▶ 2.3.2.1.1 Documents for Test Cases

TASK 2.3.2.1.1.1 Test Case for UCD 2.3.2.1

Closed #442: Created by Joe Gene Quesada APC. Last updated on 10/12/2025 1:30 PM.

WBS:	2.3.2.1.1.1
Work Package:	2.3.2.1.1.1 Test Case for UCD
Package Owner:	QuadThink
Owner Organization:	DOST-STII IRAD
Participants:	- Mark Lyster Marabi - Lorenzo Emil Bernal - Gab Cabangcala - Luis Lorenzo Lazaro
Description:	A test case for a Use Case Diagram describes how a particular use case will be tested to ensure that the system behaves as expected. Each test case links back to a specific use case and includes details about inputs, steps, and expected outcomes.
Completion State:	Completed test cases mapped to each of the use cases.

ACTIVITY 15 FILES (1) RELATIONS (1) WATCHERS (1) GITHU >

Lorenzo Bernal 09/30/2025 02:30 PM

Test Case Table Commit

Lorenzo Bernal 10/07/2025 03:07 AM

Responsible* set to Gabrielle Cabangcala, Luis Lazaro, Mark Marabi, Lorenzo Bernal

Lorenzo Bernal 10/08/2025 01:03 PM

Status changed from In progress to Closed

Mark Marabi 10/12/2025 01:35 PM

Test Case Table Commit

Add a comment. Type @ to notify people.

Test Case Tables repository commit [\[Link\]](#)

Commit 1b697ef

ldlazaroz committed 2 weeks ago

Update 01 Analysis and Design Docs

demo

1 parent 9d98cec commit 1b697ef

Filter files...

docs/MSVADD1/01 Analysis ...

011 Use Case Diagrams

Use Case Diagram - Quad...

012 Fully dressed Use Cases

Fully Dressed Use Case - Q...

Fully Dressed Use Case_Q...

013 Activity diagrams with s...

Activity Diagram - QuadTh...

Activity Diagram - QuadTh...

014 Test Cases

QuadThink_TestCaseTable...

Test Case Tables - QuadThi...

7 files changed +0 -0 lines changed

Search within code

... and design documents/011 Use Case Diagrams/Use Case Diagram - QuadThink.pdf 137 KB

Binary file not shown.

...documents/012 Fully dressed Use Cases/Fully Dressed Use Case - QuadThink.pdf 716 KB

Binary file not shown.

...n documents/012 Fully dressed Use Cases/Fully Dressed Use Case_QUADTHINK.pdf -485 KB

Binary file not shown.

...ents/013 Activity diagrams with swim-lanes/Activity Diagram - QuadThink .pdf 931 KB

Binary file not shown.

Activity Diagram with Swimlanes [\[Link\]](#)

OpenProject

Search in OpenProject

Hierarchy: 2.0 Planning Phase > 2.3 Requirements and Analysis Design Diagrams

TASK 2.3.4 Activity Diagram with Swimlanes

In progress #3014: Created by Lorenzo Bernal. Last updated on 10/12/2025 1:29 PM.

This outlines the Activity Diagram with Swimlane activity following the format of the Use Case Diagram with three main actors: User, Employee, and System Administrator

PEOPLE

Assignee	LB Lorenzo Bernal	Responsible*	GC Gabrielle Cabangcala
			MM Mark Marabi
			LB Lorenzo Bernal
			LL Luis Lazaro
Accountable	LB Lorenzo Bernal	Consulted	-
Informed	-		

ESTIMATES AND PROGRESS

Work	8h	Remaining work	0h
% Complete	100%	Spent time	10h

ACTIVITY FILES RELATIONS (1) WATCHERS (1) GITHUB

The work is now complete with the final "Manage Data Table" being finished by the team and just awaiting for approval.

% Complete changed from 80% to 100%
Remaining work changed from 1.6h to 0h

LB Lorenzo Bernal 10/08/2025 01:04 PM
The changes were retracted.

GC Gabrielle Cabangcala 10/12/2025 01:29 PM
Activity Diagram Commit

Add a comment. Type @ to notify people.

Corresponding Github repository commit [\[Link\]](#)

7 files changed

docs/MSYAD01/01 Analysis and design documents/011 Use Case Diagrams/Use Case Diagram - Quadthink.pdf 137 KB

Binary file not shown.

docs/MSYAD01/01 Analysis and design documents/012 Fully dressed Use Cases/Fully Dressed Use Case - Quadthink.pdf 716 KB

Binary file not shown.

docs/MSYAD01/01 Analysis and design documents/012 Fully dressed Use Cases/Fully Dressed Use Case - QuadTHINK.pdf 485 KB

Binary file not shown.

docs/MSYAD01/01 Analysis and design documents/013 Activity diagrams with swim-lanes/Activity Diagram - Quadthink .pdf 915 KB

Binary file not shown.

docs/MSYAD01/01 Analysis and design documents/013 Activity diagrams with swim-lanes/Activity Diagram - Quadthink.pdf 545 KB

Binary file not shown.

docs/MSYAD01/01 Analysis and design documents/014 Test Cases/Quadthink_TestCaseTable.xlsx 22.1 KB

Binary file not shown.

docs/MSYAD01/01 Analysis and design documents/014 Test Cases/Test Case Tables - Quadthink.xlsx 25.3 KB

Binary file not shown.

Comments 0 Lock conversation

Comment

Subscribe You're not receiving notifications from this thread.
